


PHASE IV Continue Construction of Bridge Across the Riverside Drainage Canal.
 Detour Through Traffic to Broadway VIA 55th Street South and 63rd Street South.

PHASE IVa Continue Construction of Roadway on West side of Hydraulic Ave. from North of 63rd Street to the Riverside Drainage Canal While maintaining 1 Way Traffic North Bound on Existing Pavement from 63rd Street to 60th Street (South Bound Traffic VIA Kansas Ave), Two-way traffic on Existing Pavement from 60th Street to 59th Street, and 1 Lane Access to Properties from the Riverside Drainage Canal to 59th Street with Flagman as required. East-West Traffic on 60th Street.

SCALE: 1" = 150'

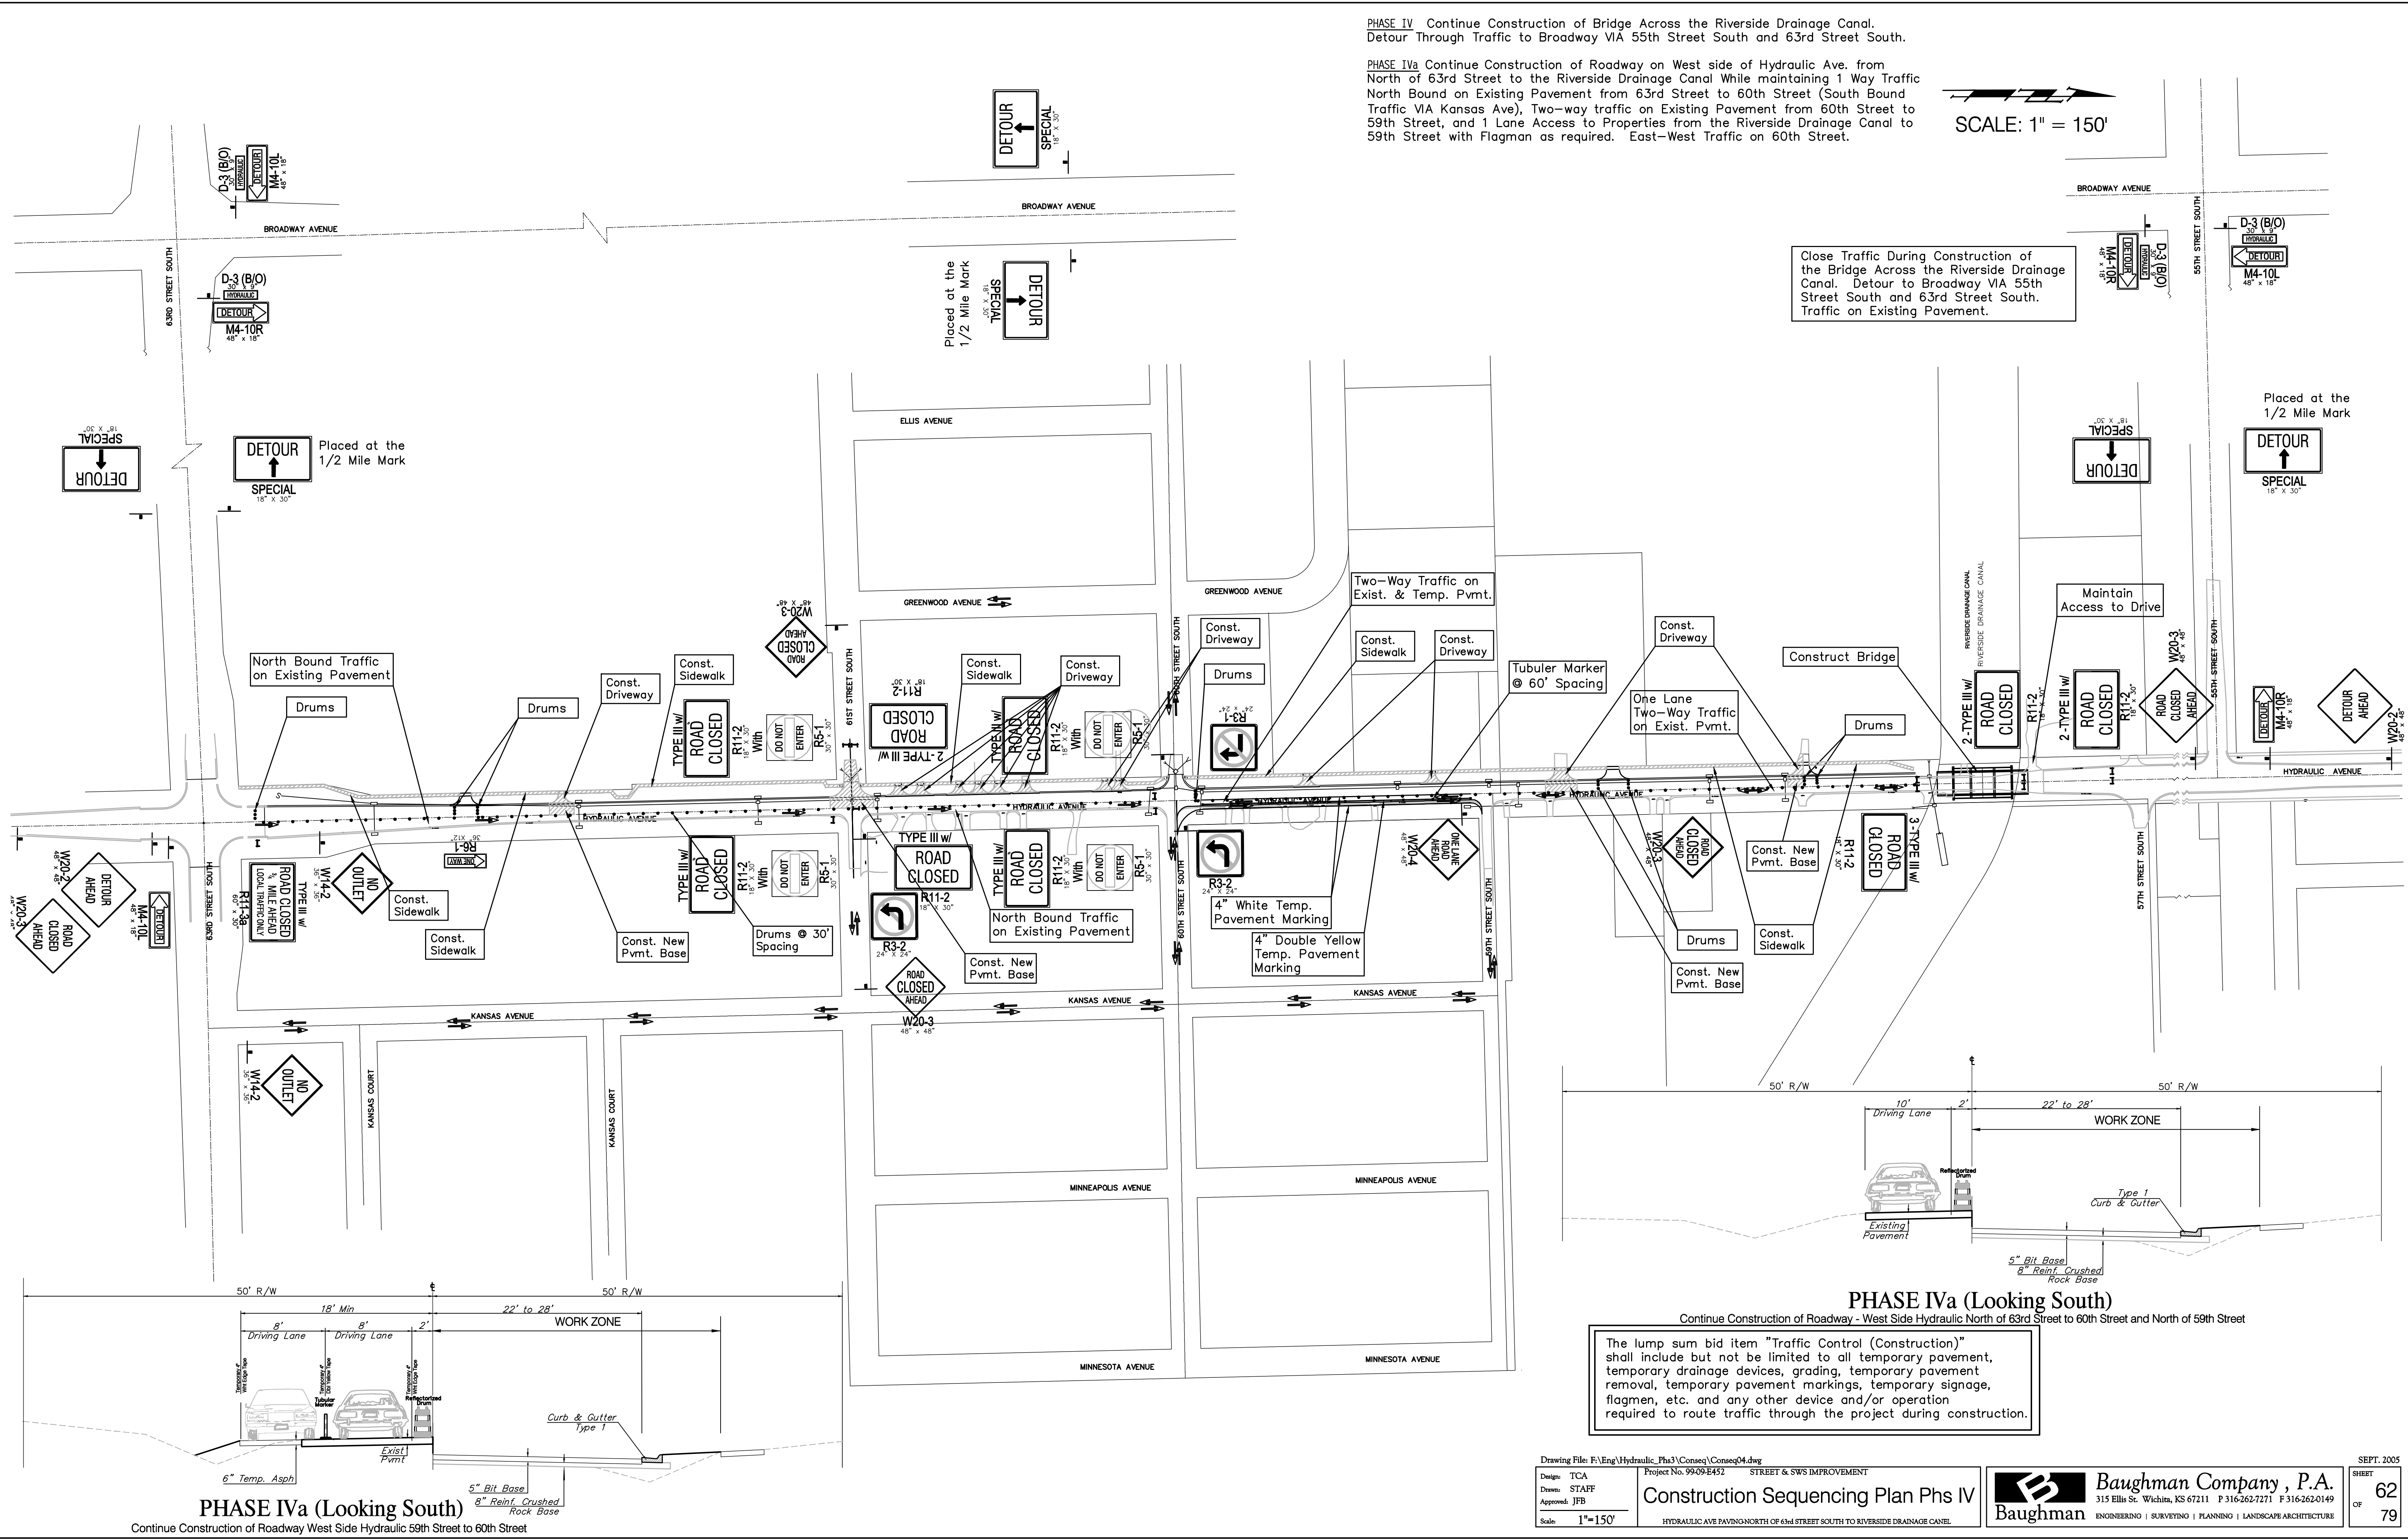

Close Traffic During Construction of the Bridge Across the Riverside Drainage Canal. Detour to Broadway VIA 55th Street South and 63rd Street South. Traffic on Existing Pavement.

The lump sum bid item "Traffic Control (Construction)" shall include but not be limited to all temporary pavement, temporary drainage devices, grading, temporary pavement removal, temporary pavement markings, temporary signage, flagmen, etc. and any other device and/or operation required to route traffic through the project during construction.

PHASE IVa (Looking South)

Continue Construction of Roadway - West Side Hydraulic North of 63rd Street to 60th Street and North of 59th Street

PHASE IVa (Looking South)
 Continue Construction of Roadway West Side Hydraulic 59th Street to 60th Street

Drawing File: F:\Eng\Hydraulic_Ph3\Conseq\Conseq04.dwg
 Design: TCA
 Drawn: STAFF
 Approved: JFB
 Scale: 1"=150'

Project No. 99-09-E452 STREET & SWS IMPROVEMENT
 Construction Sequencing Plan Phs IV
 HYDRAULIC AVE PAVING-NORTH OF 63rd STREET SOUTH TO RIVERSIDE DRAINAGE CANAL

Baughman Company, P.A.
 315 Ellis St. Wichita, KS 67211 P 316-262-7271 F 316-262-0149
 Baughman ENGINEERING | SURVEYING | PLANNING | LANDSCAPE ARCHITECTURE

SEPT. 2005
 SHEET 62 OF 79
