


STATE	PROJECT NO.	YEAR	SHEET NO.	TOTAL SHEETS
KANSAS	54-87 K-8258-08	2005	198	223

GENERAL SEQUENCE OF CONSTRUCTION:

THE NORTH FRONTAGE ROAD AND SOUTH FRONTAGE ROAD HAVE BEEN CONSTRUCTED IN PREVIOUS PROJECTS. DETOURS HAVE BEEN CONSTRUCTED AND BOTH EASTBOUND AND WESTBOUND EAST KELLOGG HAVE BEEN SHIFTED TO THE NEW FRONTAGE ROADS.

STAGE 1

- A. CONSTRUCT THE PROPOSED IMPROVEMENTS INCLUDING GRADING, CONCRETE PAVEMENT, STORM SEWERS, BRIDGES, RETAINING WALLS, LIGHTING, SIGNING AND PAVEMENT MARKING BETWEEN STATIONS 4+350 AND 4+700. FINAL PAVEMENT MARKING AND SIGNING OF THE FRONTAGE ROADS ARE NOT INCLUDED IN THIS PHASE.
- B. BETWEEN STATIONS 4+244.422 AND 4+350, AND BETWEEN STATIONS 4+700 AND 4+846.942 CONSTRUCT THE SOUTH SECTION OF THE PROPOSED IMPROVEMENTS INCLUDING GRADING, CONCRETE PAVEMENT, STORM SEWERS, BRIDGES, RETAINING WALLS, LIGHTING, SIGNING, AND PAVEMENT MARKING. CONSTRUCTION INCLUDES THE MEDIAN BARRIER AND SHOULDERS. EARTH SLOPES SHALL BE AT A SAFE ANGLE IN COMPLIANCE WITH ALL LAWS AND REGULATIONS.
- C. CONSTRUCT EASTERN AND ASSOCIATED LIGHTING AND PAVERS.
- D. CONST. ASPHALT TRANSITION FROM STA. 4+023 TO STA. 4+244.422.
- E. CONST. ASPHALT TRANSITION FROM STA. 4+846.942 TO STA. 4+958.

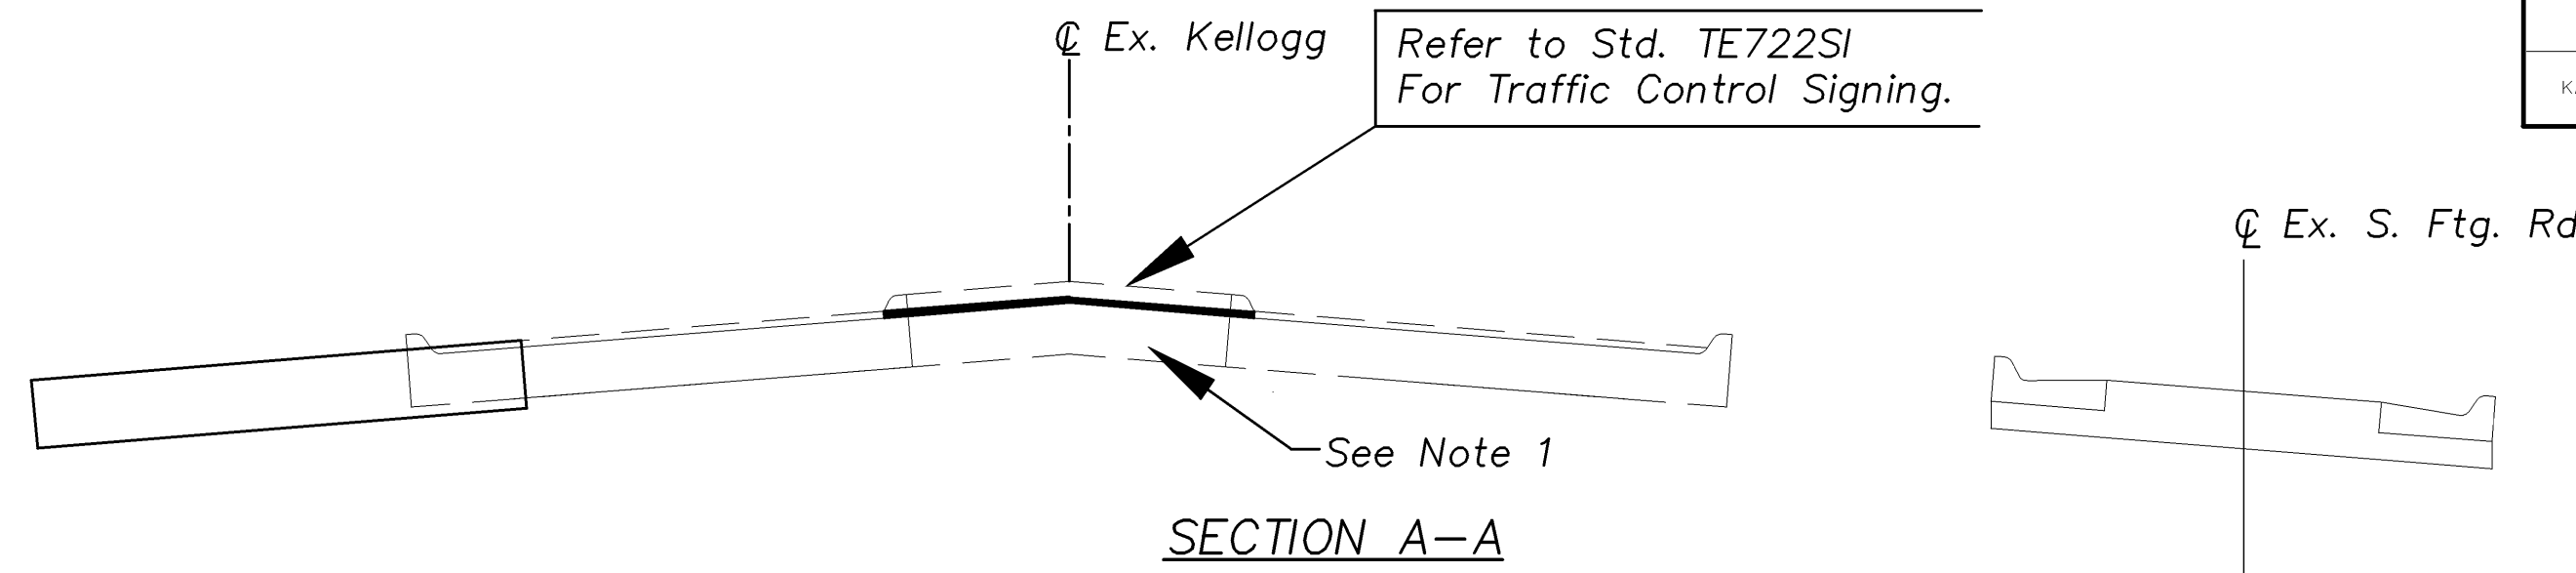


NOTES:
1. THE EXISTING CURB AND MEDIAN WERE CONSTRUCTED OVER CONCRETE PAVEMENT WHICH SHALL REMAIN.

LEGEND

- TEMPORARY ASPHALT CONSTRUCTION THIS STAGE
- TEMPORARY CONSTRUCTION REMOVE CURB/MEDIAN AND PLACE PLANT MIX BITUMINOUS MIXTURE - COMMERCIAL GRADE (APPROXIMATELY 50 mm THICK)
- PERMANENT CONCRETE CONSTRUCTION THIS STAGE
- TRAFFIC FLOW
- CHANNELIZING DEVICES
- 35 M.P.H. EXISTING SIGNING TO REMAIN IN PLACE

NOTE: The existing ROAD WORK AHEAD (W20-1a) & END ROAD WORK (G20-2a)/SPEED LIMIT 40 (R2-1) Signs at the beginning and end of this phase that were installed for the north and south frontage road construction will remain in place until completion of this project. All signs that are in place within the interior of the ring of temporary concrete safety barriers shall be relocated or stockpiled for use in future stages.

Scale: 1:500

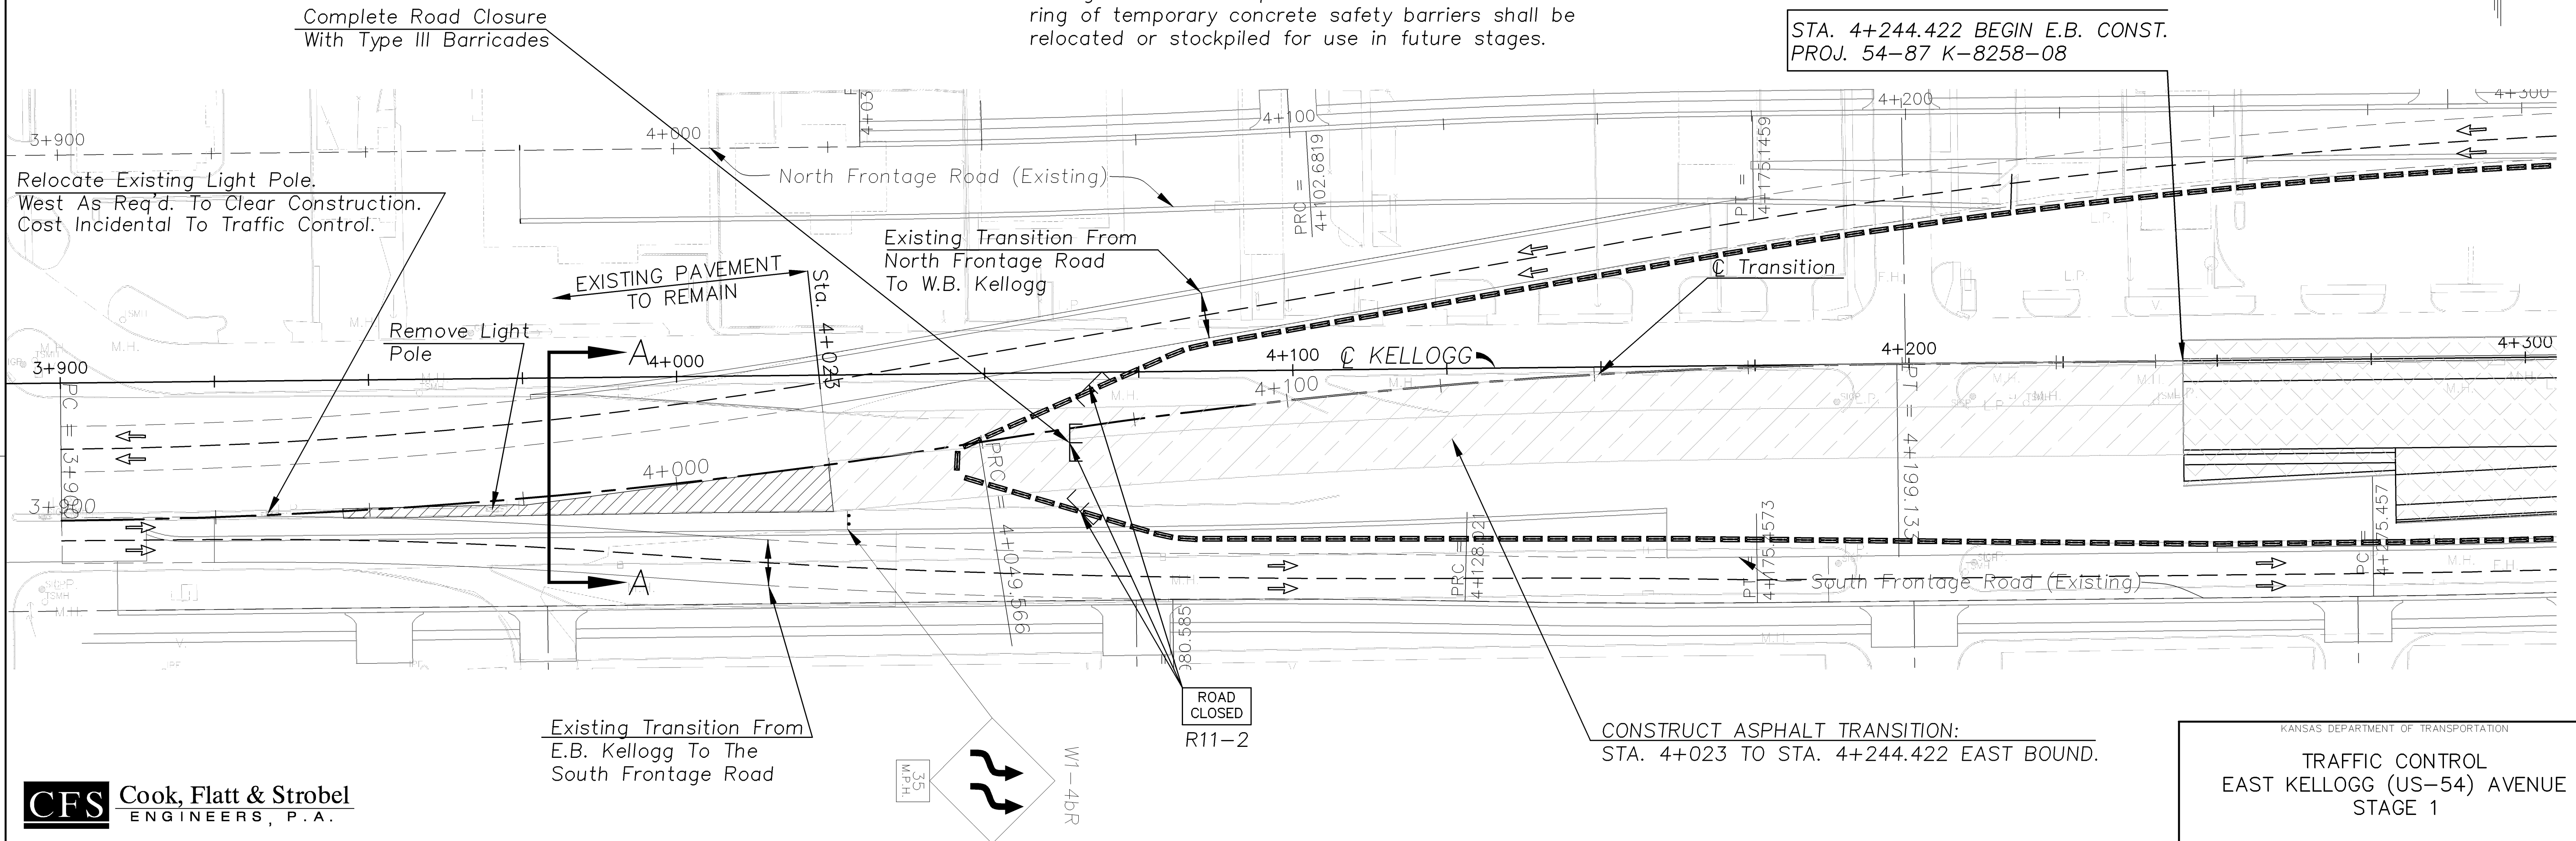

STA. 4+244.422 BEGIN E.B. CONST. PROJ. 54-87 K-8258-08

CONSTRUCT ASPHALT TRANSITION: STA. 4+023 TO STA. 4+244.422 EAST BOUND.

KANSAS DEPARTMENT OF TRANSPORTATION
TRAFFIC CONTROL
EAST KELLOGG (US-54) AVENUE
STAGE 1

DATE	
BY	
REFERENCE NOTED	
REFERENCE CHECKED	

Drawn by: Plotter: SCALE: File:

