
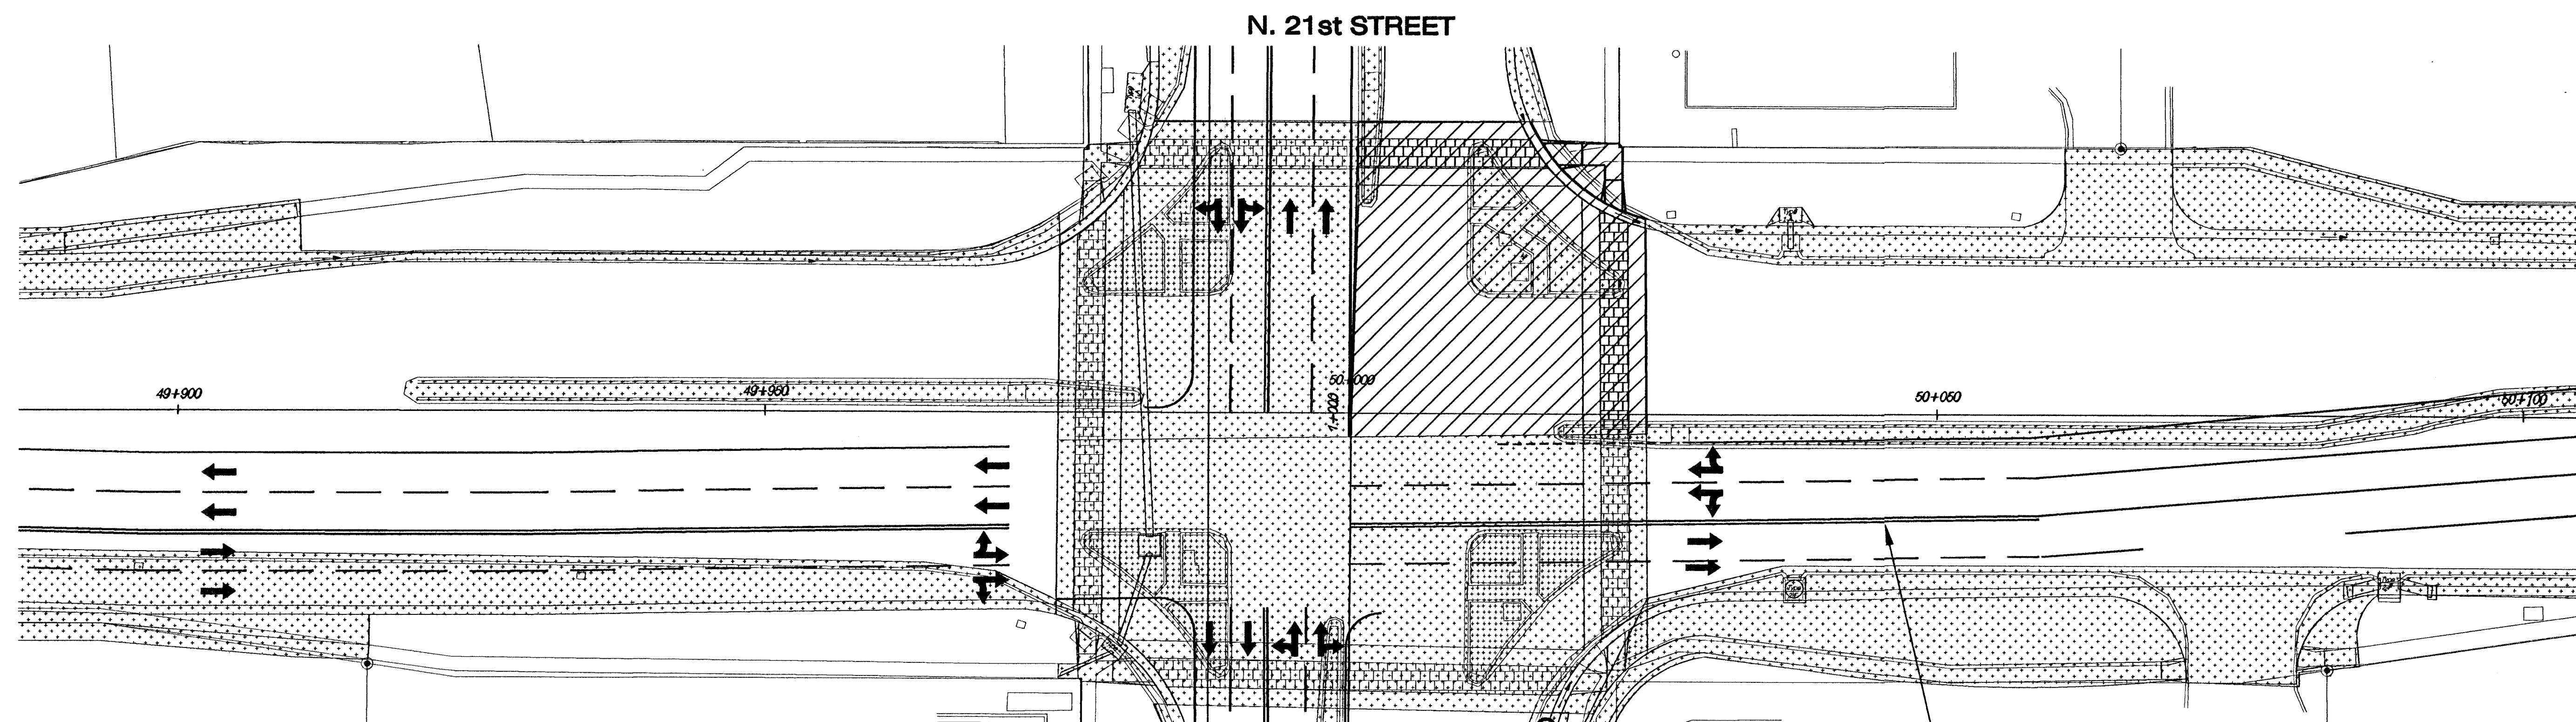


FHWA REG NO.	STATE	PROJECT NO.	YEAR	SHEET NO.	TOTAL SHEETS
7	KANSAS	87 N-0199-01	2002	33	158

FED. AID NO. 9MQ-NO19(901)

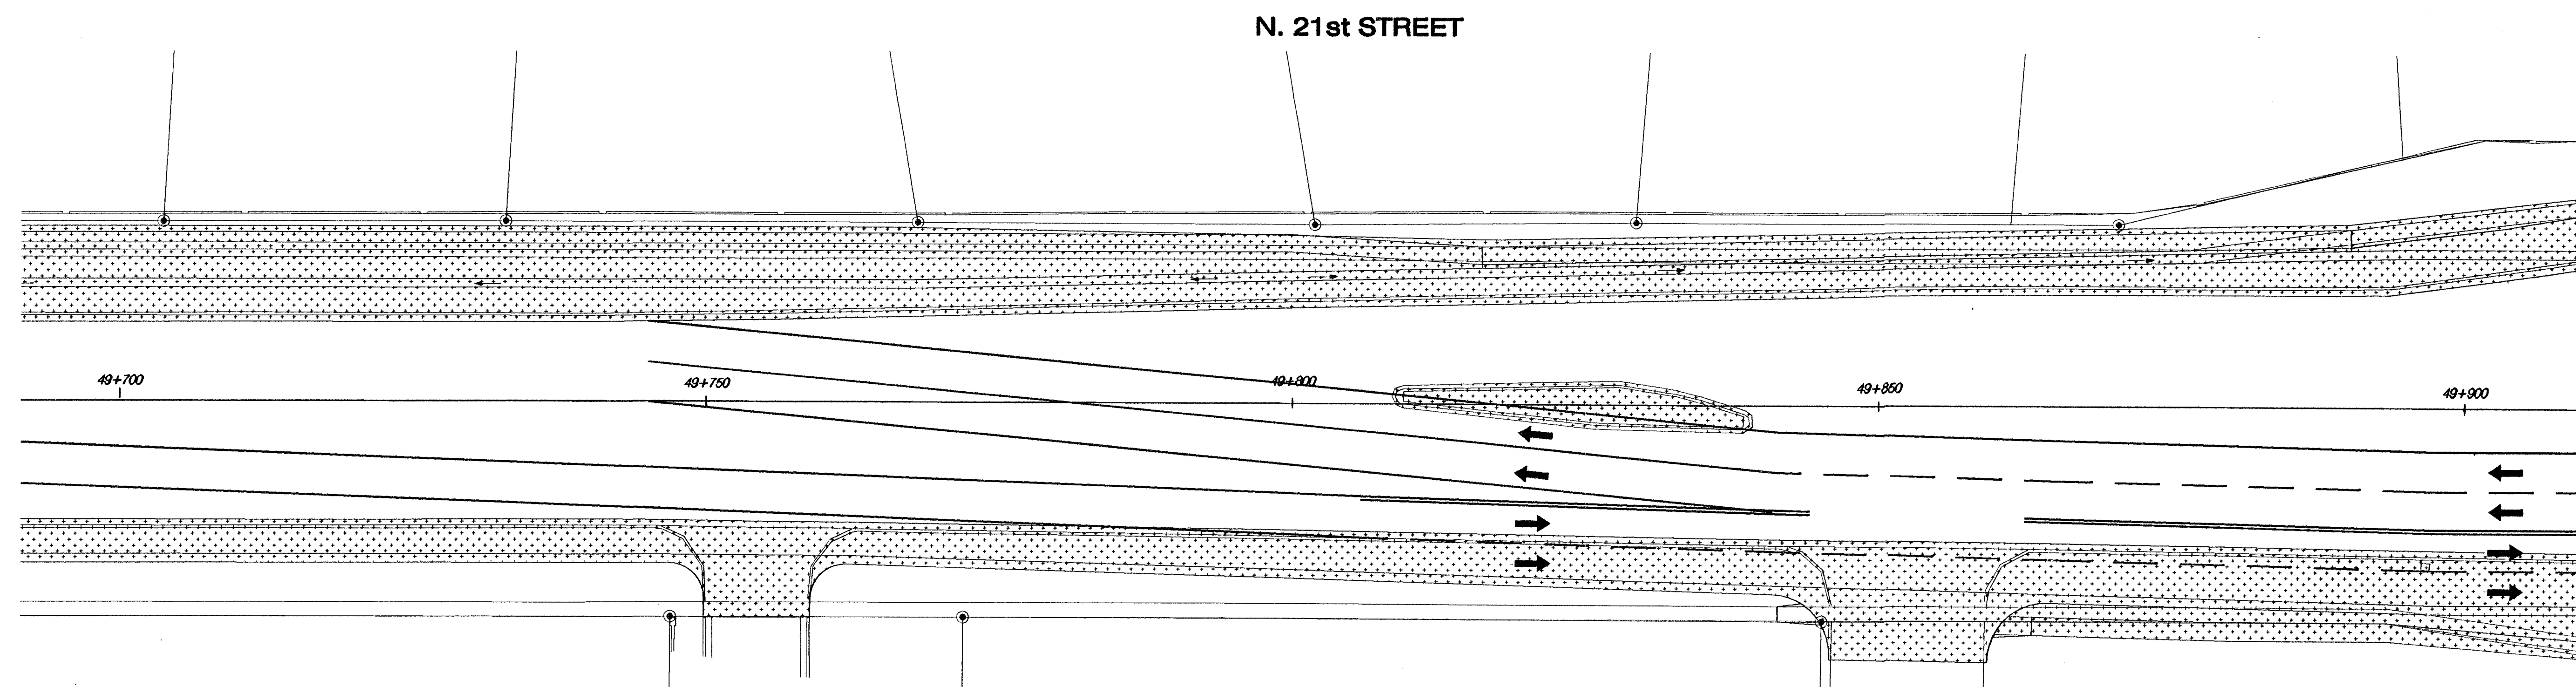


Legend

- Area Under Construction In Phase 7
Northeast 1/4 of N. 21st STREET and N. ROCK ROAD.
- Area Previously Constructed (Phases 1,2,3,4,5 & 6)

GENERAL WORK ACTIVITIES

1. Construct Temporary Lane Striping.
 2. Move Traffic To South Side of 21st St., Maintain 2 Lanes in Each Direction And Left Turn Capability At N. ROCK ROAD & 21st
 3. Remove Existing Pavement, Curb & Gutter, Median Surfacing And Previously Constructed Temporary Asphalt
 4. Construct Curb & Gutter And Pavement Base
 5. Construct Pavement And Brick Paver Crosswalk
 6. Construct Sidewalk And Wheelchair Ramps
- See Plan Sheets for Removal and Construction Information

**N. 21st STREET
PHASE 7
STA. 49+700 - 50+100**



Designed By:	BWE	Checked By:	RJK
Drawn By:	HIS	Date:	03-25-2002 Job No. 55-70-2003
