


HHWA REGION NO.	STATE	PROJECT NO.	FISCAL YEAR	SHEET NO.	TOTAL SHEETS
7	KANSAS	87N-0378-01	2008	53	72

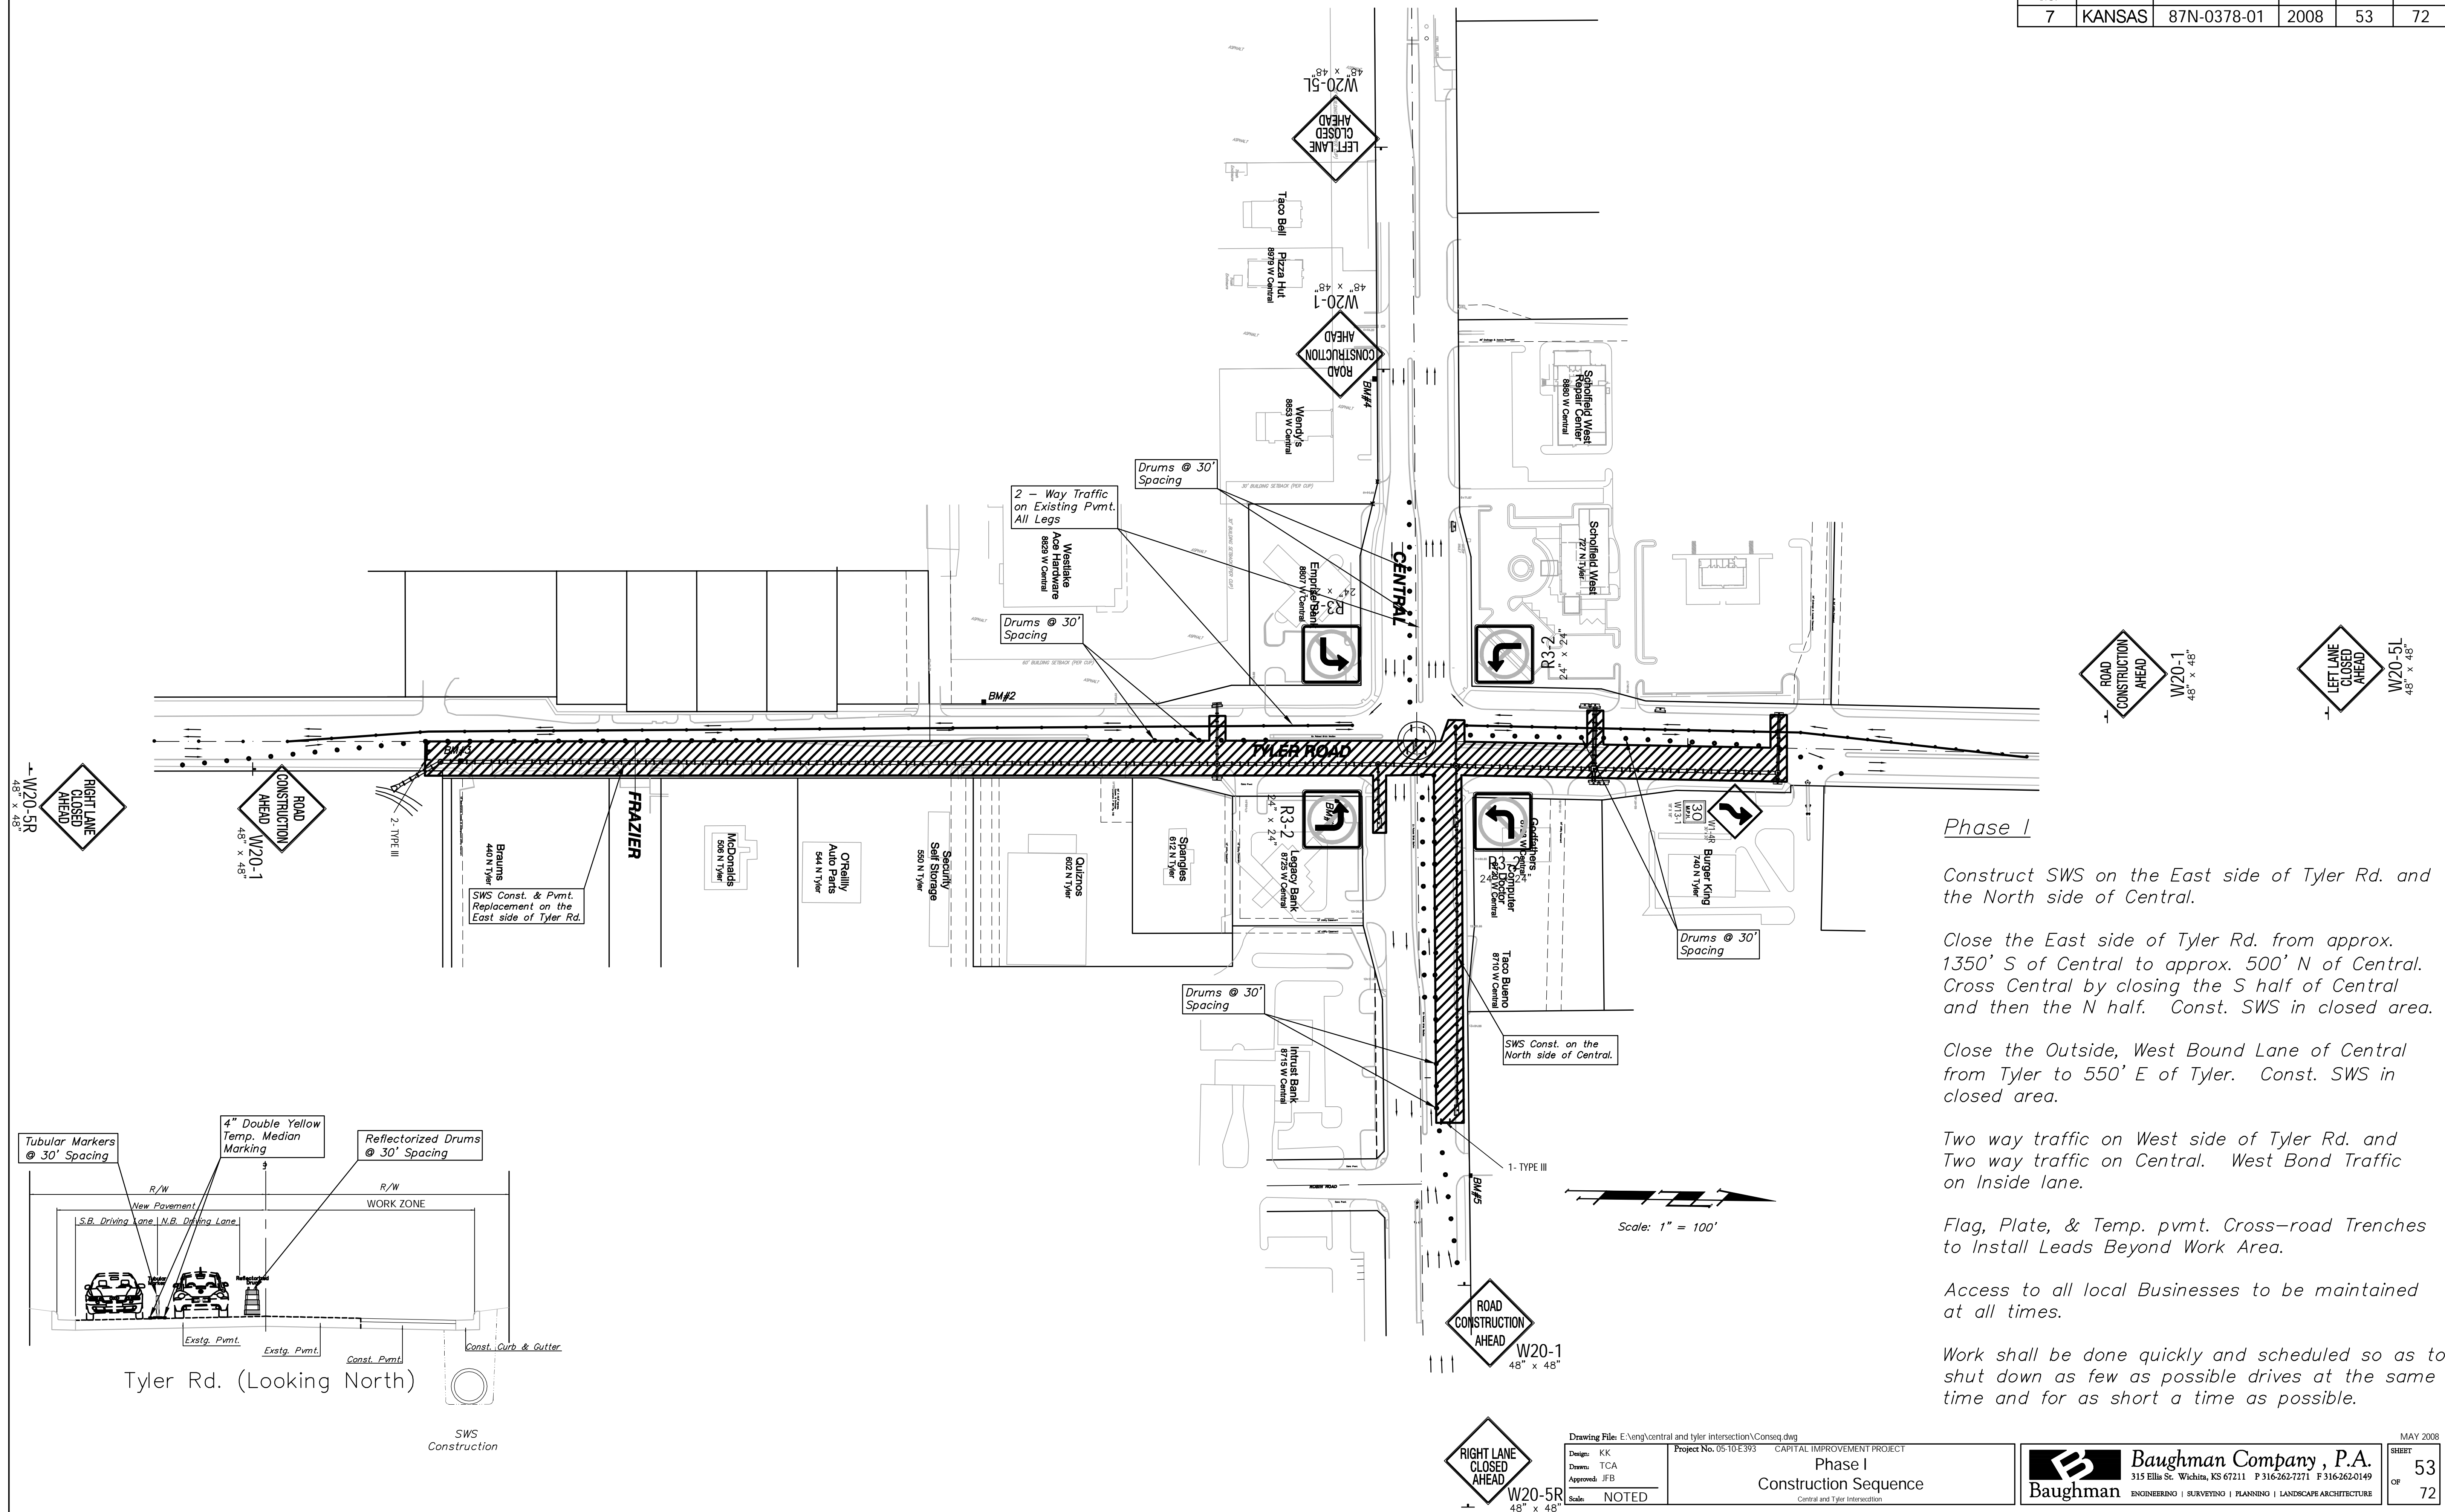

Phase I

Construct SWS on the East side of Tyler Rd. and the North side of Central.

Close the East side of Tyler Rd. from approx. 1350' S of Central to approx. 500' N of Central. Cross Central by closing the S half of Central and then the N half. Const. SWS in closed area.


Close the Outside, West Bound Lane of Central from Tyler to 550' E of Tyler. Const. SWS in closed area.

Two way traffic on West side of Tyler Rd. and Two way traffic on Central. West Bond Traffic on Inside lane.

Flag, Plate, & Temp. pvmt. Cross-road Trenches to Install Leads Beyond Work Area.

Access to all local Businesses to be maintained at all times.

Work shall be done quickly and scheduled so as to shut down as few as possible drives at the same time and for as short a time as possible.

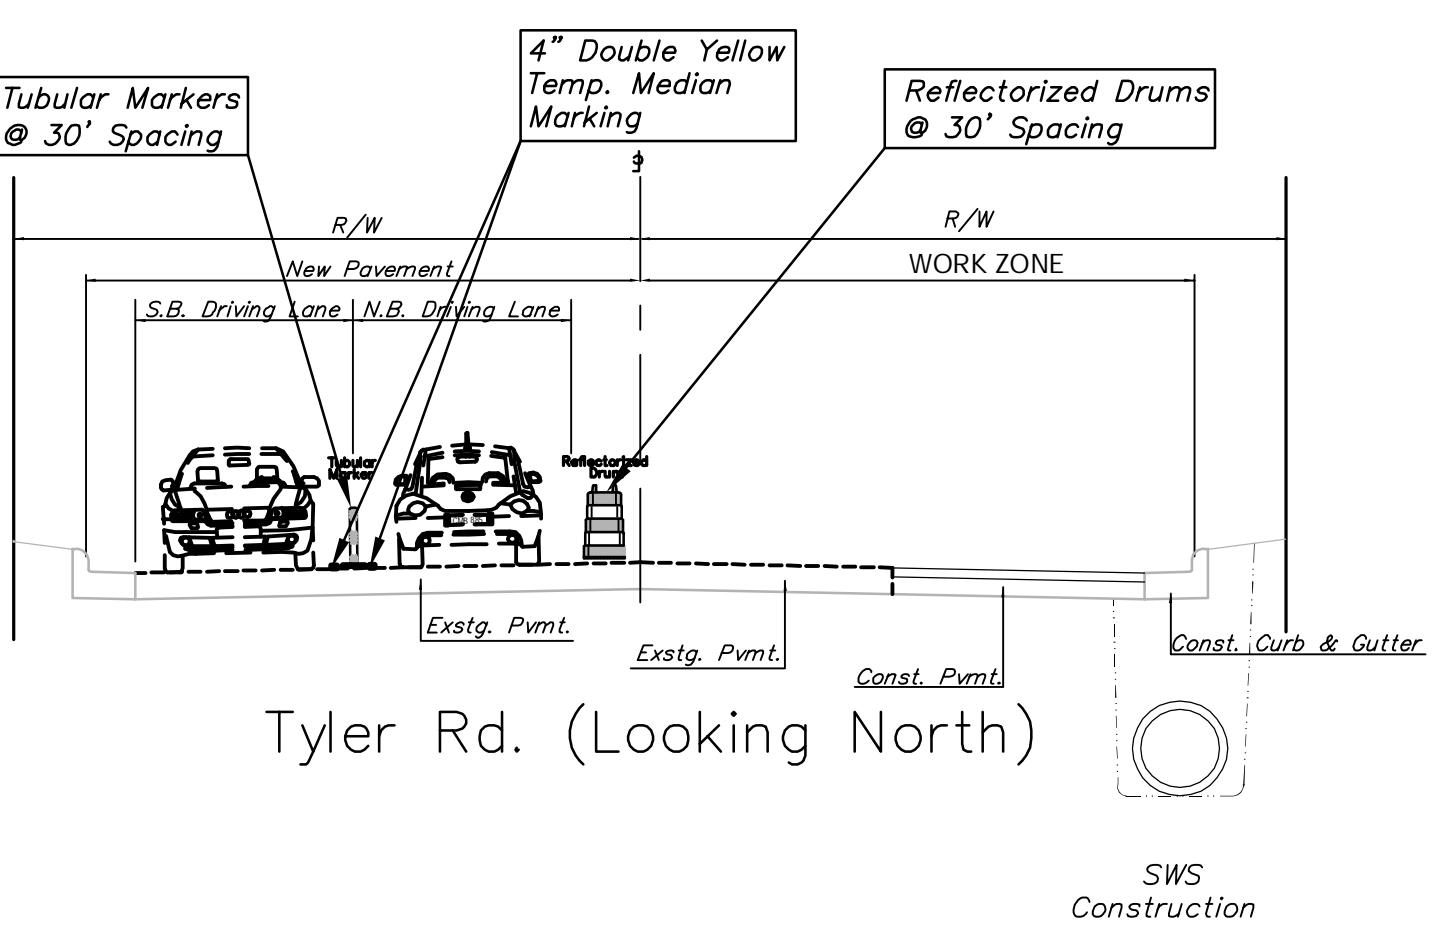

Scale: 1" = 100'

Drawing File: E:\eng\central and tyler intersection\Conseq.dwg

Design: KK
 Drawn: TCA
 Approved: JFB
 Scale: NOTED

Project No. 05-10-E393 CAPITAL IMPROVEMENT PROJECT

Phase I
 Construction Sequence
 Central and Tyler Intersection

Baughman Company, P.A.
 315 Ellis St. Wichita, KS 67211 P 316-262-7271 F 316-262-0149

ENGINEERING | SURVEYING | PLANNING | LANDSCAPE ARCHITECTURE

MAY 2008

SHEET 53 OF 72
