


BENCHMARK:
 "□" Chiseled on Top of Curb, end of cul-de-sac of Meadow Oaks Circle, Meadow Oaks Addition.
 Elevation=1362.10 (NAVD 88)
 "□" Chiseled on CL front of CB at end of cul-de-sac of Ironhorse Circle, Ironhorse Addition.
 Elevation=1362.07 (NAVD 88)

EROSION CONTROL PLAN LEGEND
 (Installation Details Found in the SMP2 Plan)

- DROP INLET PROTECTION
- CURB INLET PROTECTION
- DITCH CHECKS
- SILT FENCING
- CUT-OFF TRENCH
- BACK OF CURB PROTECTION
- EROSION CONTROL MAT
- TEMPORARY DITCH

NO SCALE

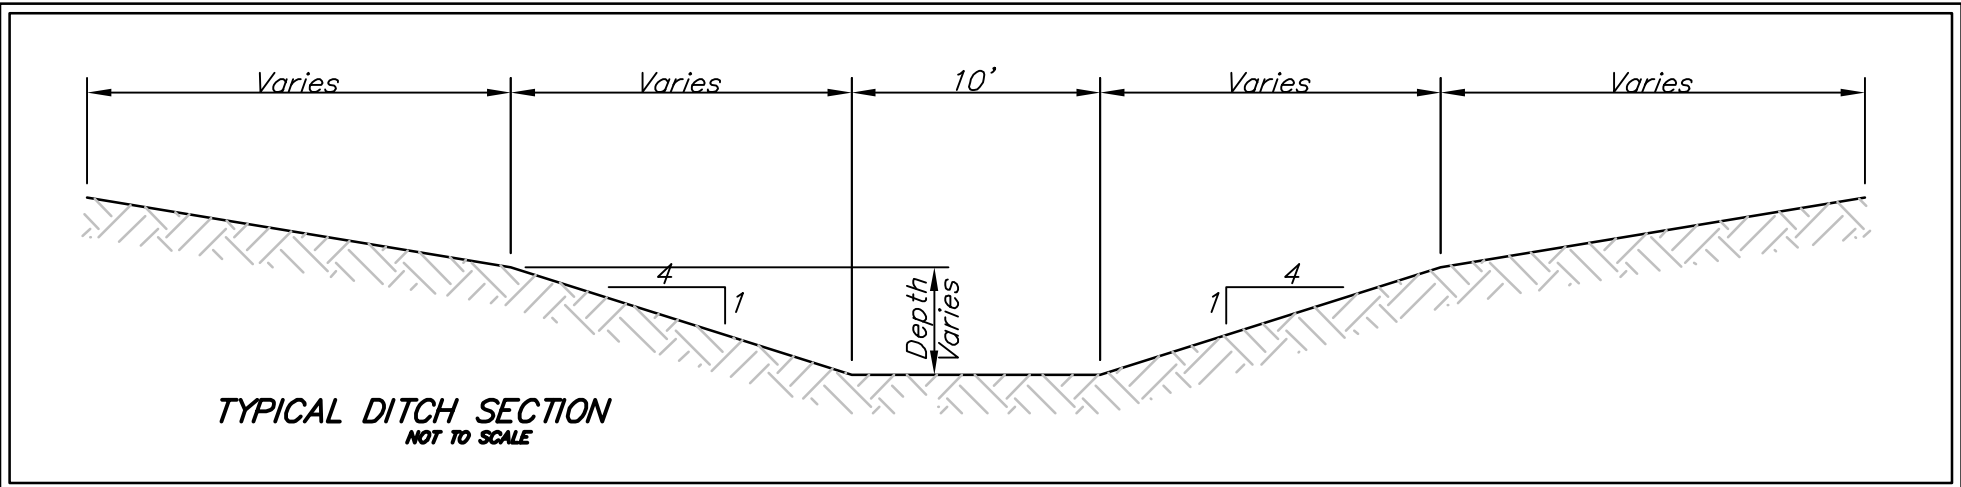

EROSION CONTROL MEASURE	INSTALL	MAINTAIN	REMOVE
BACK OF CURB PROTECTION (LF)	0	0	0
CONSTRUCTION ENTRANCE (EA)	1	0	0
CURB INLET BARRIER (EA)	0	0	0
DITCH CHECK (EA)	4	0	0
DROP INLET PROTECTION (EA)	3	0	0
EROSION CONTROL (LS)	0	0	0
EROSION CONTROL BERM (LF)	0	0	0
SILT FENCE (LF)	0	0	0
EROSION CONTROL MAT (SY)	0	0	0

QUANTITIES ARE FOR INFORMATION ONLY! CONTRACTOR SHALL VERIFY QUANTITIES PER FINAL BID QUANTITY SHEET.

* ALL EXISTING BMPs INCLUDING CONSTRUCTION ENTRANCE, SEDIMENT BARRIERS, SILT FENCE, CUT-OFF TRENCH, AND EROSION CONTROL MAT SHALL BE MAINTAINED AND REPAIRED IF NECESSARY. REPLACEMENT OR REMOVAL OF EROSION CONTROL MEASURES TO BE PAID FOR BY L.S. BID ITEM "MAINTAIN EXISTING EROSION CONTROL BMPs"

Baughman IRONHORSE AT OXFORD ADD.
 EROSION CONTROL PLAN

Baughman Company, P.A. 315 Ellis St. Wichita, KS 67211 P 316-262-7271 F 316-262-0149
 ENGINEERING | SURVEYING | PLANNING | LANDSCAPE ARCHITECTURE

PROJECT NUMBER: 468-84795 DESIGN: NBW DRAWN: TMS
 APPROVED: NBW DATE: 09/12
 SCALE: Noted
 SHEET: 9 OF 15

E:/Projects/Ironhorse Addition_11-10-E682/07.30.12/_09_SWSep.dwg 11-10-E682
