

**SITE 18**

Bayley

Pattie

Lulu

The line from MH 5546-539 north to Lincoln Street is scheduled for open cut replacement. Contractor may need to coordinate with the Public Works Field Engineer.



Install 239 lf of 8" Cured-in-Place Liner from MH 5546-539 to MH 5546-538

MH 5546-539  
Approx. depth = 7.1 ft

MH 5546-538  
Approx. depth = 6.7 ft

Parking Lot

Parking Lot

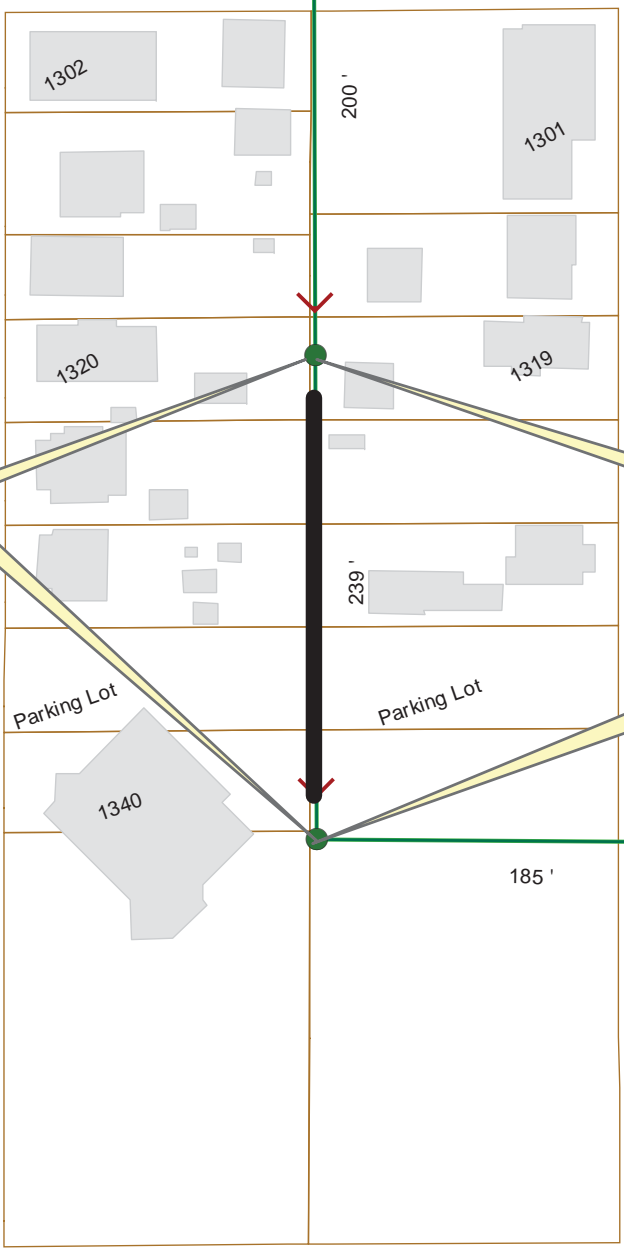

540  
E BAYLEY ST

SILULU AVE

S PATTIE AVE


539

E ST JOHN ST

538

537

536

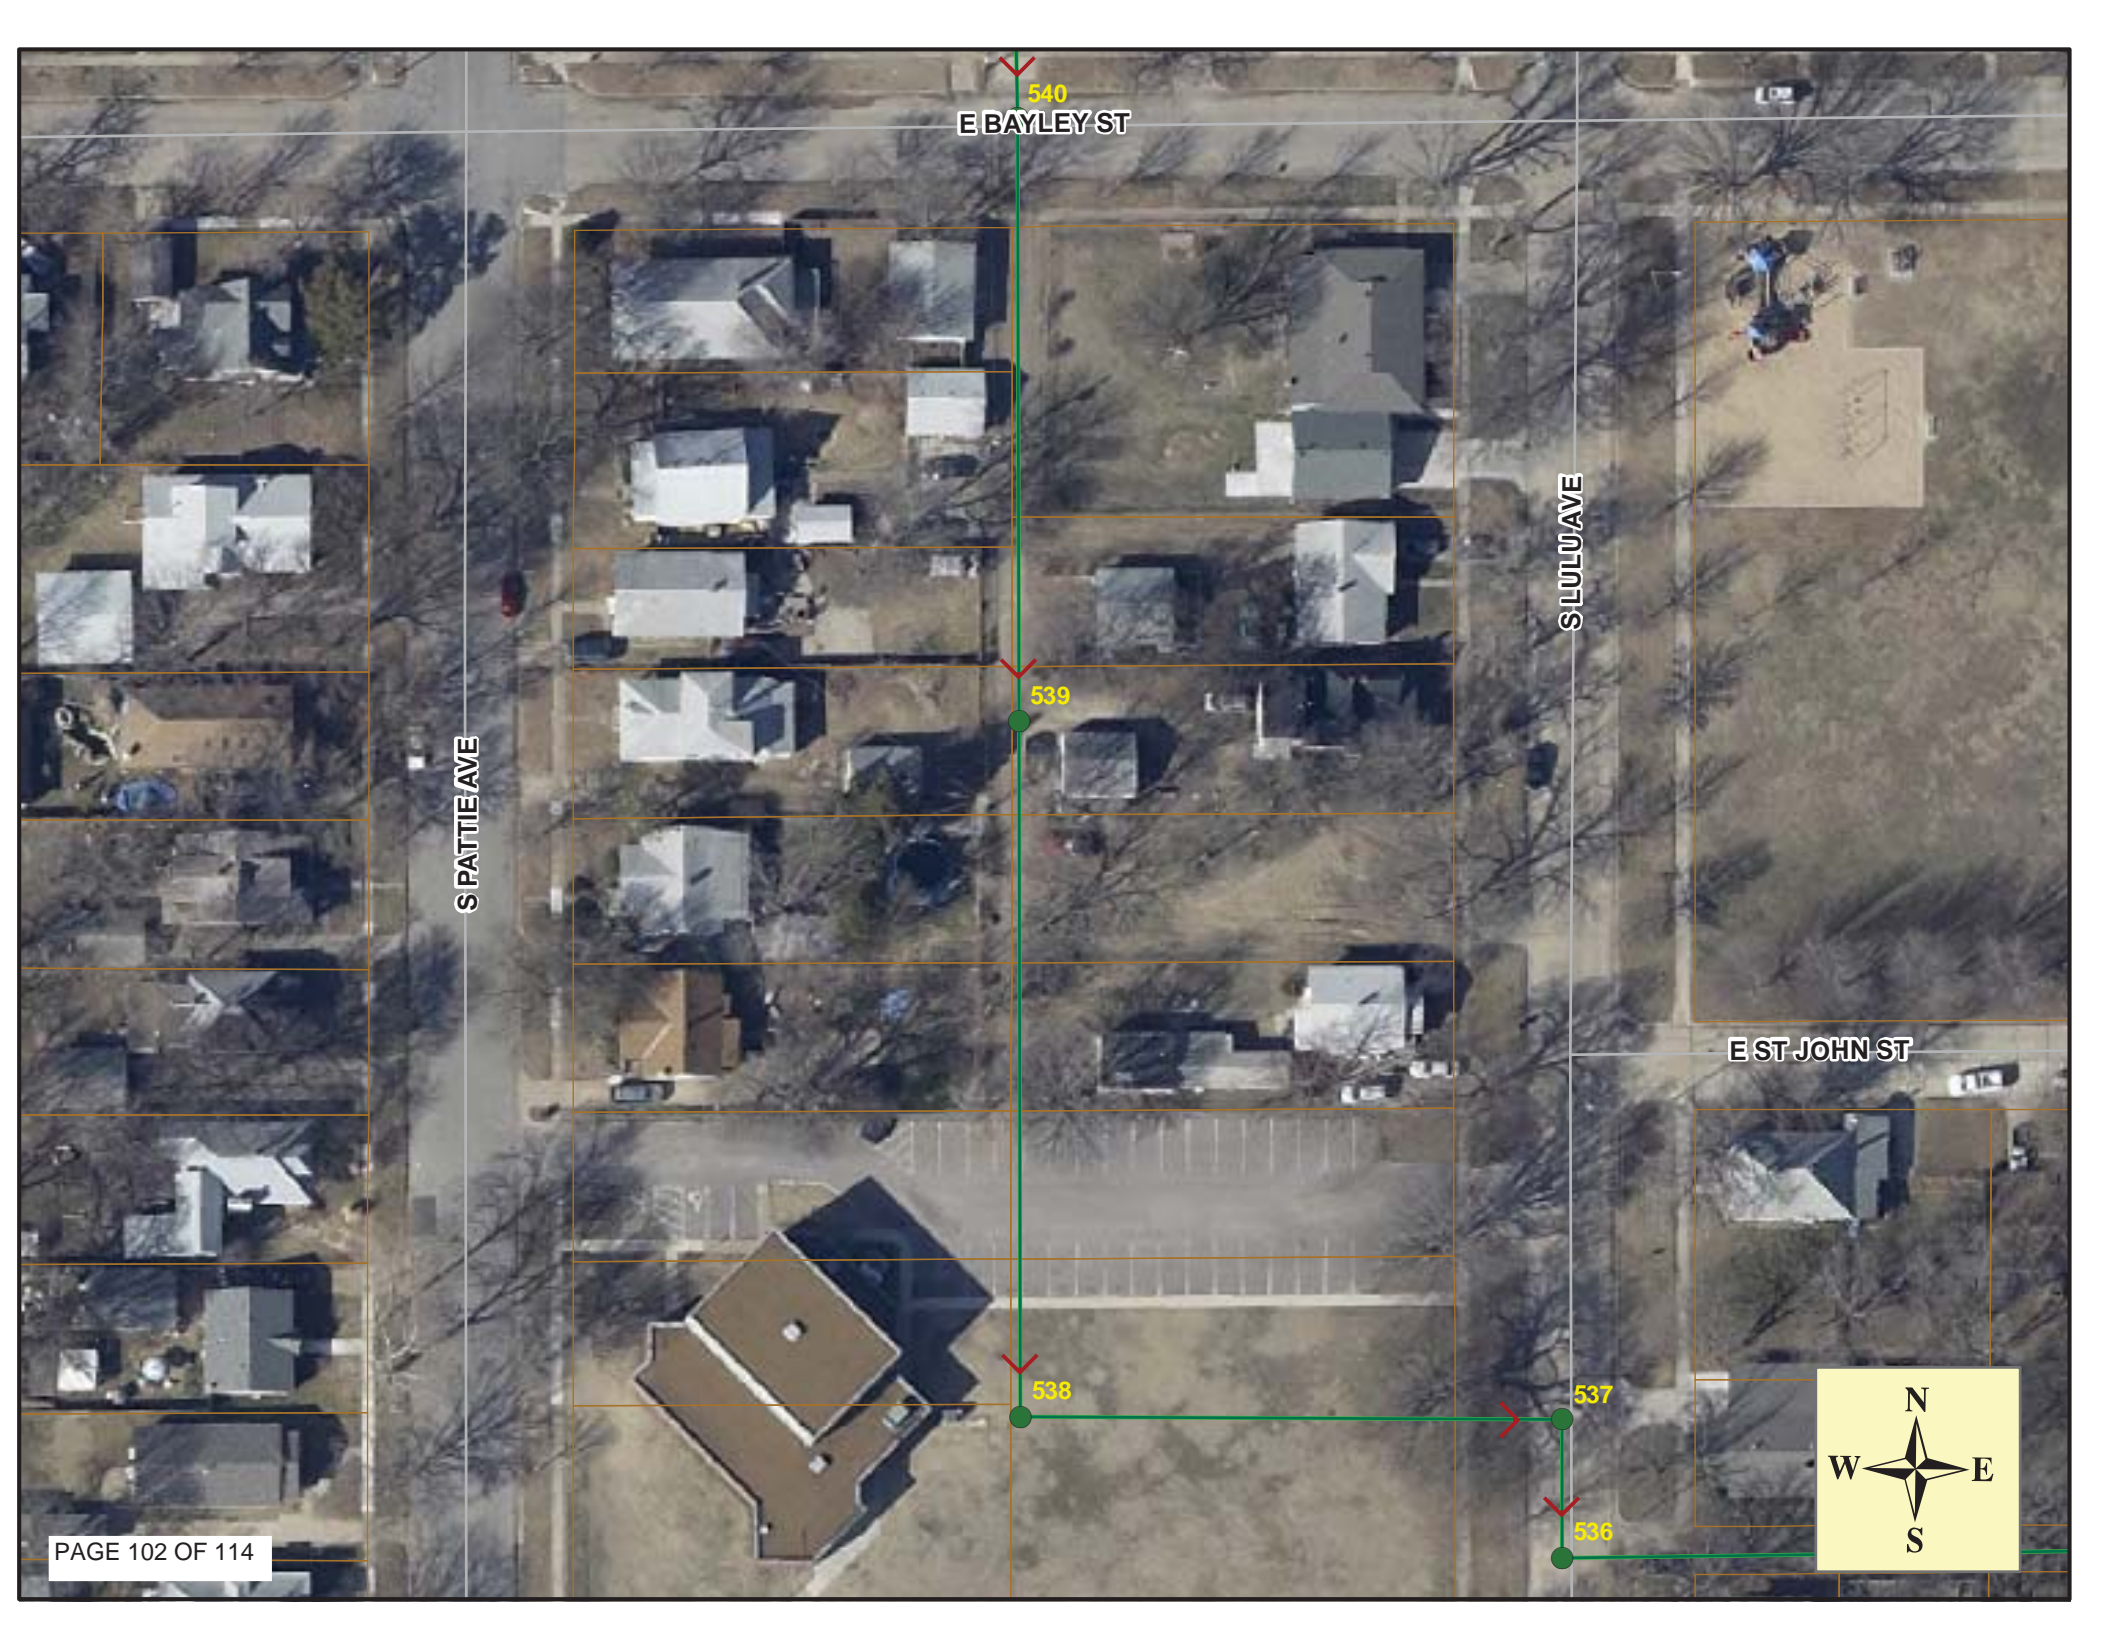

## Video Inspection Master Report

9/10/2012  
7:36 AM

US Structure: 5546-539      1319 S LULLU AVE      Date Insp: 9/19/2011      Basin: C02A  
 DS Structure: 5546-538      1340 S PATTIE ST      Dir Televised: Upstream To Downstream

**Pipe Information**  
 Project No. : D-108      Dia: 8      Material: VCP      Length: 239      Slope: 0.400      Surface: Alley Unpaved

Obs. #	VTR Counter	Distance	Location	Description	Rating	Ratings			
						Obsrvd (gpm)	Est. (gpm)	Struct Clean	Remain (gpm)
1		0.0		5546-539 US Manhole	1	0.001	0	0	0.001
2		13.9	1319 SOUTH LULLU	Break-In Conn	1	0.000	0	0	0.000
3		15.5		Sealed Off Wye	1	0.000	0	0	0.000
4		18.2		Sealed Off Wye	1	0.000	0	0	0.000
5		19.7		Broken Pipe	3	0.010	60	0	0.010
6		20.4		Break-In Conn	4	0.008	60	0	0.008
7		24.1		Debris (loose tile)	3	0.000	0	0	0.000
8		27.5		Crack-Radial	3	0.004	5	0	0.004
9		38.2		Crack-Radial	3	0.004	5	0	0.004
10		41.9		Sealed Off Wye	1	0.000	0	0	0.000
11		44.6		Sealed Off Wye	3	0.000	0	0	0.000
12		66.7		Broken Pipe	3	0.010	60	0	0.010
13		68.1		Wye Service	1	0.000	0	0	0.000
14		70.5		Sealed Off Wye	1	0.000	0	0	0.000
15		77.2		Broken Pipe	3	0.010	60	0	0.010
16		79.9		Crack-Radial	3	0.004	5	0	0.004
17		87.9		Crack-Radial	3	0.004	5	0	0.004
18		93.0		Crack-Radial	2	0.002	2	0	0.002
19		94.4		Wye Service / roots inside	3	0.000	2	0	0.000
20		96.8		Sealed Off Wye	1	0.000	0	0	0.000
21		99.3		Break-In Conn	1	0.001	0	0	0.001
22		103.0		Broken Pipe	3	0.010	60	0	0.010
23		119.2		Broken Pipe	3	0.010	60	0	0.010
24		120.4		Sealed Off Wye	1	0.000	0	0	0.000
25		123.1		Sealed Off Wye	1	0.000	0	0	0.000
26		142.2		Sealed Off Wye	1	0.000	0	0	0.000
27		147.0		Sealed Off Wye	1	0.000	0	0	0.000
28		149.4		Sealed Off Wye	1	0.000	0	0	0.000
29		158.7		Broken Pipe	3	0.010	60	0	0.010
30		173.1		Sealed Off Wye	3	0.000	0	0	0.000
31		174.8		Broken Pipe	3	0.010	60	0	0.010
32		175.5		Sealed Off Wye	3	0.000	0	0	0.000
33		190.5		Broken Pipe	4	0.030	78	0	0.030
34		198.1		Broken Pipe	2	0.008	44	0	0.008
35		199.3		Sealed Off Wye	1	0.000	0	0	0.000
36		201.8		Sealed Off Wye	1	0.000	0	0	0.000
37		215.0		Break-In Conn	1	0.001	0	0	0.001
38		225.2		Sealed Off Wye	1	0.000	0	0	0.000
39		227.8		Sealed Off Wye	1	0.000	0	0	0.000
40		239.6		5546-538 DS Manhole	1	0.000	0	0	0.000
