
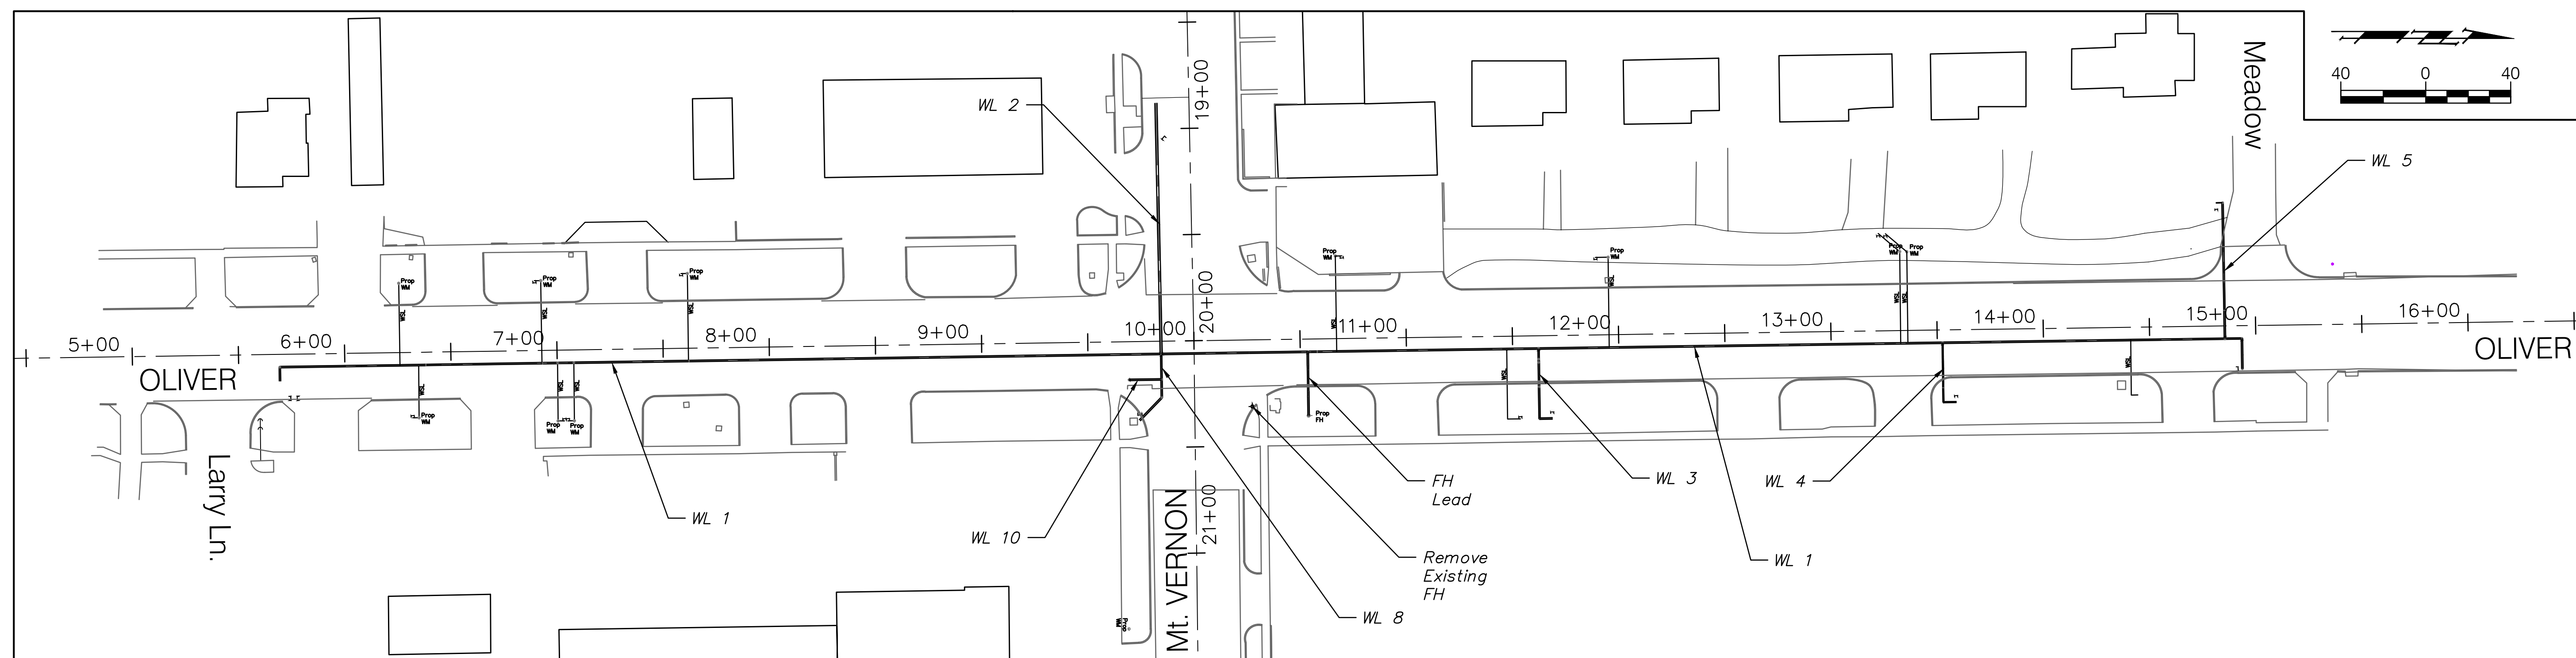


NOTE: Dellrose Street North & South of Mt. Vernon may be Closed During Construction. Place Advanced Warning Signs "STREET CLOSED AHEAD", W20-3 One Block from Closure. Use Type III Barricades W/"ROAD CLOSED R11-2 at Construction Site.

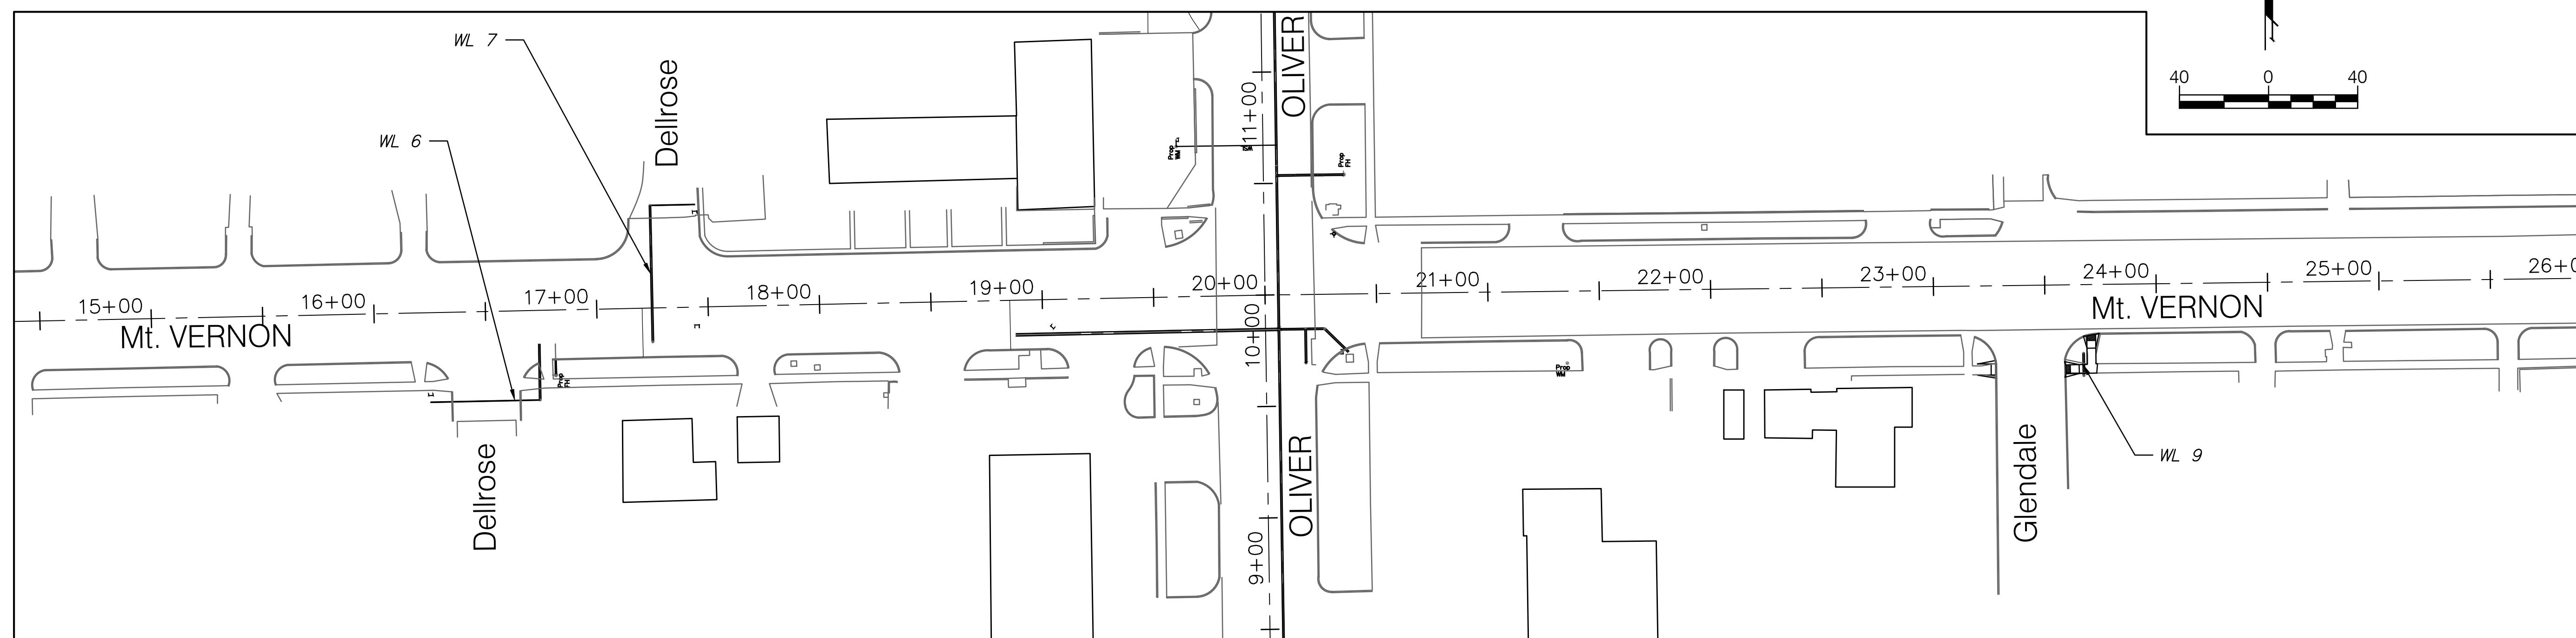

### Phase I

NOTE: Any Trench That Will be Driven on Prior to Construction of New Pavement Shall be Covered with 5" Thick Temporary Asphalt Pavement. To be Included in the Bid Price for the Water Pipe.

Install all Water Lines in Mt. Vernon & Oliver. Abandon Existing Lines as Soon as New Waterlines are tested and accepted. Maintain 2-Way Traffic at all Times using Flaggers and Steel Plating as Required. Control Traffic with ReflectORIZED Cones Utilizing Standard Taper Lengths and Proper Signing. Maintain Access to Businesses at all Times.

Design: KEK  
 Drawn: JDM  
 Approved: T Azicre  
 Scale: Noted

Project No. 1208-ES04  
 CAPITAL IMPROVEMENT PROJECT  
 Mt Vernon & Oliver  
 Construction Sequence Ph 1  
 Mt. Vernon & Oliver Intersection

**Baughman** **Baughman Company, P.A.**  
 315 Ellis St. Wichita, KS 67211 P 316-262-7271 F 316-262-0149  
 ENGINEERING | SURVEYING | PLANNING | LANDSCAPE ARCHITECTURE

FEBRUARY, 2014  
 SHEET  
**31**  
 OF  
**61**
