


Plotted By : J. TRUMPP
Plot File : 2232TCP3
Plot Date : 4-25-02

Std. Base File :
Server File :
Server :
View=

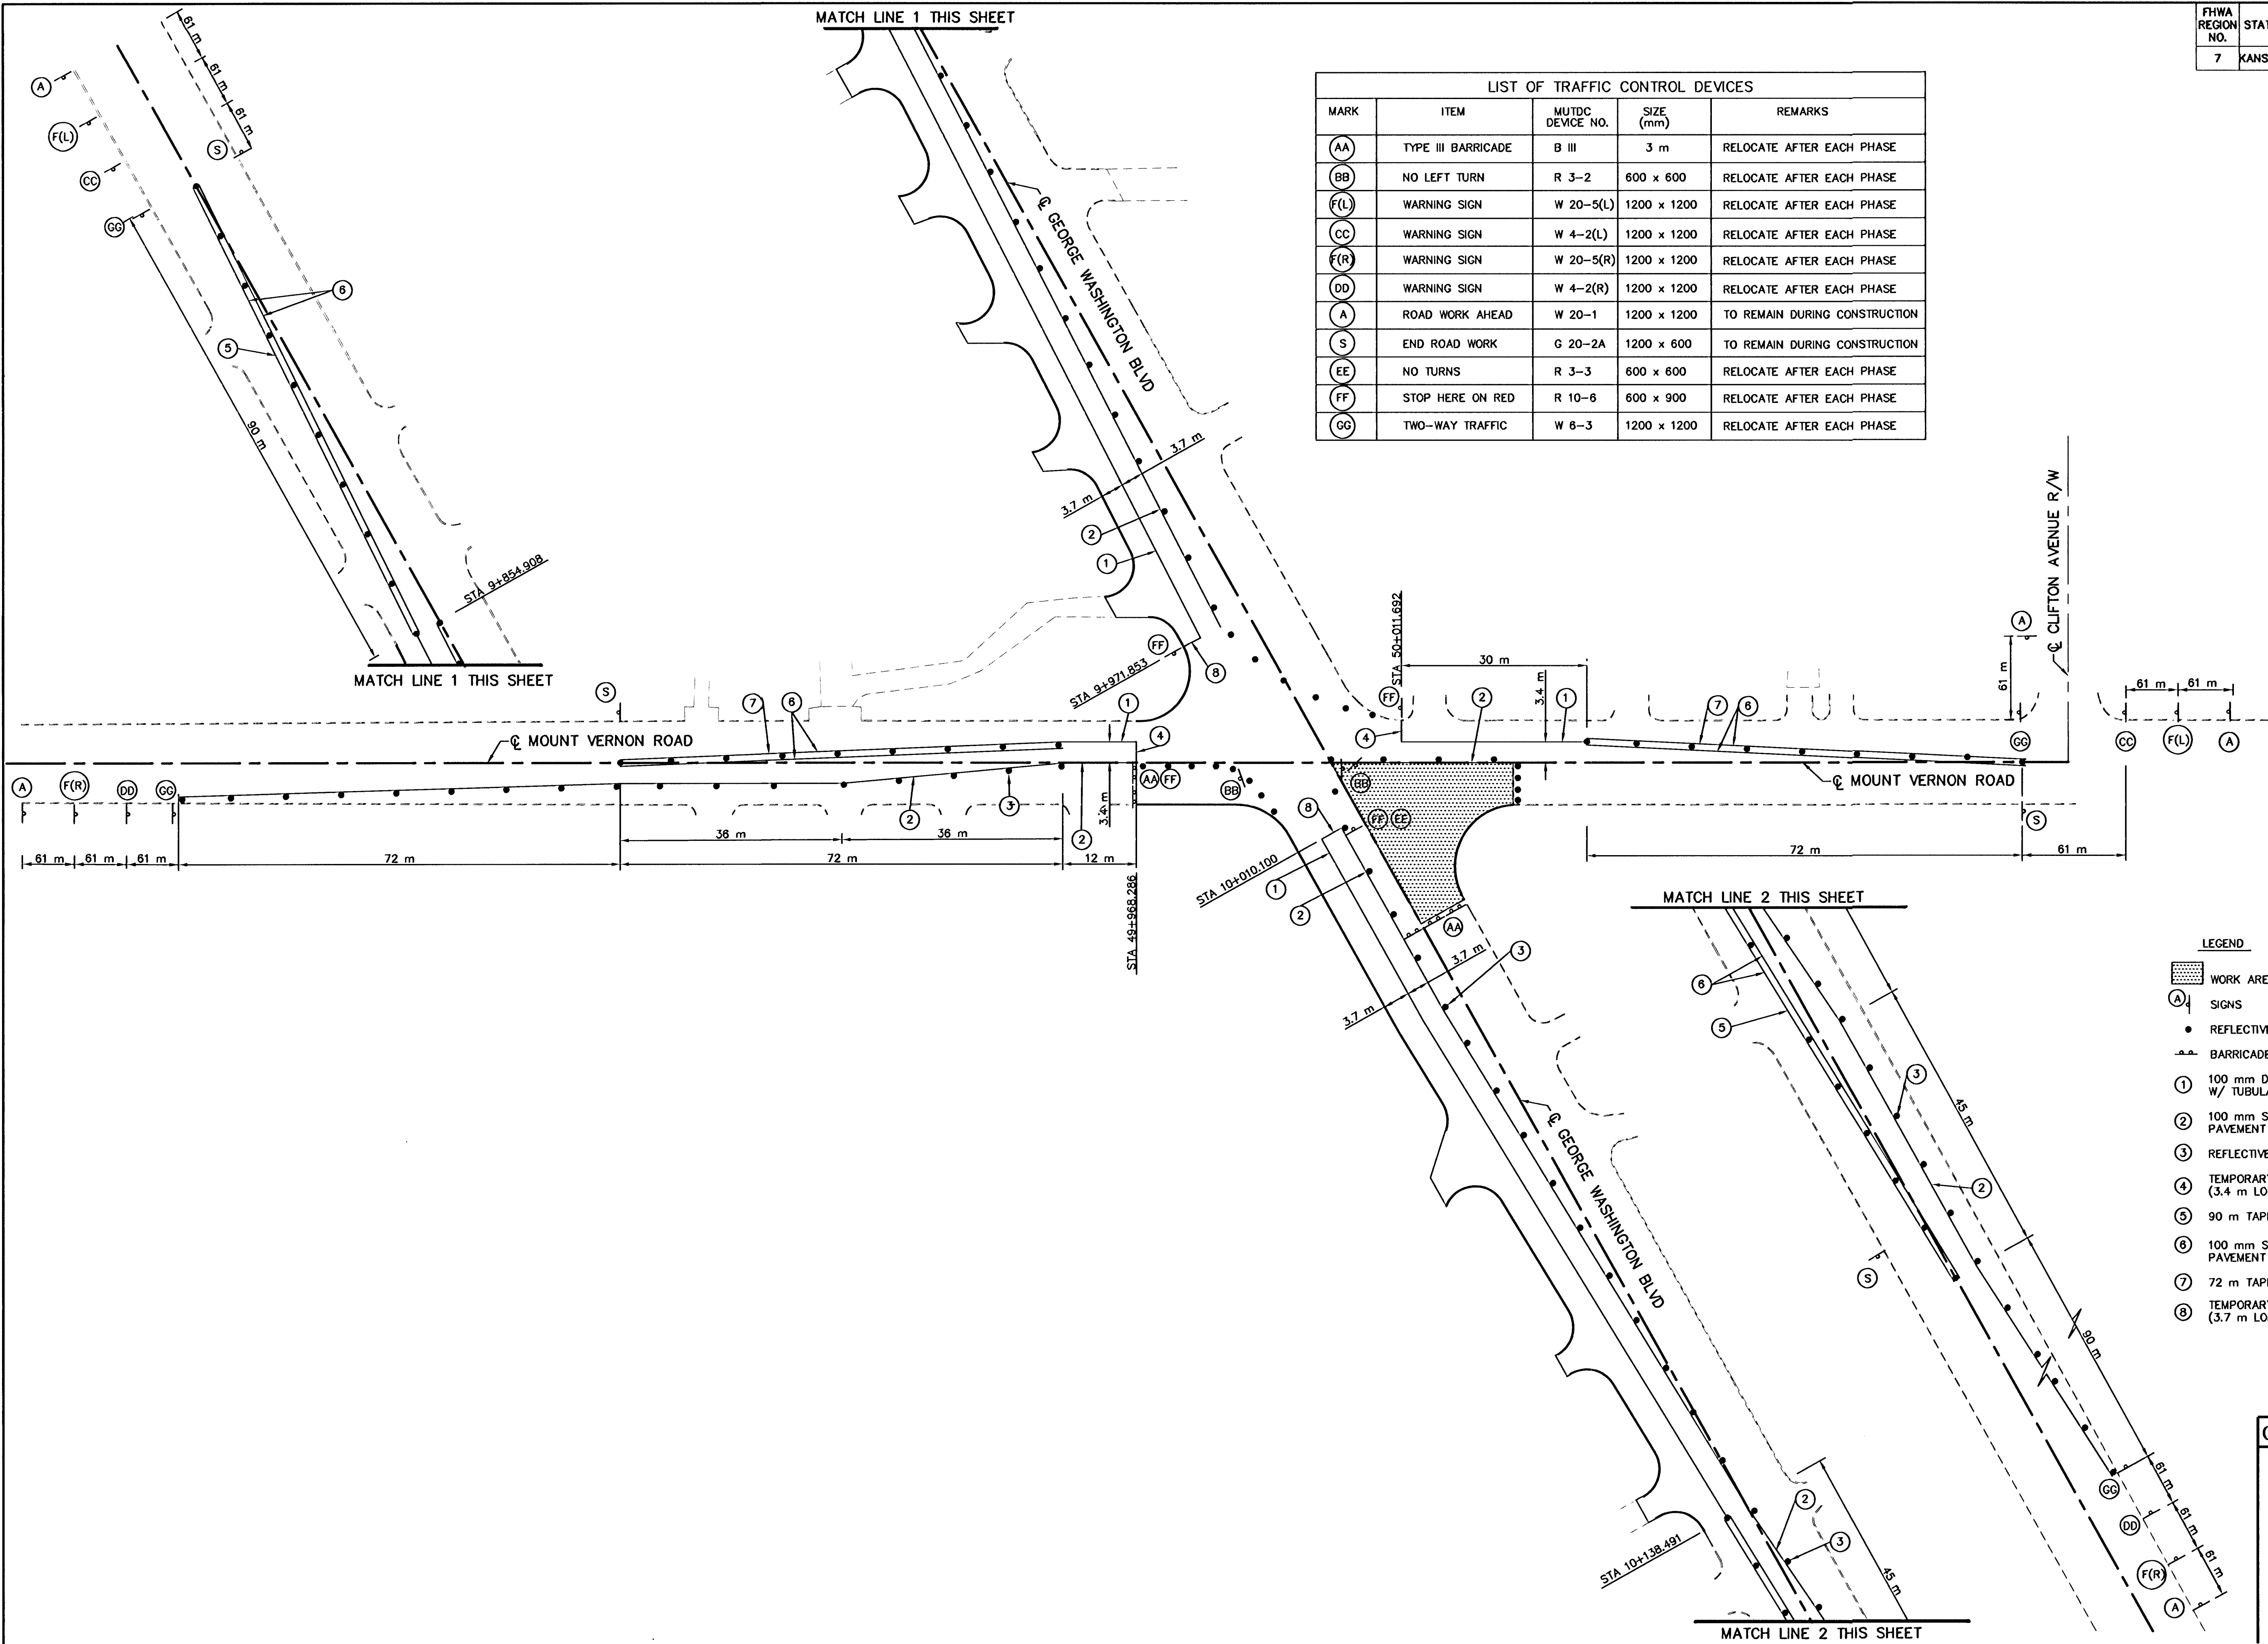

LIST OF TRAFFIC CONTROL DEVICES				
MARK	ITEM	MUTDC DEVICE NO.	SIZE (mm)	REMARKS
AA	TYPE III BARRICADE	B III	3 m	RELOCATE AFTER EACH PHASE
BB	NO LEFT TURN	R 3-2	600 x 600	RELOCATE AFTER EACH PHASE
F(L)	WARNING SIGN	W 20-5(L)	1200 x 1200	RELOCATE AFTER EACH PHASE
CC	WARNING SIGN	W 4-2(L)	1200 x 1200	RELOCATE AFTER EACH PHASE
F(R)	WARNING SIGN	W 20-5(R)	1200 x 1200	RELOCATE AFTER EACH PHASE
DD	WARNING SIGN	W 4-2(R)	1200 x 1200	RELOCATE AFTER EACH PHASE
A	ROAD WORK AHEAD	W 20-1	1200 x 1200	TO REMAIN DURING CONSTRUCTION
S	END ROAD WORK	G 20-2A	1200 x 600	TO REMAIN DURING CONSTRUCTION
EE	NO TURNS	R 3-3	600 x 600	RELOCATE AFTER EACH PHASE
FF	STOP HERE ON RED	R 10-6	600 x 900	RELOCATE AFTER EACH PHASE
GG	TWO-WAY TRAFFIC	W 6-3	1200 x 1200	RELOCATE AFTER EACH PHASE

FHWA REGION NO.	STATE	PROJECT NO.	YEAR	SHEET NO.	TOTAL SHEETS
7	KANSAS	87 N-0212-01	2002	48	59

- LEGEND
- WORK AREA
 - SIGNS
 - REFLECTIVE DRUM
 - BARRICADE
 - 100 mm DOUBLE YELLOW TEMPORARY PAVEMENT MARKING W/ TUBULAR MARKERS @ 9 m SPACING IN NON-TAPER AREAS
 - 100 mm SOLID WHITE TEMPORARY PAVEMENT MARKING
 - REFLECTIVE DRUMS @ 9 m SPACING
 - TEMPORARY 600 mm WHITE STOP BAR (3.4 m LONG)
 - 90 m TAPER W/ REFLECTIVE DRUMS
 - 100 mm SOLID YELLOW TEMPORARY PAVEMENT MARKING
 - 72 m TAPER W/ REFLECTIVE DRUMS
 - TEMPORARY 600 mm WHITE STOP BAR (3.7 m LONG)

PHASE 3

CONSTRUCTION TRAFFIC CONTROL PLAN

KAW VALLEY ENGINEERING
ENGINEERS AND LAND SURVEYORS
2319 NORTH JACKSON
P.O. BOX 1304
JUNCTION CITY, KANSAS 66441
(785)762-5040 FAX (785)762-7744
E-MAIL jco@kveng.com

PROJ. NO. A02232	DATE 4-25-02
DESIGNER CDM	DRAWN BY JT/JL
CHECKED BY CFN	SHEET 48 OF 59
