



BENCHMARKS:
 CHISELED "□", TOP OF CURB INLET, NW COR.
 OF CURB INLET, 77.8' W. & 16.1' N. OF NW
 COR., E1/2, NW1/4, SEC. 34, TWP. 27-S,
 R-2-E.
 ELEV. = 1332.09 NAVD88

CHISELED "□", TOP OF CURB INLET, NW COR.
 OF CURB INLET, 272.1' E. & 16.1' N. OF NW
 COR., E1/2, NW1/4, SEC. 34, TWP. 27-S,
 R-2-E.
 ELEV. = 1329.53 NAVD88



WILLOW CREEK EAST 4TH ADDITION

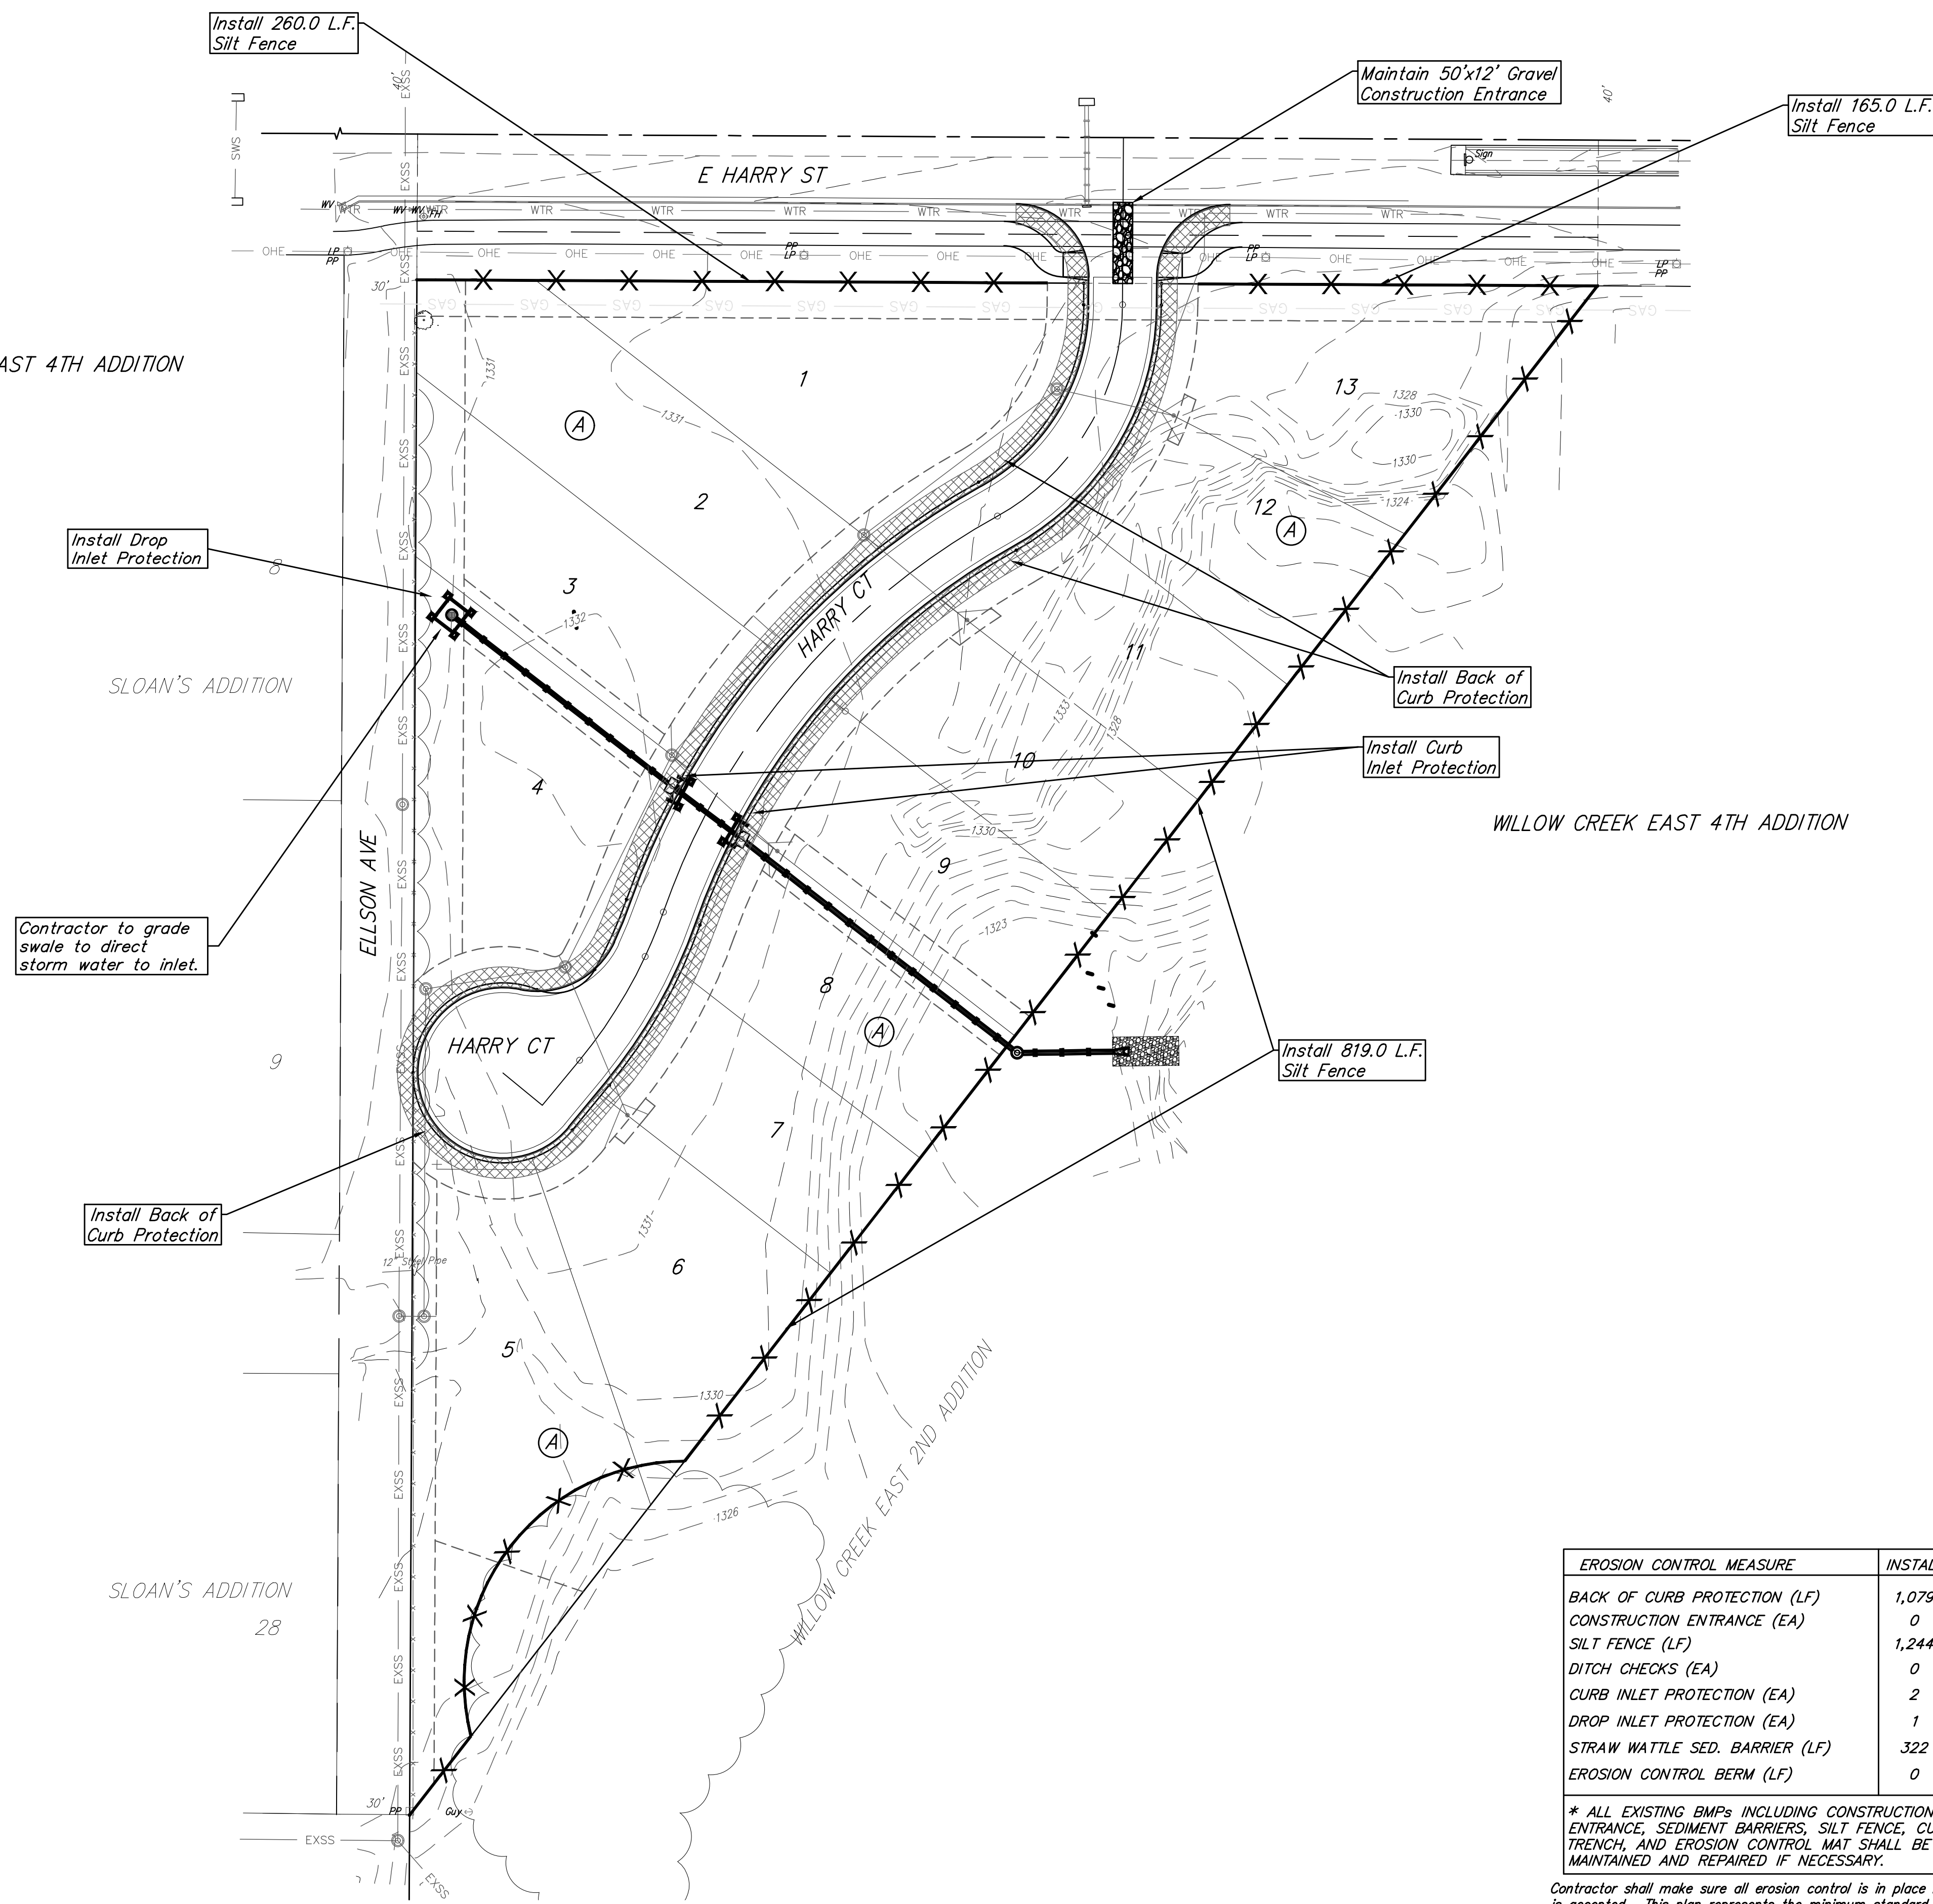


SLOAN'S ADDITION

WILLOW CREEK EAST 4TH ADDITION

Contractor to grade swale to direct storm water to inlet.

Install Back of Curb Protection

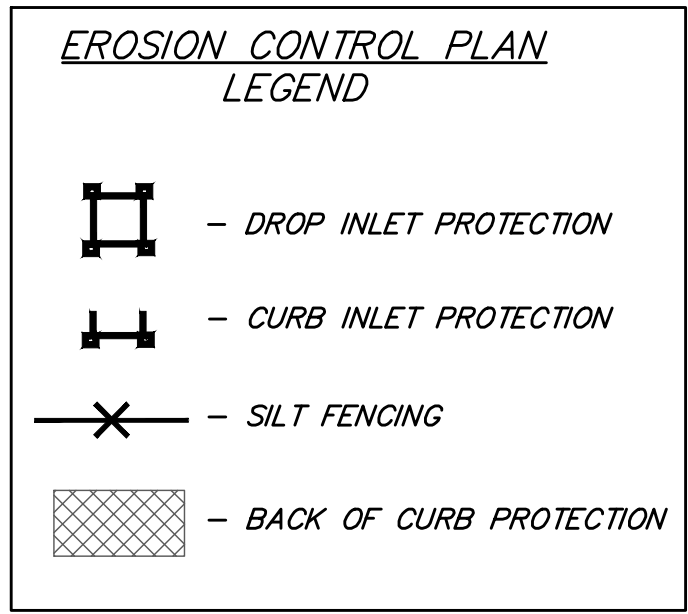

Native Seed Mixture:
 PLS Rate: lbs./ac.

Item:	Rate:
Fertilizer (16-20-0)	80
Big Bluestem Grass Seed (Kaw)	2
Canada Wildrye Grass Seed	10
Indiangrass Seed (Osage)	2
Little Bluestem Grass Seed (Aldous)	2
Side Oats Grama Grass Seed (El Reno)	6.3
Sterile Wheatgrass (Regreen/Quick Guard)	10
Switchgrass Seed (Blackwell)	1
Tall Dropseed	0.5
Western Wheatgrass Seed (Barton)	4
Annual Rye	5
Prairie Hay/Bromegrass Hay mulch	2 tons/acre

EROSION CONTROL MEASURE	INSTALL	MAINTAIN
BACK OF CURB PROTECTION (LF)	1,079	0
CONSTRUCTION ENTRANCE (EA)	0	1
SILT FENCE (LF)	1,244	0
DITCH CHECKS (EA)	0	0
CURB INLET PROTECTION (EA)	2	0
DROP INLET PROTECTION (EA)	1	0
STRAW WATTLE SED. BARRIER (LF)	322	0
EROSION CONTROL BERM (LF)	0	0

* ALL EXISTING BMPs INCLUDING CONSTRUCTION ENTRANCE, SEDIMENT BARRIERS, SILT FENCE, CUT-OFF TRENCH, AND EROSION CONTROL MAT SHALL BE MAINTAINED AND REPAIRED IF NECESSARY.

Contractor shall make sure all erosion control is in place before project is accepted. This plan represents the minimum standard. Any additional erosion control measures shall be installed by the Contractor as needed.

Willow Creek East 4th Addition
EROSION CONTROL PLAN
 Street/SWS Improvements

Baughman Company, P.A. 315 Ellis St. Wichita, KS 67211 P 316-262-7271 F 316-262-0149
 ENGINEERING | SURVEYING | PLANNING | LANDSCAPE ARCHITECTURE

<small>PROJECT NUMBER</small> 472-2020-085611	<small>DESIGN</small> AEG
<small>DRAWN</small> HW	<small>DATE</small> 10/05/20
<small>REVISIONS:</small>	<small>SCALE</small> Noted
11 OF 25	

C:\Projects\Willow Creek East 4th Addition_19-09-1485\Engineering\Phase 1\STR SWS\SWS.dwg
