


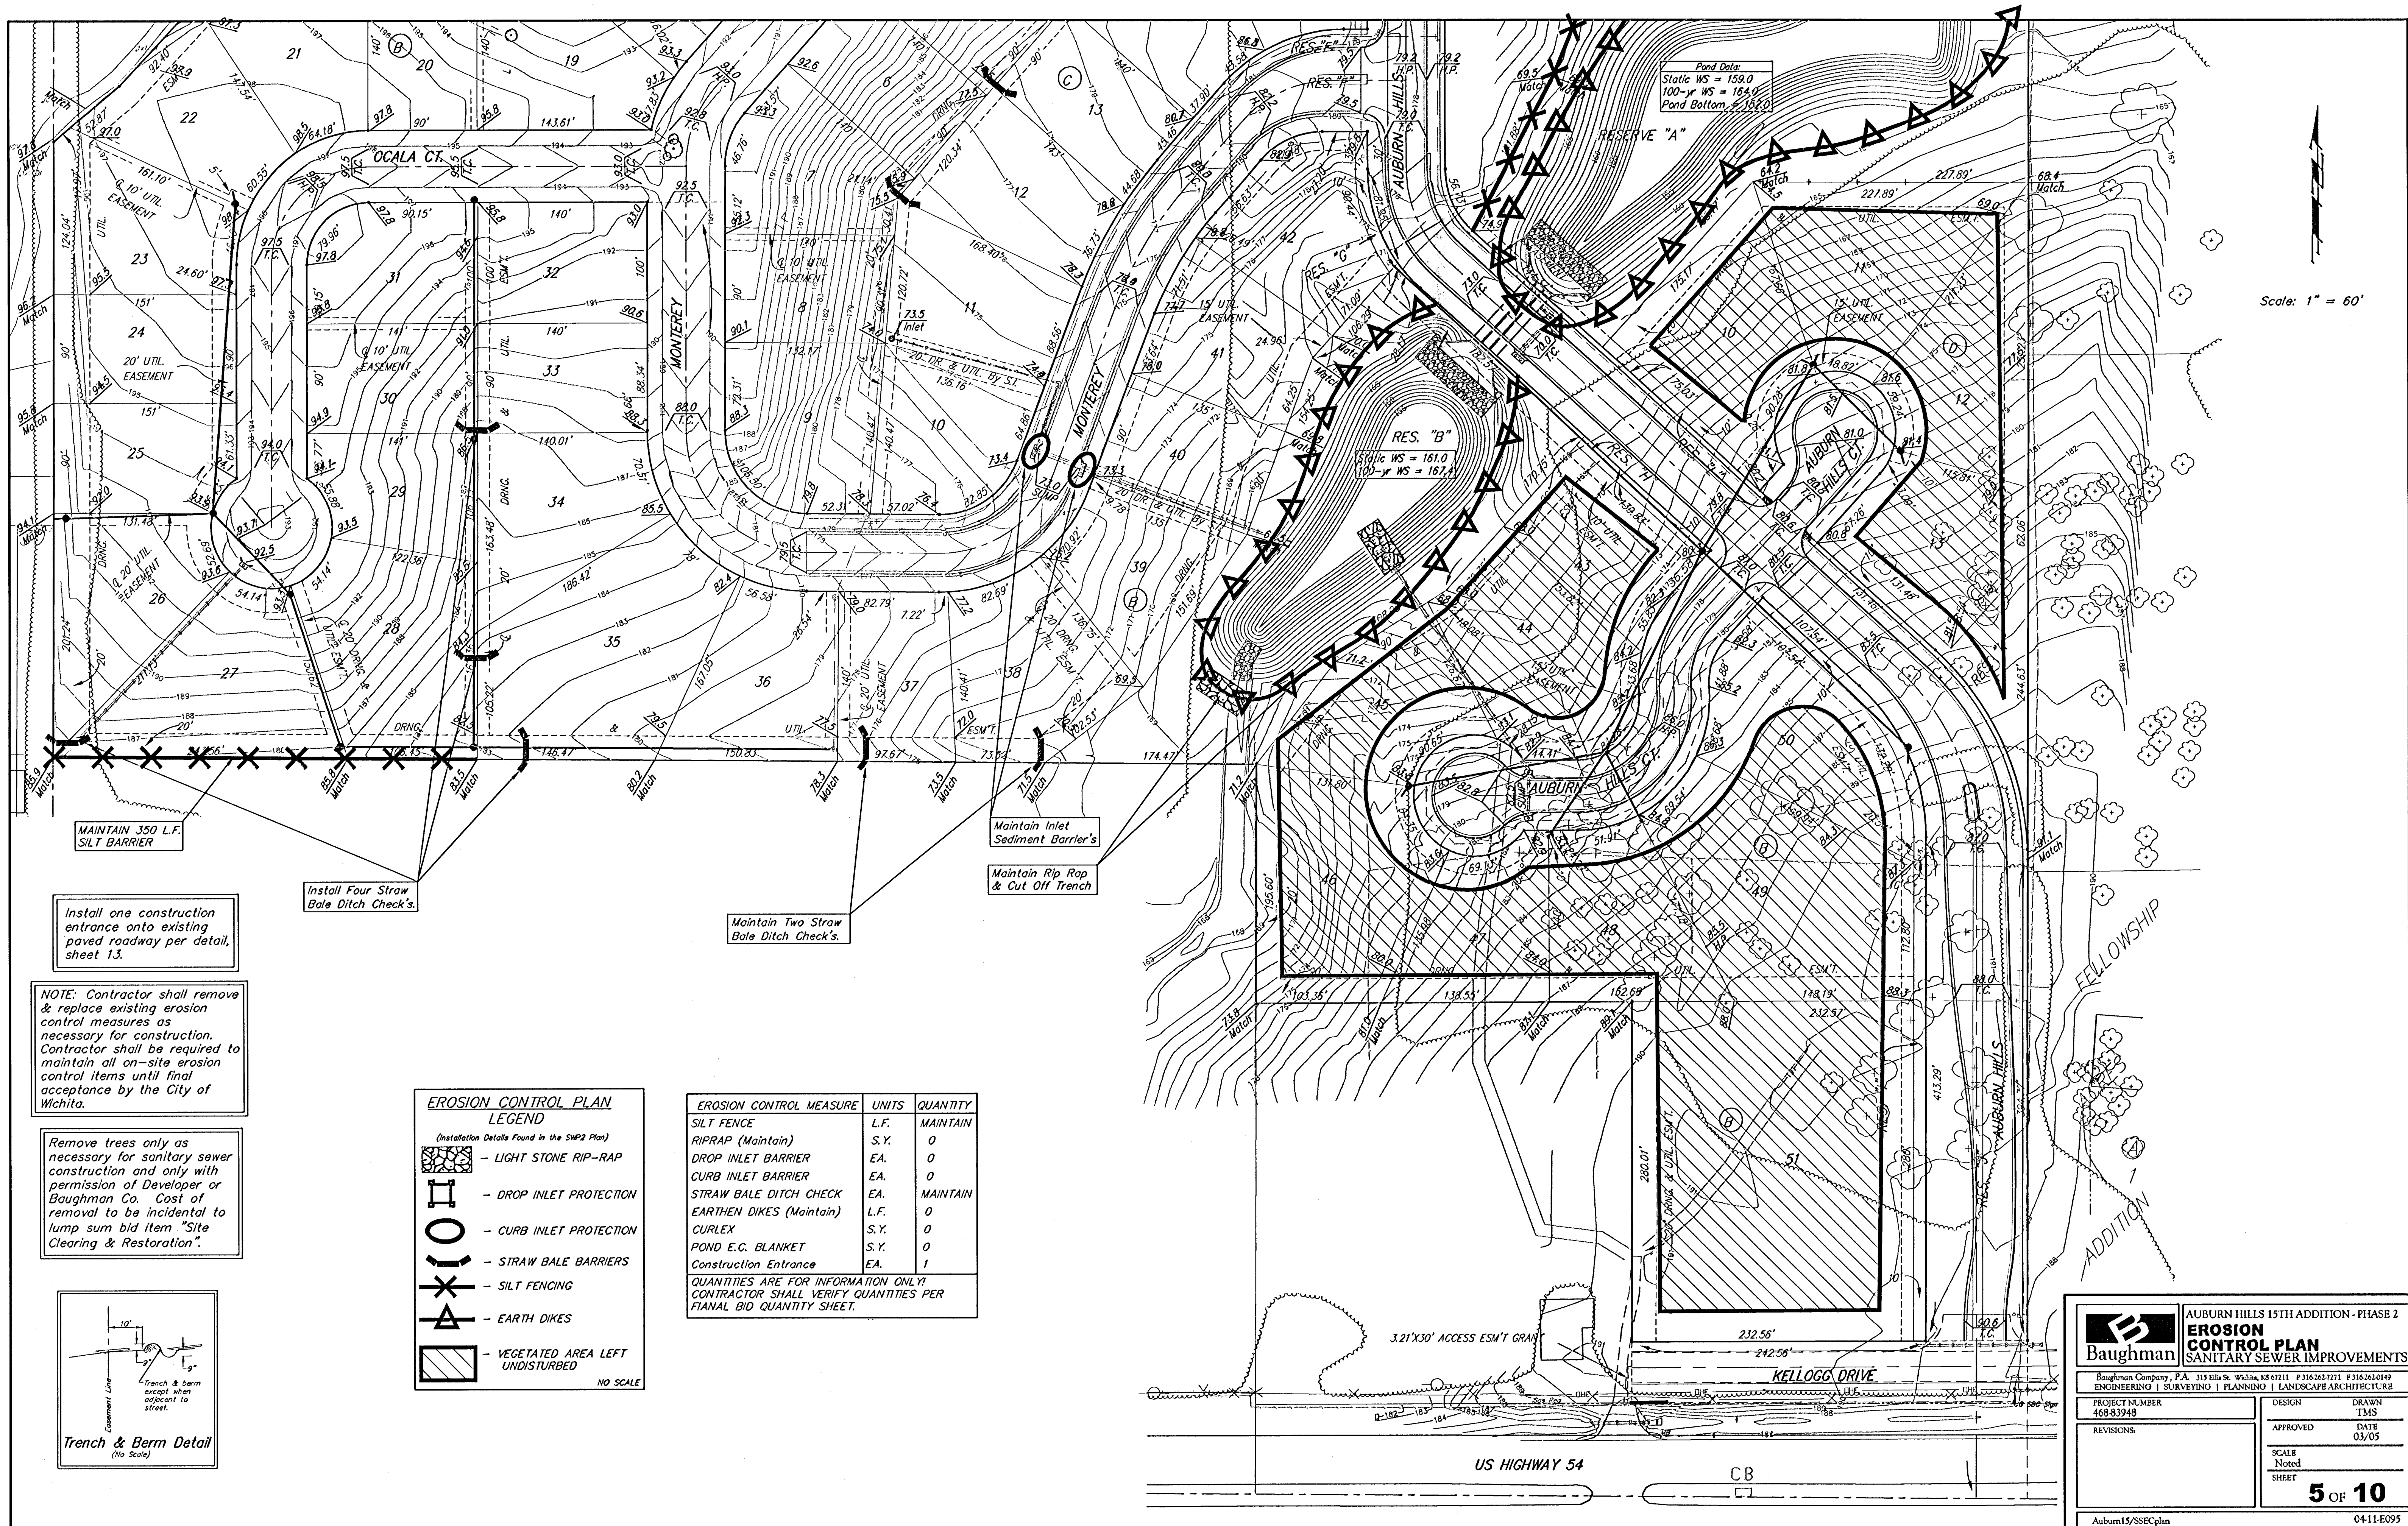

MAINTAIN 350 L.F. SILT BARRIER

Install one construction entrance onto existing paved roadway per detail, sheet 13.

NOTE: Contractor shall remove & replace existing erosion control measures as necessary for construction. Contractor shall be required to maintain all on-site erosion control items until final acceptance by the City of Wichita.

Remove trees only as necessary for sanitary sewer construction and only with permission of Developer or Baughman Co. Cost of removal to be incidental to lump sum bid item "Site Clearing & Restoration".

Install Four Straw Bale Ditch Check's.

Maintain Two Straw Bale Ditch Check's.

Maintain Inlet Sediment Barrier's

Maintain Rip Rap & Cut Off Trench


EROSION CONTROL PLAN LEGEND
(Installation Details Found in the SMP2 Plan)

- LIGHT STONE RIP-RAP
- DROP INLET PROTECTION
- CURB INLET PROTECTION
- STRAW BALE BARRIERS
- SILT FENCING
- EARTH DIKES
- VEGETATED AREA LEFT UNDISTURBED

NO SCALE

EROSION CONTROL MEASURE	UNITS	QUANTITY
SILT FENCE	L.F.	MAINTAIN
RIPRAP (Maintain)	S.Y.	0
DROP INLET BARRIER	EA.	0
CURB INLET BARRIER	EA.	0
STRAW BALE DITCH CHECK	EA.	MAINTAIN
EARTHEN DIKES (Maintain)	L.F.	0
CURLEX	S.Y.	0
POND E.C. BLANKET	S.Y.	0
Construction Entrance	EA.	1

QUANTITIES ARE FOR INFORMATION ONLY!
CONTRACTOR SHALL VERIFY QUANTITIES PER FINAL BID QUANTITY SHEET.

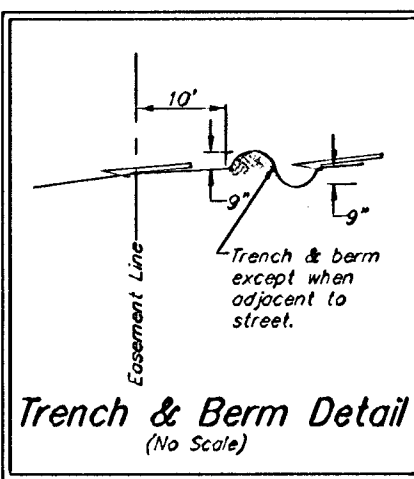

Trench & Berm Detail
(No Scale)

Baughman

Baughman Company, P.A. 315 Ellis St. Wichita, KS 67211 P 316-262-7271 F 316-262-0149
ENGINEERING | SURVEYING | PLANNING | LANDSCAPE ARCHITECTURE

AUBURN HILLS 15TH ADDITION - PHASE 2

EROSION CONTROL PLAN

SANITARY SEWER IMPROVEMENTS

PROJECT NUMBER
468-83948

DESIGN
TMS

APPROVED
DATE
03/05

REVISIONS

SCALE
Noted
SHEET

5 OF 10

Auburn15/SSecPlan

0411-E095
