


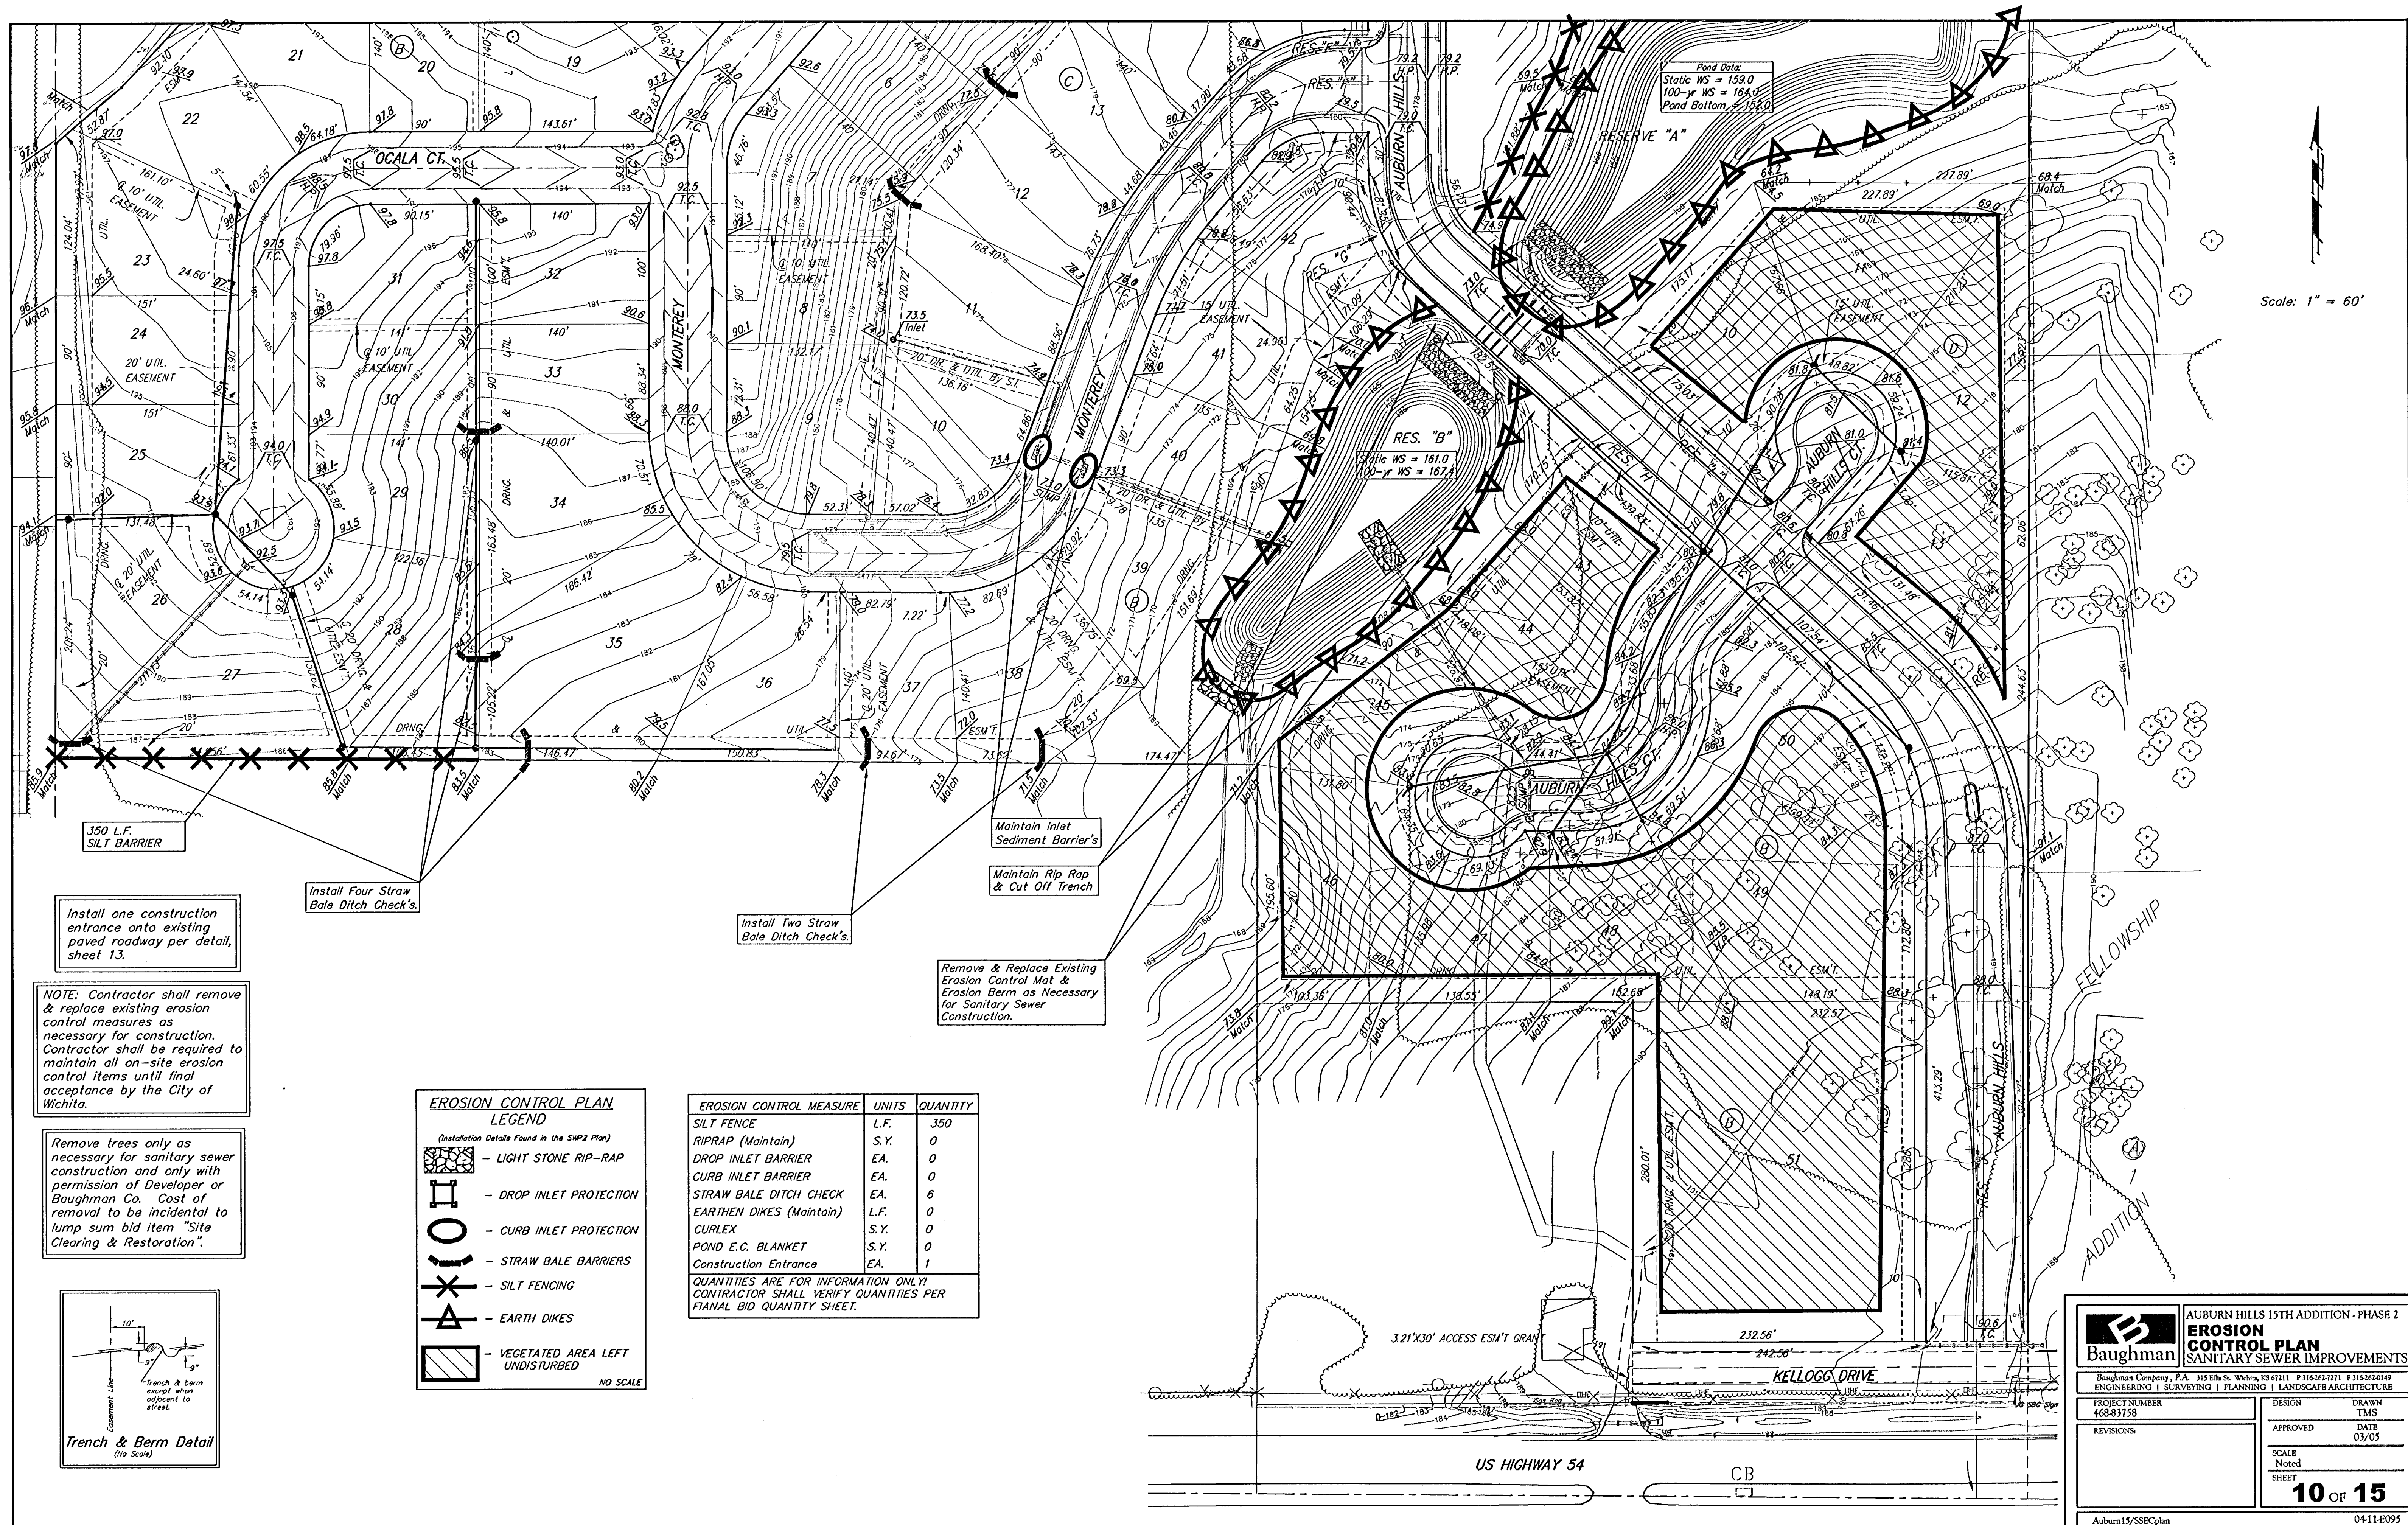


350 L.F.
SILT BARRIER

Install one construction
entrance onto existing
paved roadway per detail,
sheet 13.

NOTE: Contractor shall remove
& replace existing erosion
control measures as
necessary for construction.
Contractor shall be required to
maintain all on-site erosion
control items until final
acceptance by the City of
Wichita.

Remove trees only as
necessary for sanitary sewer
construction and only with
permission of Developer or
Baughman Co. Cost of
removal to be incidental to
lump sum bid item "Site
Clearing & Restoration".

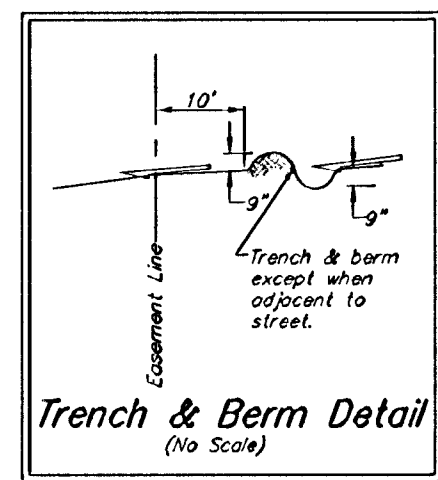

Install Four Straw
Bale Ditch Check's.

Install Two Straw
Bale Ditch Check's.

Maintain Inlet
Sediment Barrier's

Maintain Rip Rap
& Cut Off Trench

Remove & Replace Existing
Erosion Control Mat &
Erosion Berm as Necessary
for Sanitary Sewer
Construction.

EROSION CONTROL PLAN LEGEND	
(Installation Details Found in the SWS Plan)	
	- LIGHT STONE RIP-RAP
	- DROP INLET PROTECTION
	- CURB INLET PROTECTION
	- STRAW BALE BARRIERS
	- SILTING FENCING
	- EARTH DIKES
	- VEGETATED AREA LEFT UNDISTURBED

EROSION CONTROL MEASURE	UNITS	QUANTITY
SILT FENCE	L.F.	350
RIPRAP (Maintain)	S.Y.	0
DROP INLET BARRIER	EA.	0
CURB INLET BARRIER	EA.	0
STRAW BALE DITCH CHECK	EA.	6
EARTHEN DIKES (Maintain)	L.F.	0
CURLEX	S.Y.	0
POND E.C. BLANKET	S.Y.	0
Construction Entrance	EA.	1

QUANTITIES ARE FOR INFORMATION ONLY!
CONTRACTOR SHALL VERIFY QUANTITIES PER
FINAL BID QUANTITY SHEET.

Baughman

AUBURN HILLS 15TH ADDITION - PHASE 2
EROSION CONTROL PLAN
SANITARY SEWER IMPROVEMENTS

Baughman Company, P.A. 115 Ellis St. Wichita, KS 67211 P 316.263.7711 F 316.263.7419
ENGINEERING | SURVEYING | PLANNING | LANDSCAPE ARCHITECTURE

PROJECT NUMBER 468-83758	DESIGN TMS
REVISIONS	APPROVED DATE 03/05
	SCALE Noted

10 OF 15
Auburn15/SSecplan 0411E095
