




Q SYMMETRIC



NO SCALE



DEPARTMENT OF PUBLIC WORKS-ENGINEERING DIVISION
B. E. SMITH CITY ENGINEER
DATE: MARCH 1971 PROJ. NO. ~~CIO-35~~

DATE: MARCH 1971

CITY ENGINEER
PROJ. NO. ~~C10-88~~
DAKS 570035



Engl. - 12
14.62 - 1"

Contractor to notify Mr. C. R. Rogers, District Supervisor, State Highway Commission, El Dorado, Kansas prior to construction & after completion of construction. Drainage requirements on State Highway ROW to be determined by the State Highway Commission Division.

Contractor to remove asphalt mat 50 ft. south of U.S. 54 Highway ROW north to U.S. 54 Concrete slab. Contractor to grade parking & clear right of way for proposed sidewalk. Compact backfill in Sidewalk area. Sidewalk by Others.

NOTE:

Construction on U.S. 54 R/W west of sta. 2+85.5 & Frontage Road construction west of sta. 3+00 & east of Sta. 4+00 is to be completed & access provided west of sta. 3+00 before the Mound Entrance at sta. 3+45 is removed. Construction on U.S. 54 R/W east of sta. 2+85.5 & Frontage Road Construction from Sta. 3+00 to sta. 4+00 is to be completed after access is provided west of sta. 3+00. Contractor is to construct temporary asphalt ramp over south curb of frontage road west of sta. 3+00 to provide access. Asphalt ramp is to be removed by Contractor after completion of frontage road improvement.

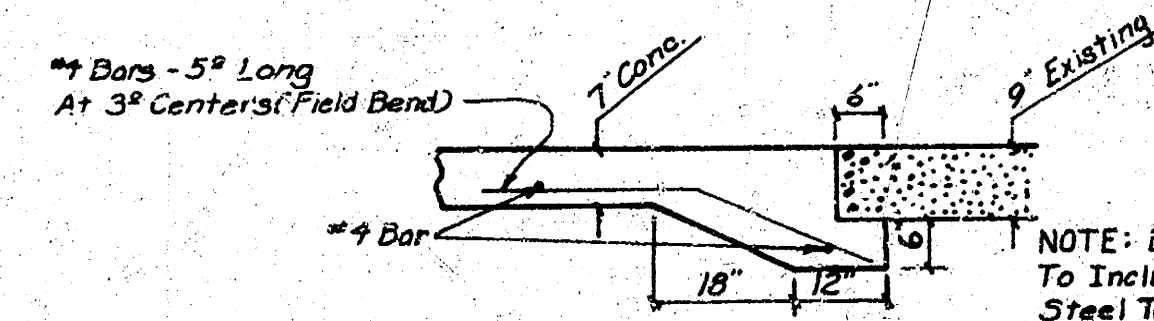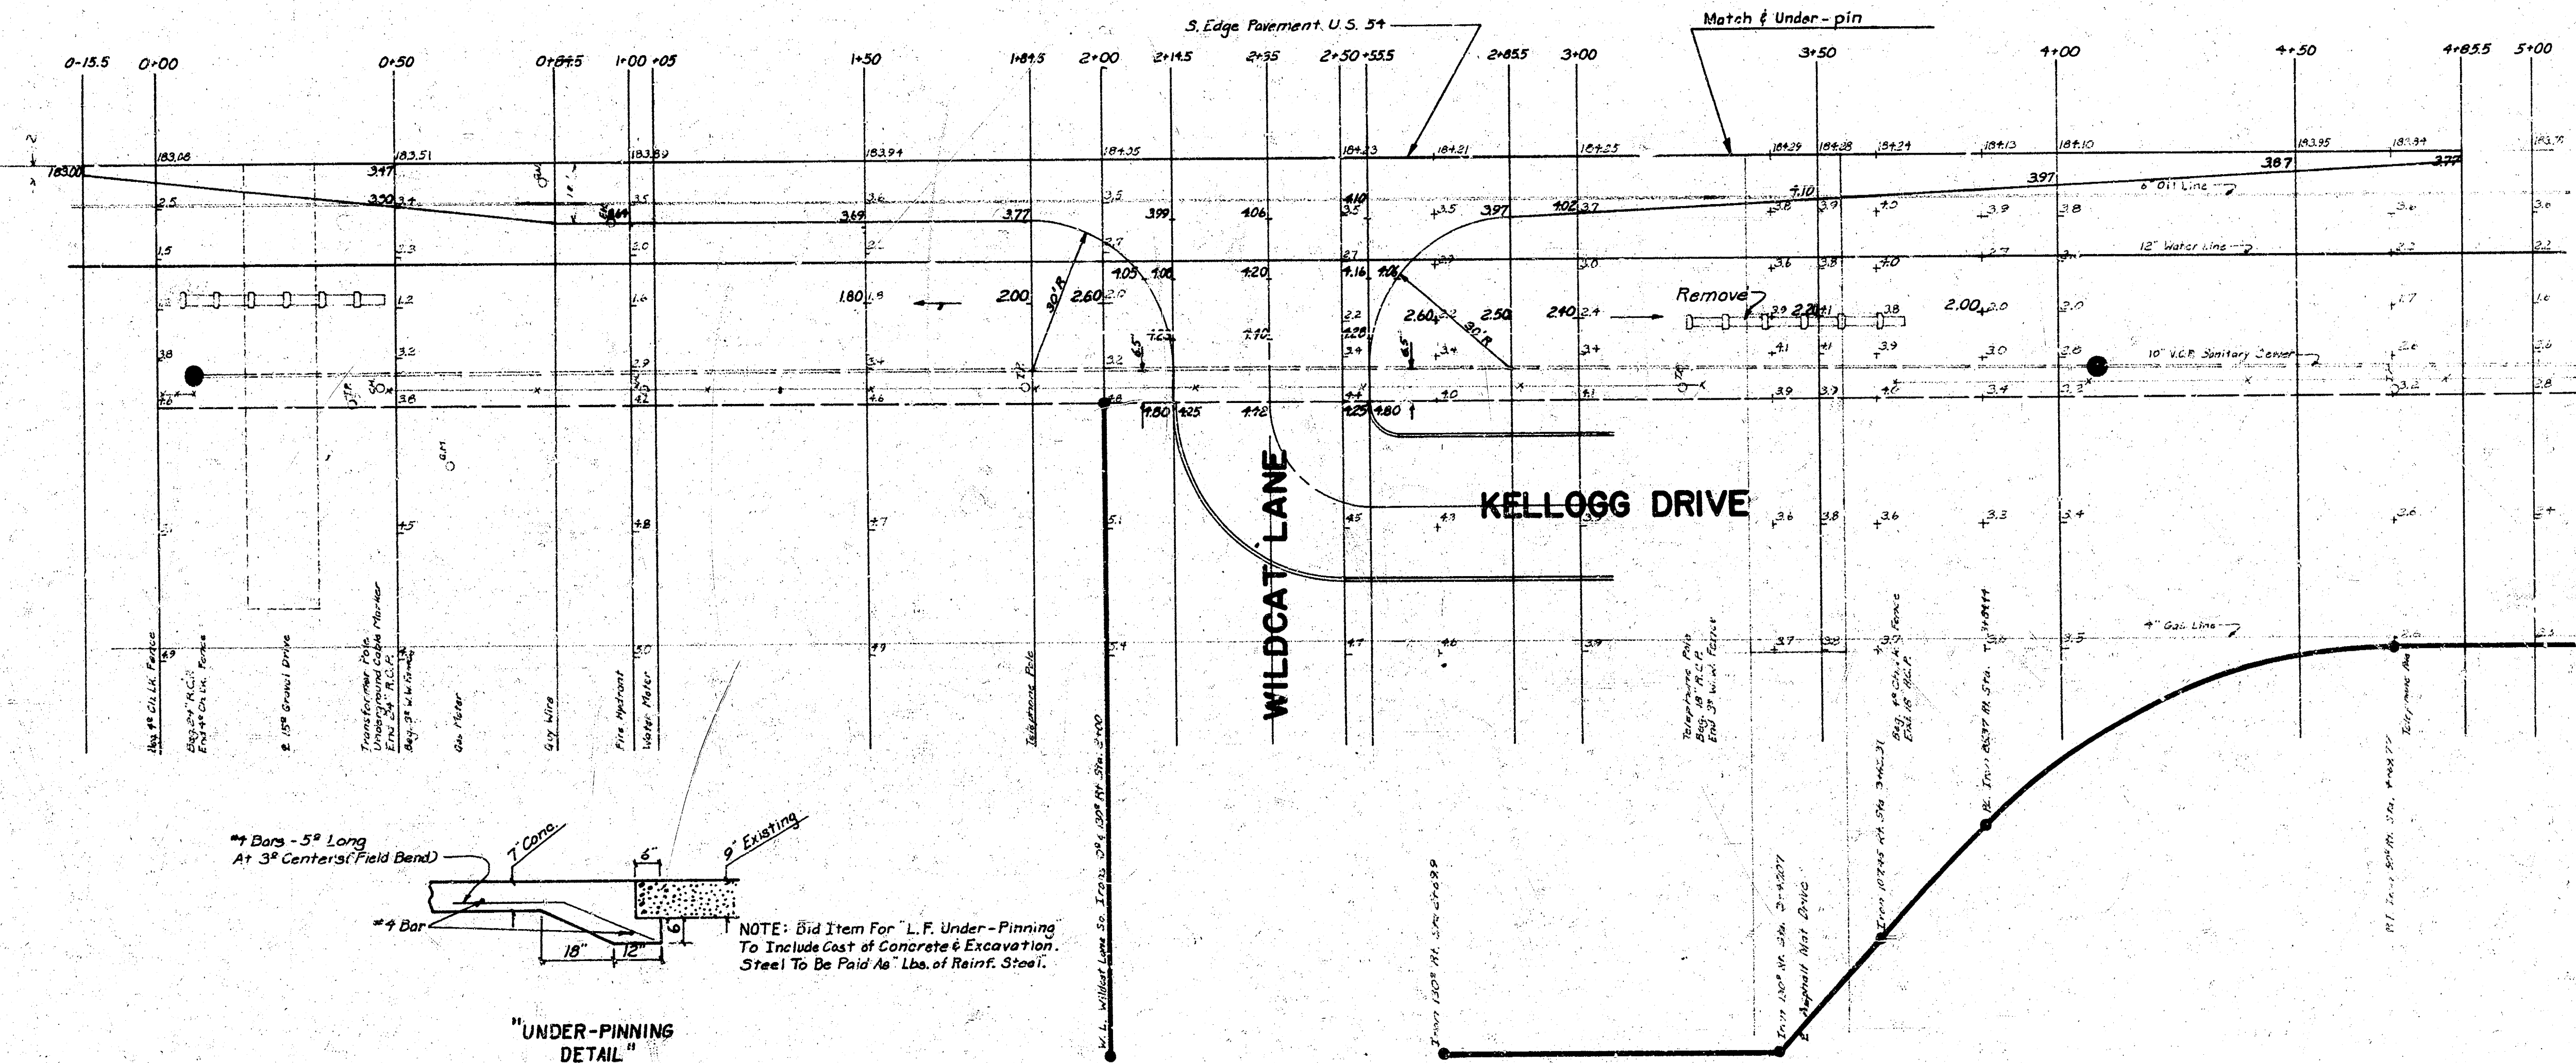

"UNDER-PINNING DETAIL"
