


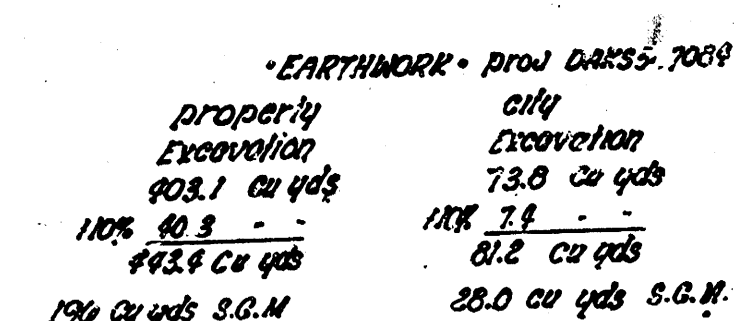

•EARTHWORK • PROJ DMS567005
Property
Excavation
777.9 cu yds
110% 77.8
855.7 cu yds
100 cu yds S.G.M.

WOOD AVE
N. L. Bekemeyer Lane to N.L. Lot 23,
Blk 2, Western Gardens.
26'-2'-30' Asphaltic Concrete


WOOD AVE
N.L. Lot 23, Blk 2, Western Gardens
to N.L. Lot 27, Blk 2, Western Gardens.
26'-2'-30' Asphaltic Concrete

CITY of WICHITA, KANSAS
R.W. LINN CITY ENGINEER
DATE July 1971 Proj No. DAKS5670

CITY of WICHITA, KANSAS
R.W. LINN CITY ENGINEER
DATE July 1971 Proj No. DAKS567085

Sheet 1 of 2

Survey done by
The Surveyor
End Project DAKS567085

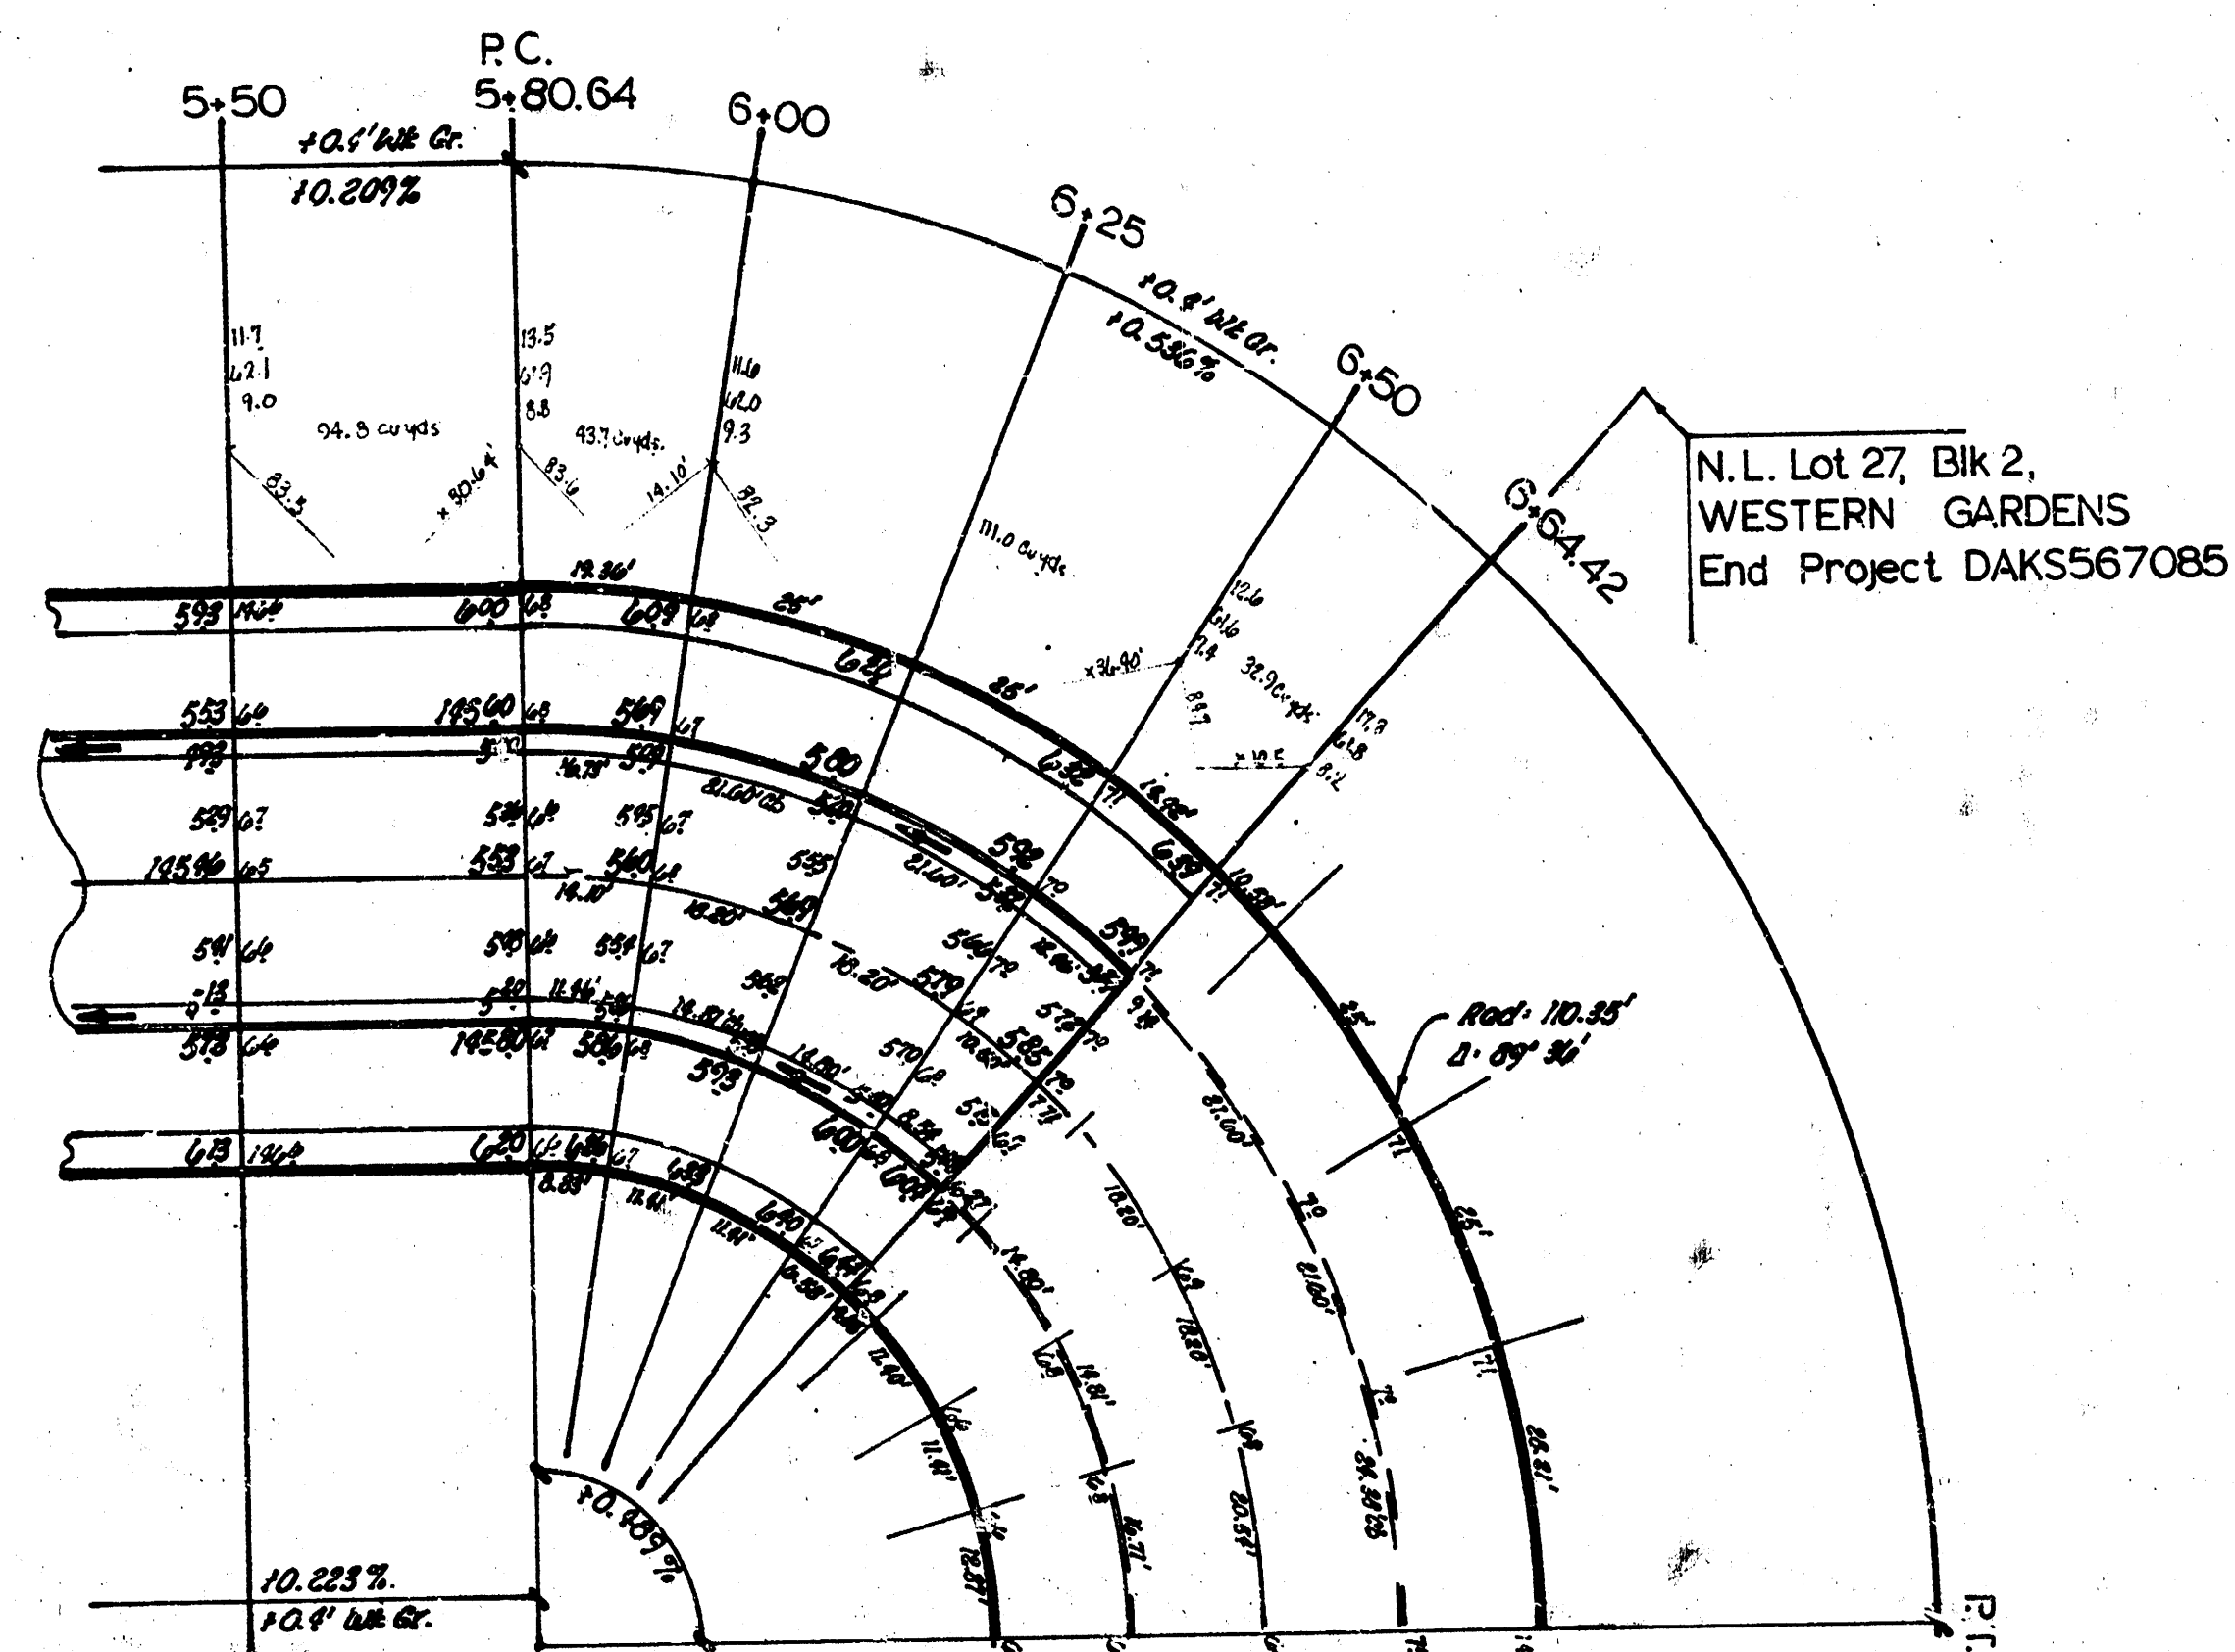

Curve data is as follows: North east property line radius = 110.35'

2.00' 30' 15.5' 11' per 11' arc.

Station	Area	Chord	Angle	Deflection	Total deflection
		10.25% 10.20%	10.25% 10.20%		
Sta. 5+80.64				0° 02' 00"	
6+00	19.86'	10.11'	10.05'	5° 04' 36"	5° 04' 36"
6+15	25.00'	23.86'	12.96'	6° 29' 25"	11° 34' 01"
6+30	25.00'	23.86'	12.96'	6° 29' 25"	18° 03' 26"
6+44.42	11.62'	13.99'	7.99'	5° 44' 57"	23° 48' 23"
6+75	22.55'	9.90'	5.99'	5° 44' 57"	29° 33' 18"
7+00	25.00'	23.86'	12.96'	6° 29' 25"	36° 02' 43"
7+15	25.00'	23.86'	12.96'	6° 29' 25"	42° 32' 08"
RT 7+53.2	20.81'	16.05'	10.05'	7° 19' 25"	49° 51' 33"

End

Construction
