





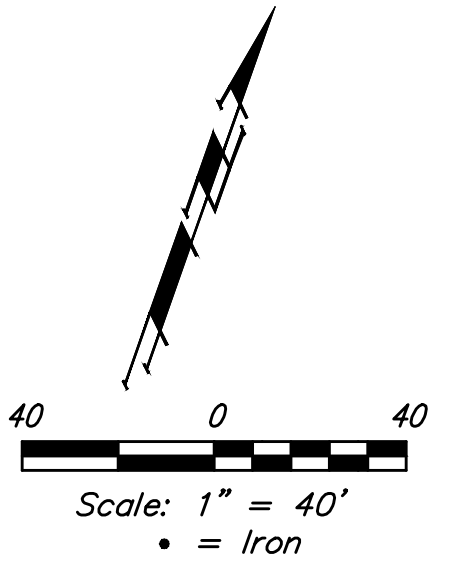


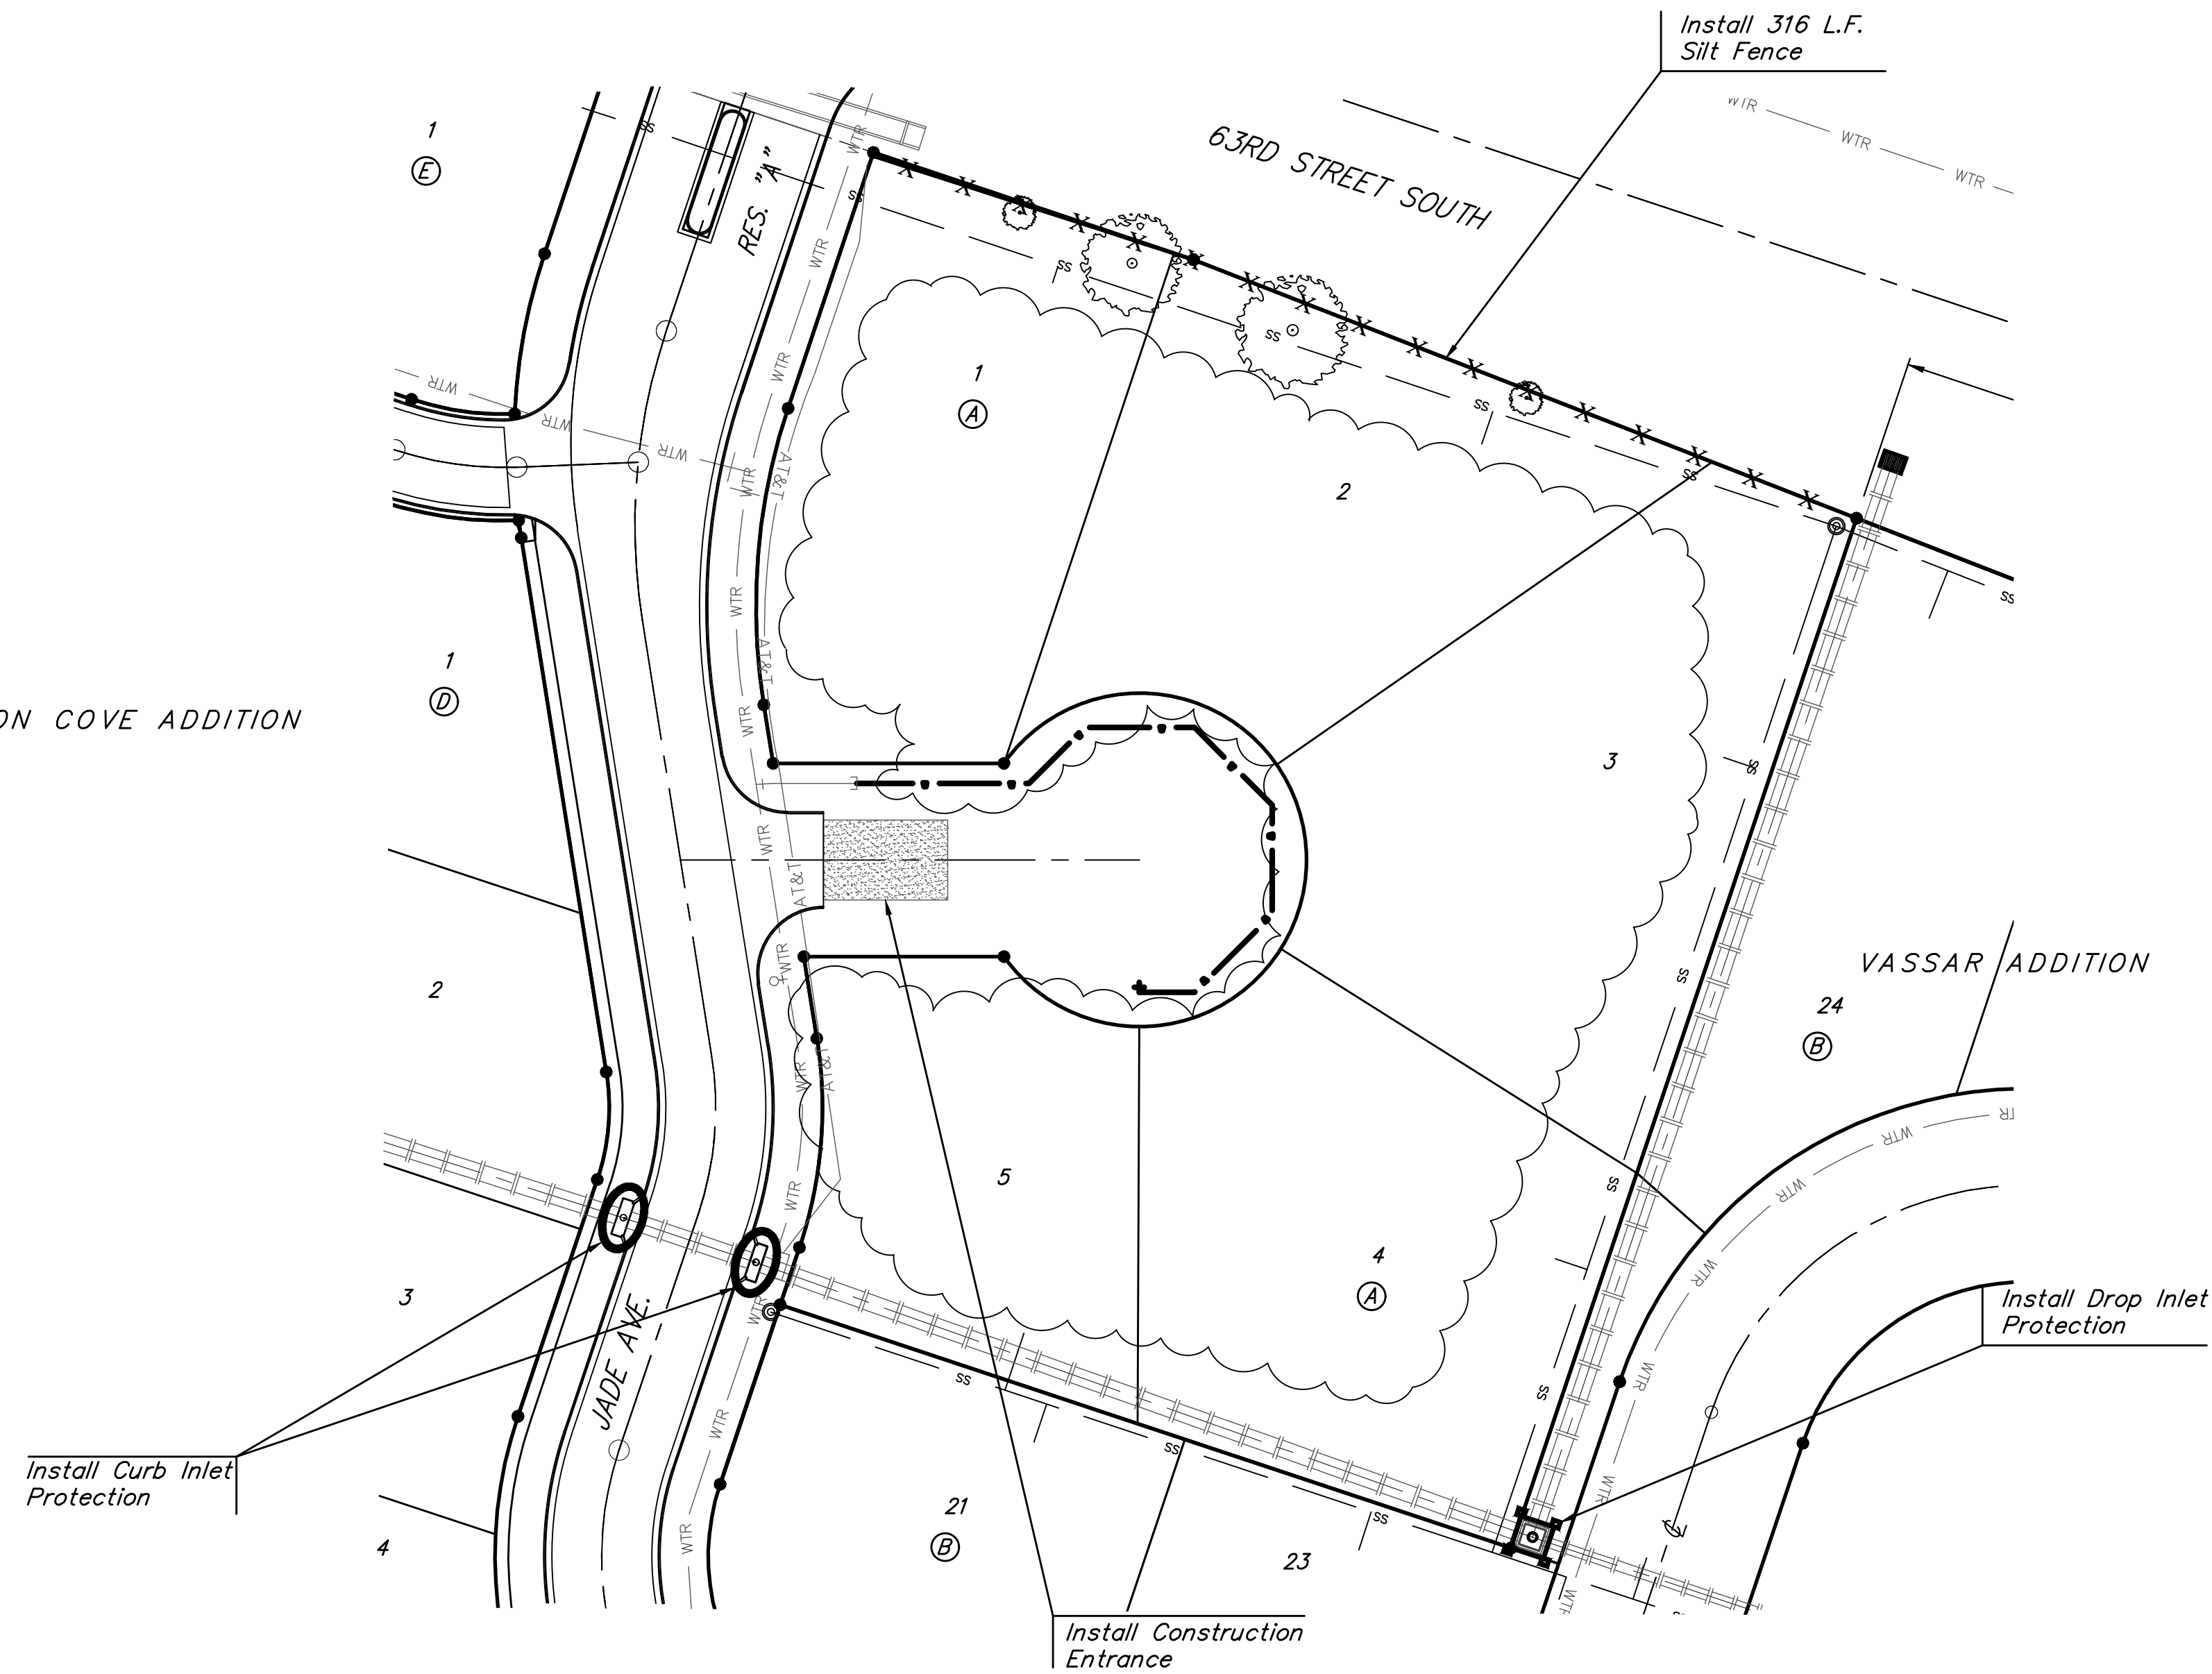


BENCHMARKS:
 BM #1: V-notch cut into sidewalk along east sidewalk along east property line at common corner of Lots 1 & 2, Block D, Clifton Cove Addition.
 Elev. = 1259.70 NGVD29

BM #2: Chiseled cross on walk, southwest of intersection of Jade Avenue and Sunflower Drive, Clifton Cove Addition.
 Elev. = 1257.78 NGVD29

CLIFTON COVE ADDITION



EROSION CONTROL PLAN LEGEND

-  - DROP INLET PROTECTION
-  - CURB INLET PROTECTION
-  - SILT FENCING
-  - STRAW WATTLE FENCING
-  - DITCH CHECKS
-  - BACK OF CURB PROTECTION
-  - RIP RAP PROTECTION
-  - CUT-OFF TRENCH


NOTES:
 Contractor shall make sure all erosion control is in place before project is accepted. This plan represents the minimum standard. Any additional erosion control measures shall be installed by the Contractor as needed.

All areas disturbed during construction shall be seeded, mulched, and fertilized as per Cover Sheet General Notes.

EROSION CONTROL MEASURE	INSTALL	MAINTAIN
CUT-OFF TRENCH (LF)	0	0
CONSTRUCTION ENTRANCE (EA)	1	0
CURB INLET BARRIER (EA)	2	0
DITCH CHECK (EA)	0	0
DROP INLET PROTECTION (EA)	1	0
EROSION CONTROL (LS)	0	0
MULCH WATTLES (LF)	0	0
SILT FENCE (LF)	316	0
EROSION CONTROL MAT (SY)	0	0
MAINTAIN EROSION CONTROL BMP's (LS)	0	0

* ALL EXISTING BMPs INCLUDING CONSTRUCTION ENTRANCE, SEDIMENT BARRIERS, SILT FENCE, CUT-OFF TRENCH, AND EROSION CONTROL MAT SHALL BE MAINTAINED AND REPAIRED IF NECESSARY.





Baughman

Clifton Cove Addition Phase II
EROSION CONTROL PLAN
 Water Distribution System

Baughman Company, P.A. 315 Ellis St. Wichita, KS 67211 P 316-262-7271 F 316-262-0149 ENGINEERING SURVEYING PLANNING LANDSCAPE ARCHITECTURE	
PROJECT NUMBER 448-90915	DESIGN AEG
REVISIONS:	DRAWN HIW
	APPROVED DATE 9/11/18
	SCALE Noted
	SHEET

5 OF 12
