


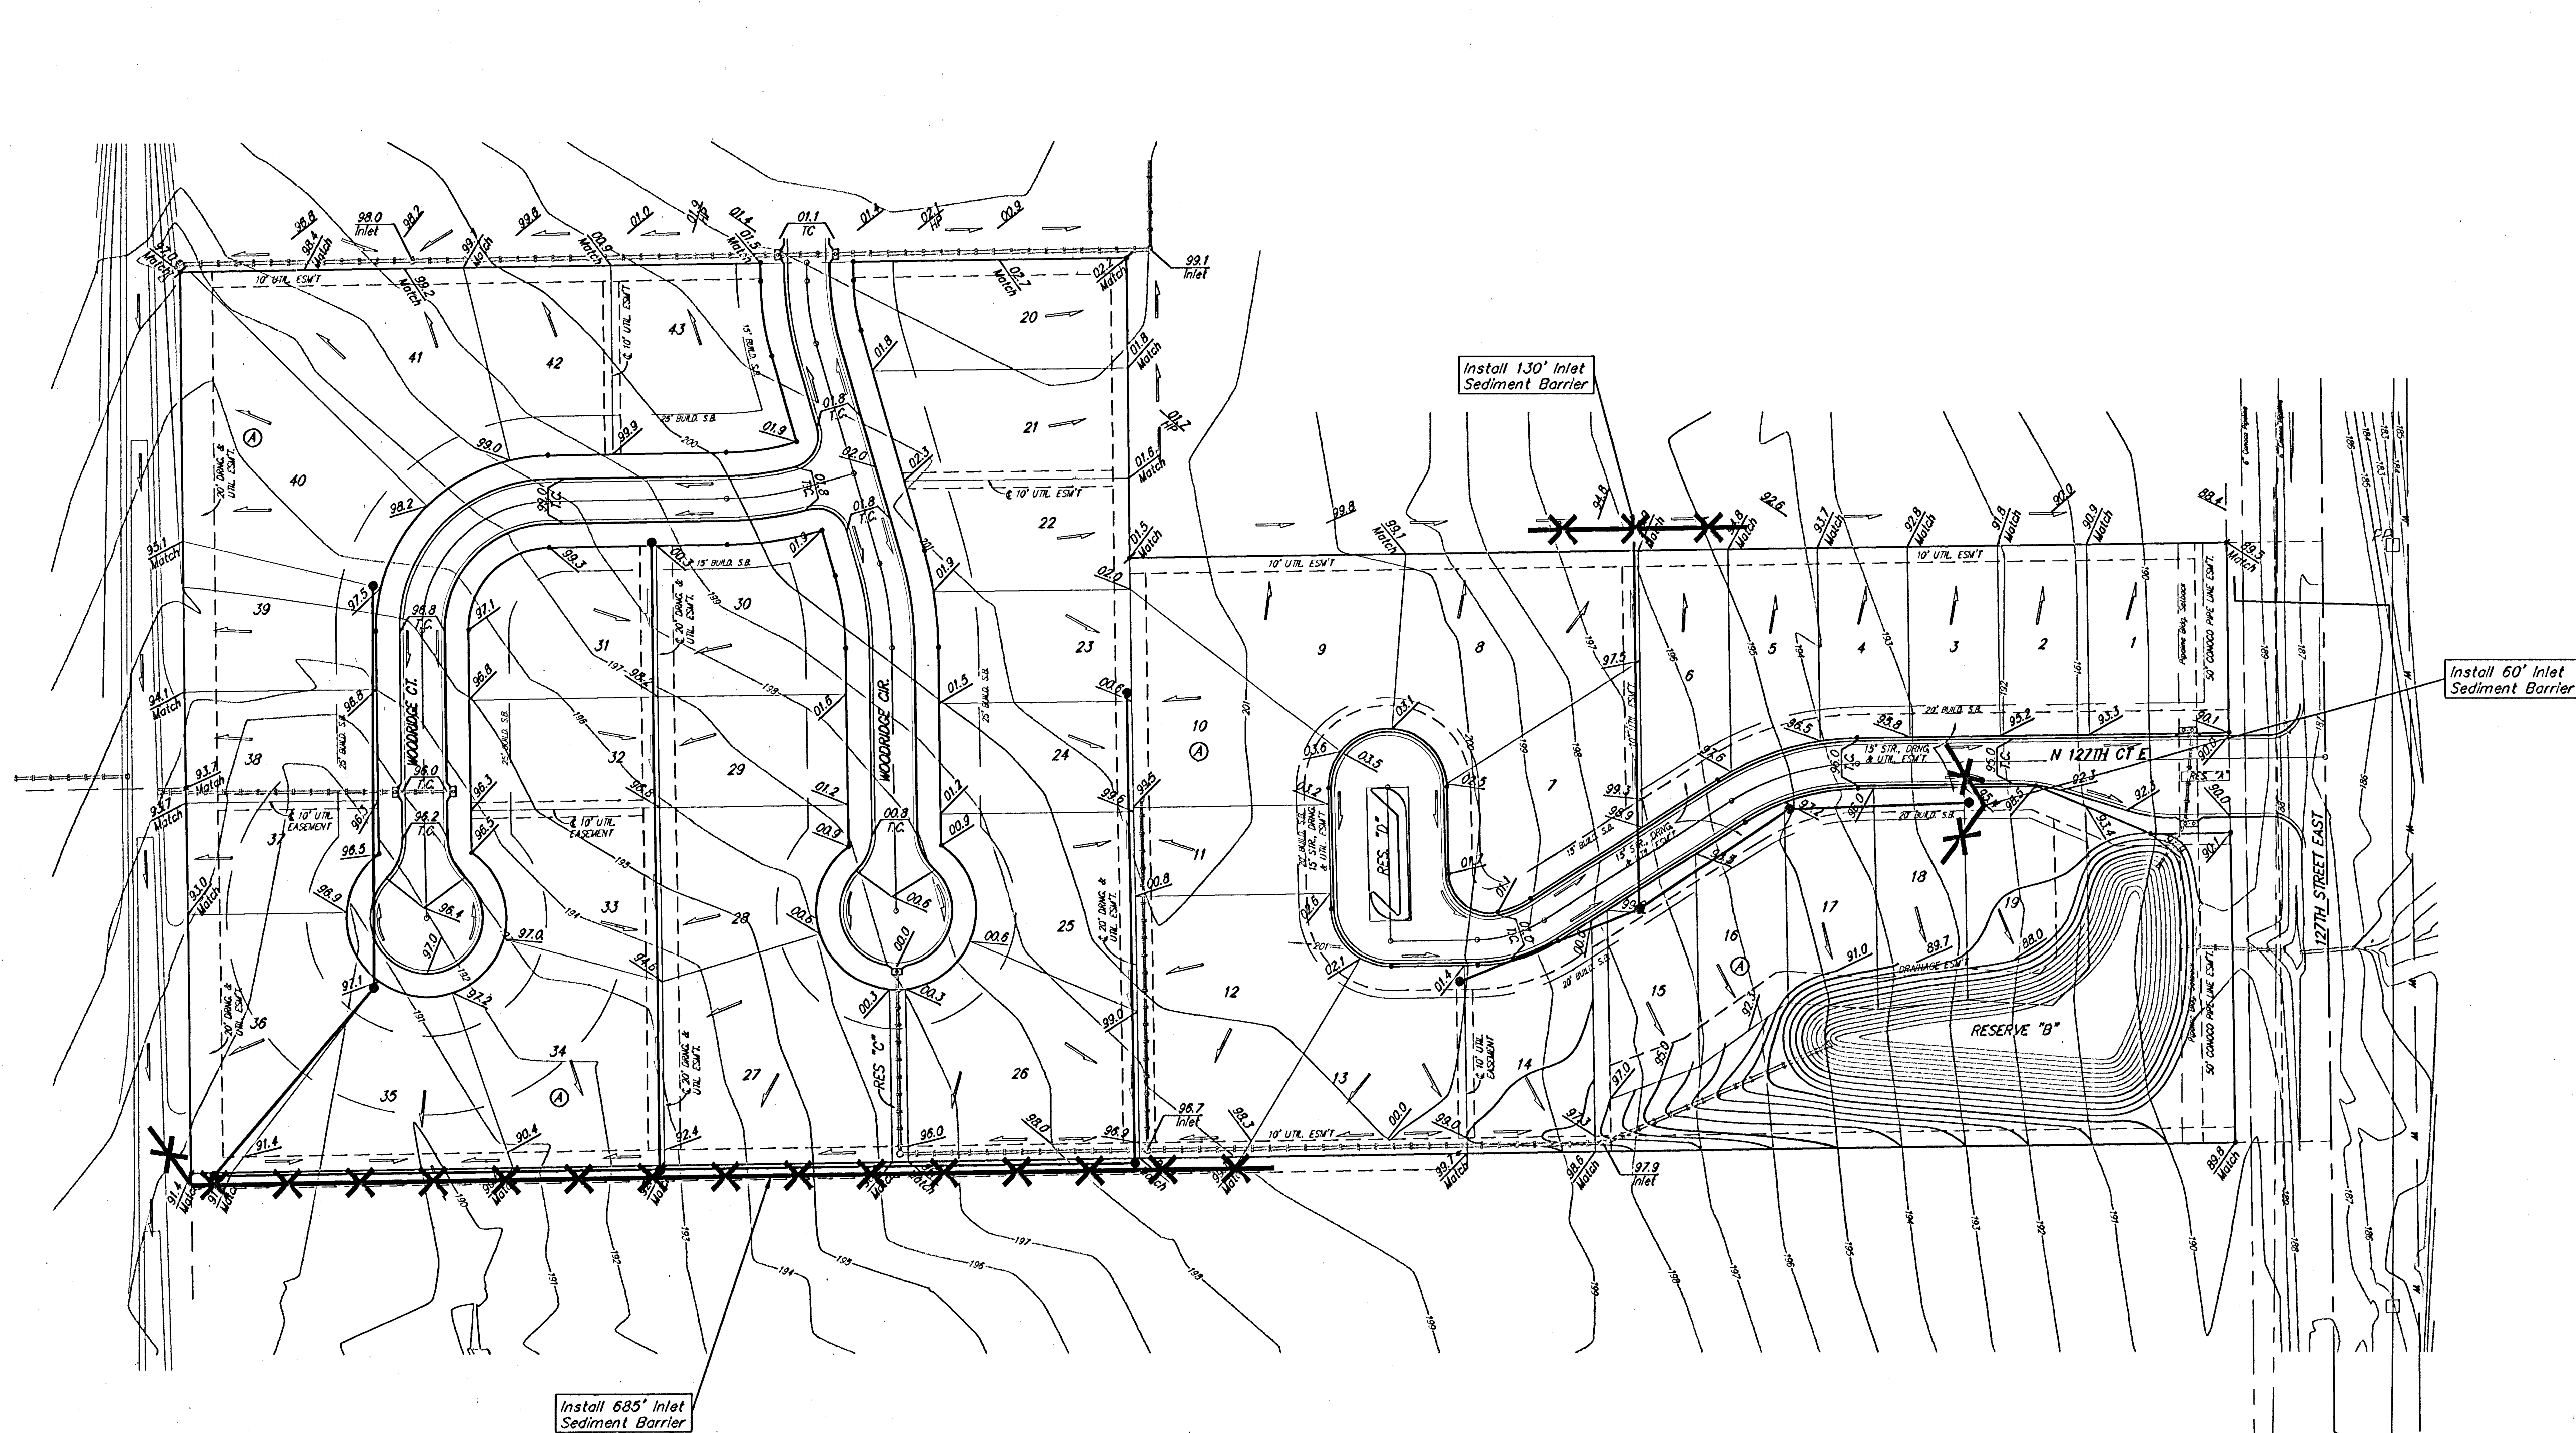

- NOTES:**
1. This Plan is Not To Be Used As A Comprehensive Grading Plan. All Spot Elevations Are Proposed & Subject To Change.
 2. Each Lot Area Disturbed By Construction Shall Be the Responsibility of Each Individual Homeowner. Owner Responsible to Follow All SWPP Plans & Guidelines For The Area.
 3. Erosion Control Matting and/or Other Approved Bank Stabilization w/Seeding & Fertilizer Shall Be Installed at Engineered Channels or Sedimentation Basins Where the Designed Slopes Will be Greater Than 8:1. All Other Disturbed Areas Shall be Seeded, Fertilized, & Mulched As Follows:
SEED --
 150 lbs. per acre of K-31 Fescue.
 200 lbs. per acre of Annual Rye.
 50 lbs. per acre of Bromes
FERTILIZER --
 12-24-12 Ratio - 350 lbs./ac.
MULCH --
 2 Tons of Prairie Hay or Bromegrass Hay per Acre
 "Patted" w/Forks Or Punched into Soil To Reduce Loss Due To Wind.
 4. All Seeding Shall Be Drilled During Spring or Fall Planting Seasons. Fall Seeding Shall Be September 1 thru Mid October. Spring Seeding Shall be From March 15 thru Mid May.
 5. Install Curlex/Excelsior Blanket, or Approved Equal, on Prepared Surface where Soil Has Been Disturbed Due To Construction of Drive Entrances Joining into the Exist. Arterial Street.

EROSION CONTROL PLAN
LEGEND
(Disturbance Outlets Found in the SWPP Plan)

- LIGHT STONE RIP-RAP

- DROP INLET PROTECTION

- CURB INLET PROTECTION

- STRAW BALE BARRIERS

- SILT FENCING

- EARTH DIKES

NO SCALE

EROSION CONTROL MEASURE	UNITS	QUANTITY
SILT FENCE	L.F.	875
RIPRAP	S.Y.	0
DROP INLET BARRIER	EA.	0
CURB INLET BARRIER	EA.	0
STRAW BALE DITCH CHECK	EA.	0
EARTHEN DIKES	L.F.	0
CURLEX	S.Y.	0
POND E.C. BLANKET	S.Y.	0
Construction Entrance	EA.	1

QUANTITIES ARE FOR INFORMATION ONLY!
 CONTRACTOR SHALL VERIFY QUANTITIES PER
 SPECIFIC ENGINEERING PLAN SHEET.

Baughman THE FAIRMONT 3RD ADDITION
Erosion Control PLAN

Baughman Company, P.A. 315 S. 1st St., Waukegan, IL 60087-1011 F316382311 F316382312
 ENGINEERING | SURVEYING | PLANNING | LANDSCAPE ARCHITECTURE

PROJECT NUMBER 468-83935	DESIGN Staff	DRAWN Staff
REVISIONS:	APPROVED	DATE DEC 2004
SCALE NOTED		SHEET 11 OF 16

F:\HYDRO\PREGRADEDWG
