



STATE	PROJECT NO.	YEAR	SHEET NO.	TOTAL SHEETS
KANSAS	54-87 K-6657-01	2002	823	1122


DATE	
BY	
REFERENCES NOTED	
REFERENCES CHECKED	

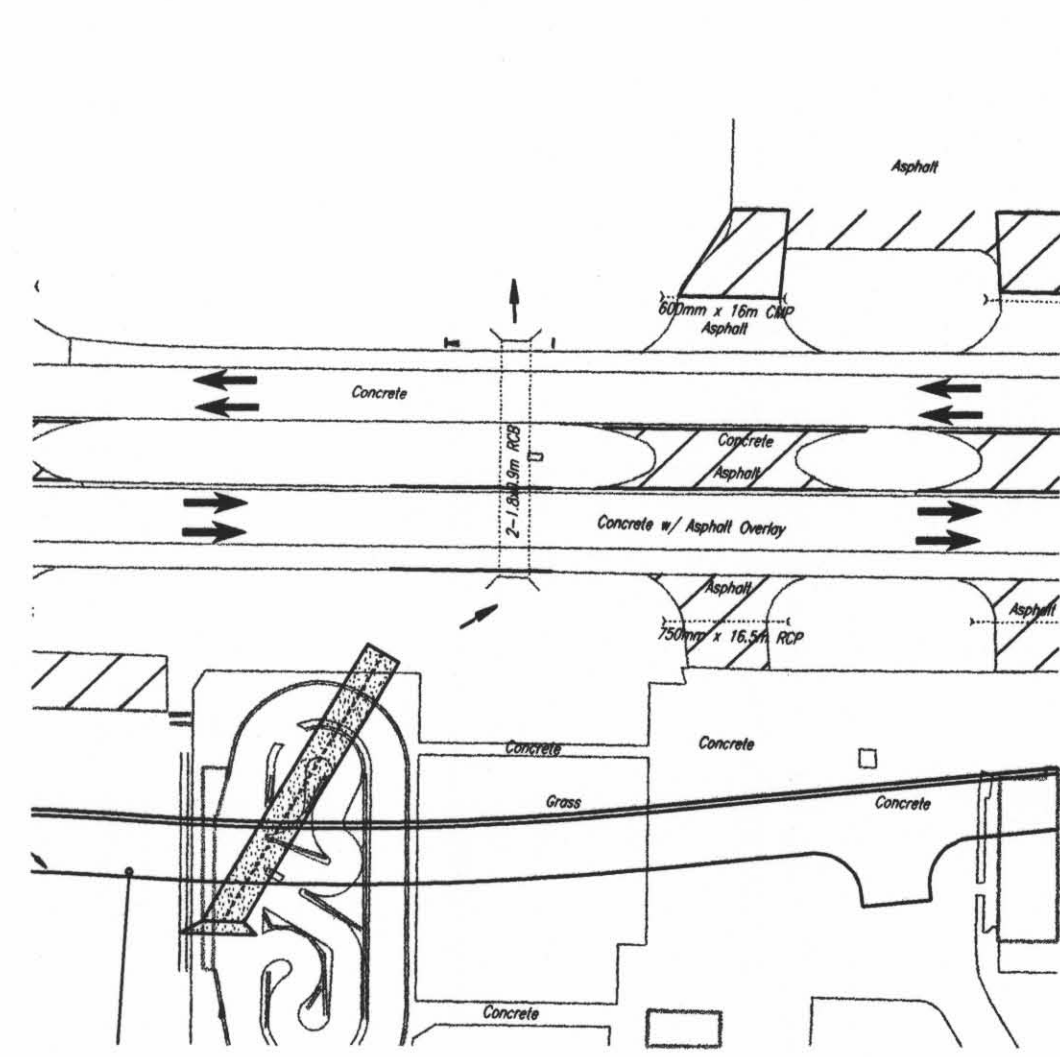


STA. 14+443
STAGE 1A
①

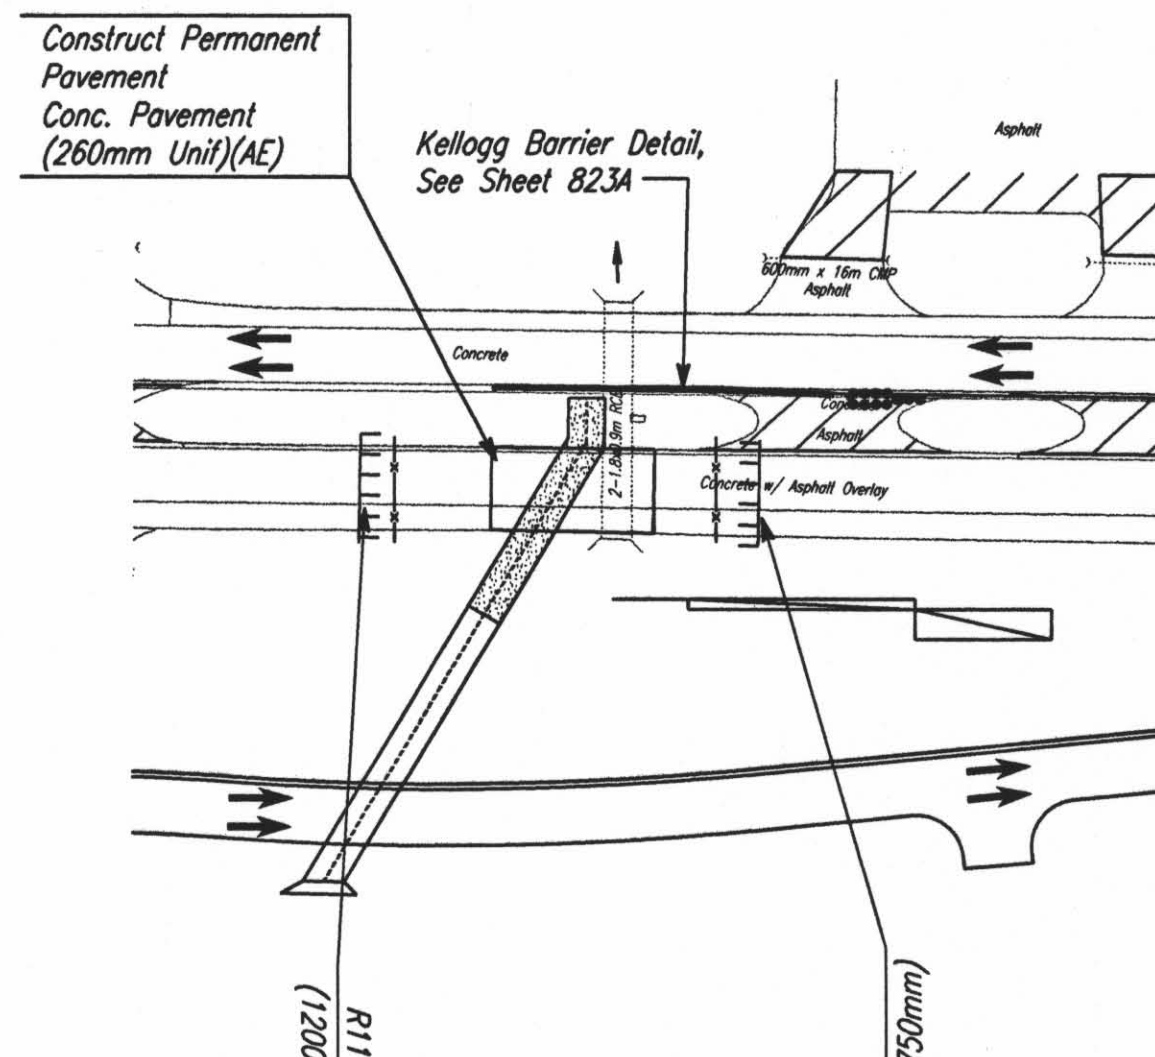


STA. 14+443
STAGE 3A
②

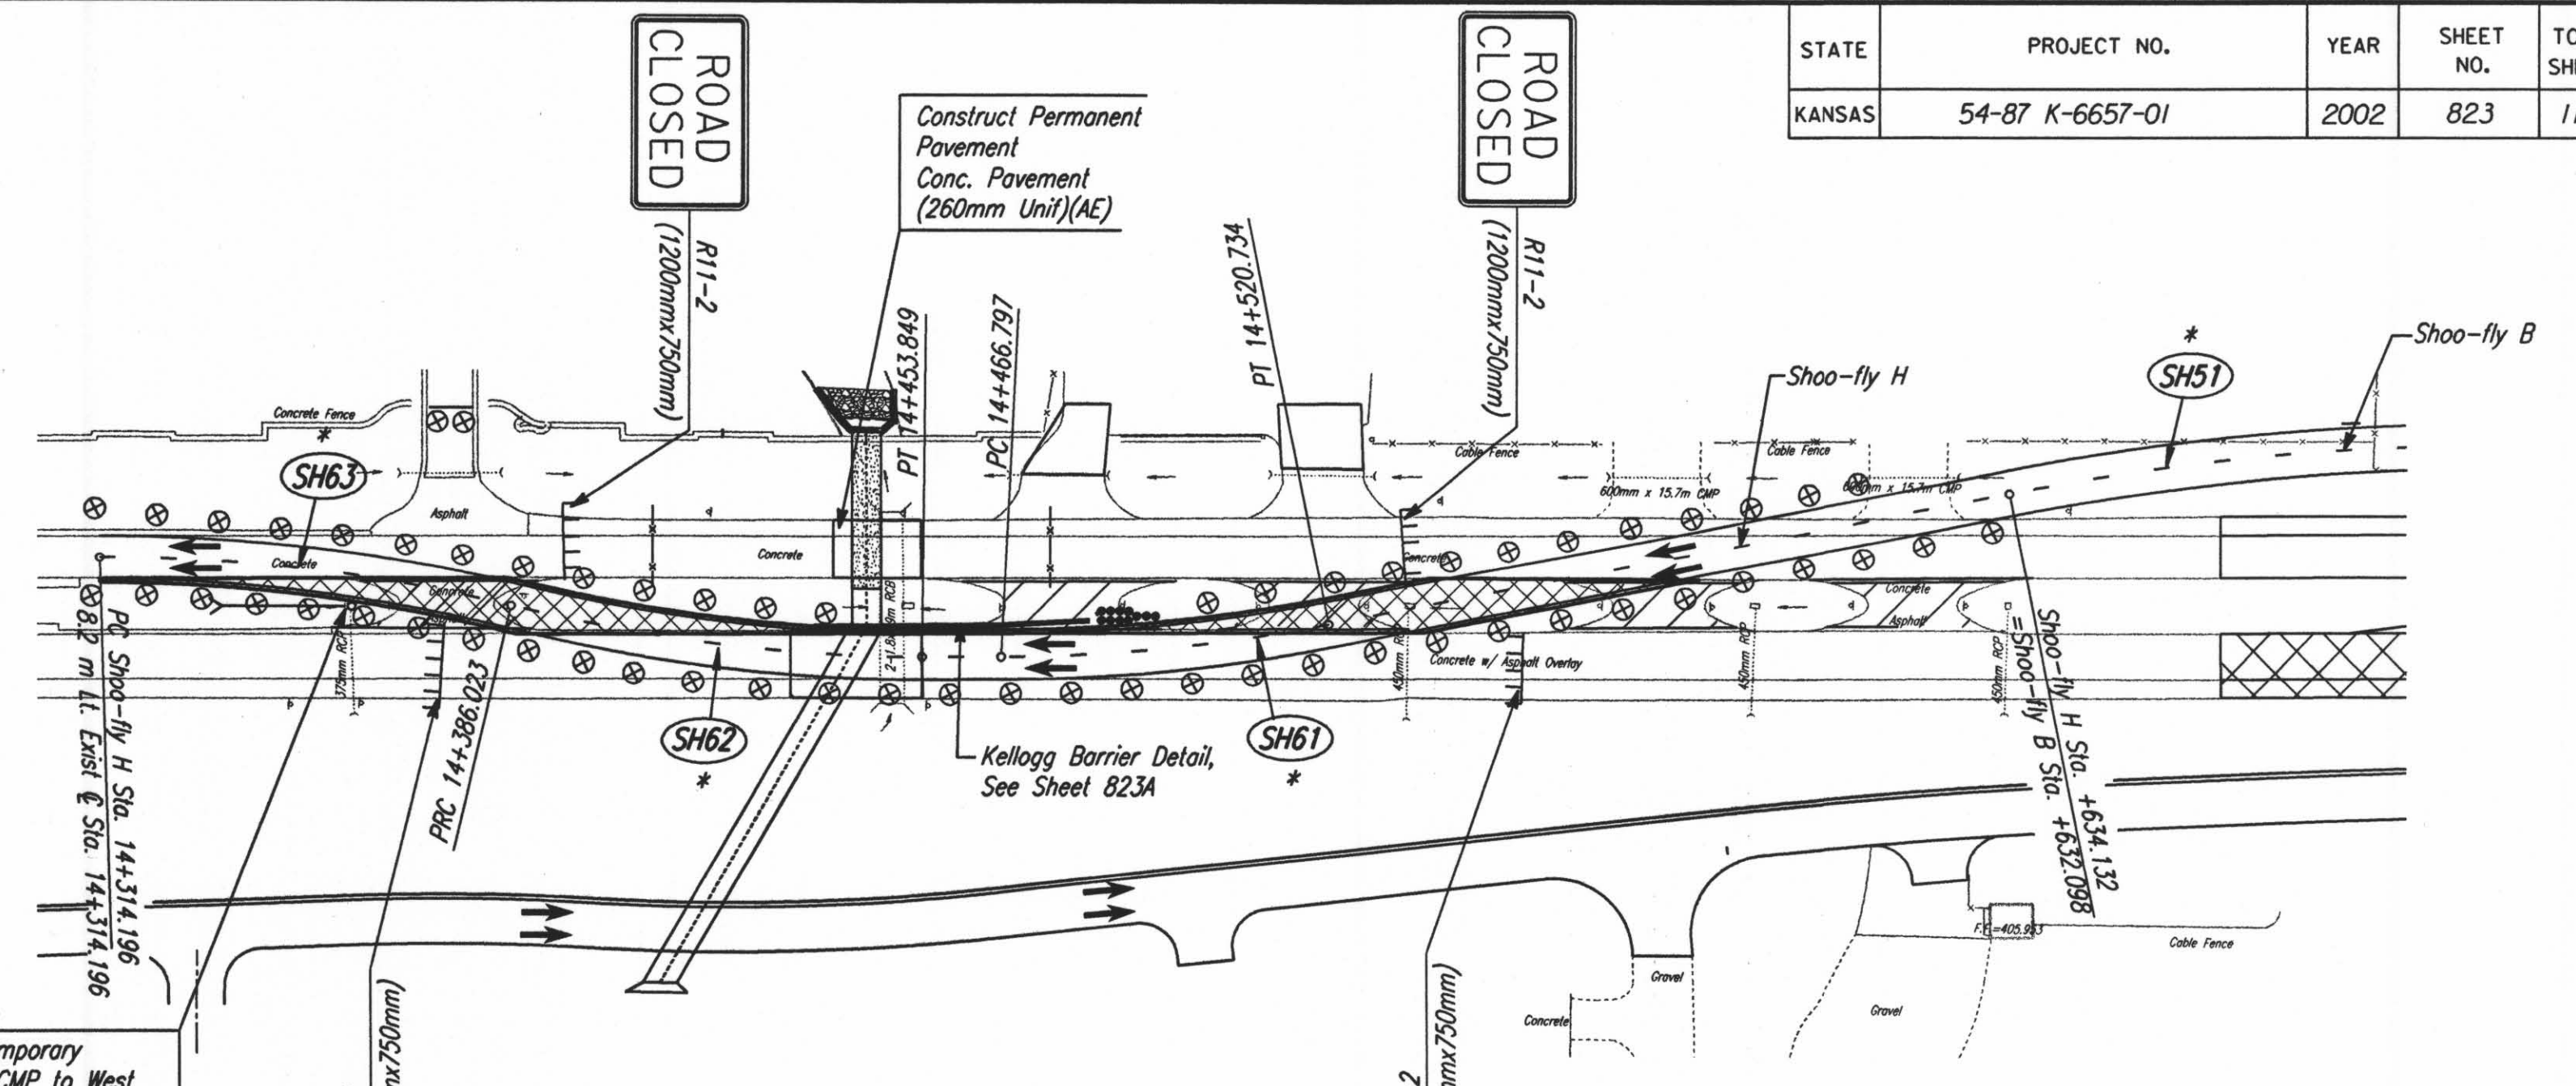


STA. 14+443
STAGE 3A
③

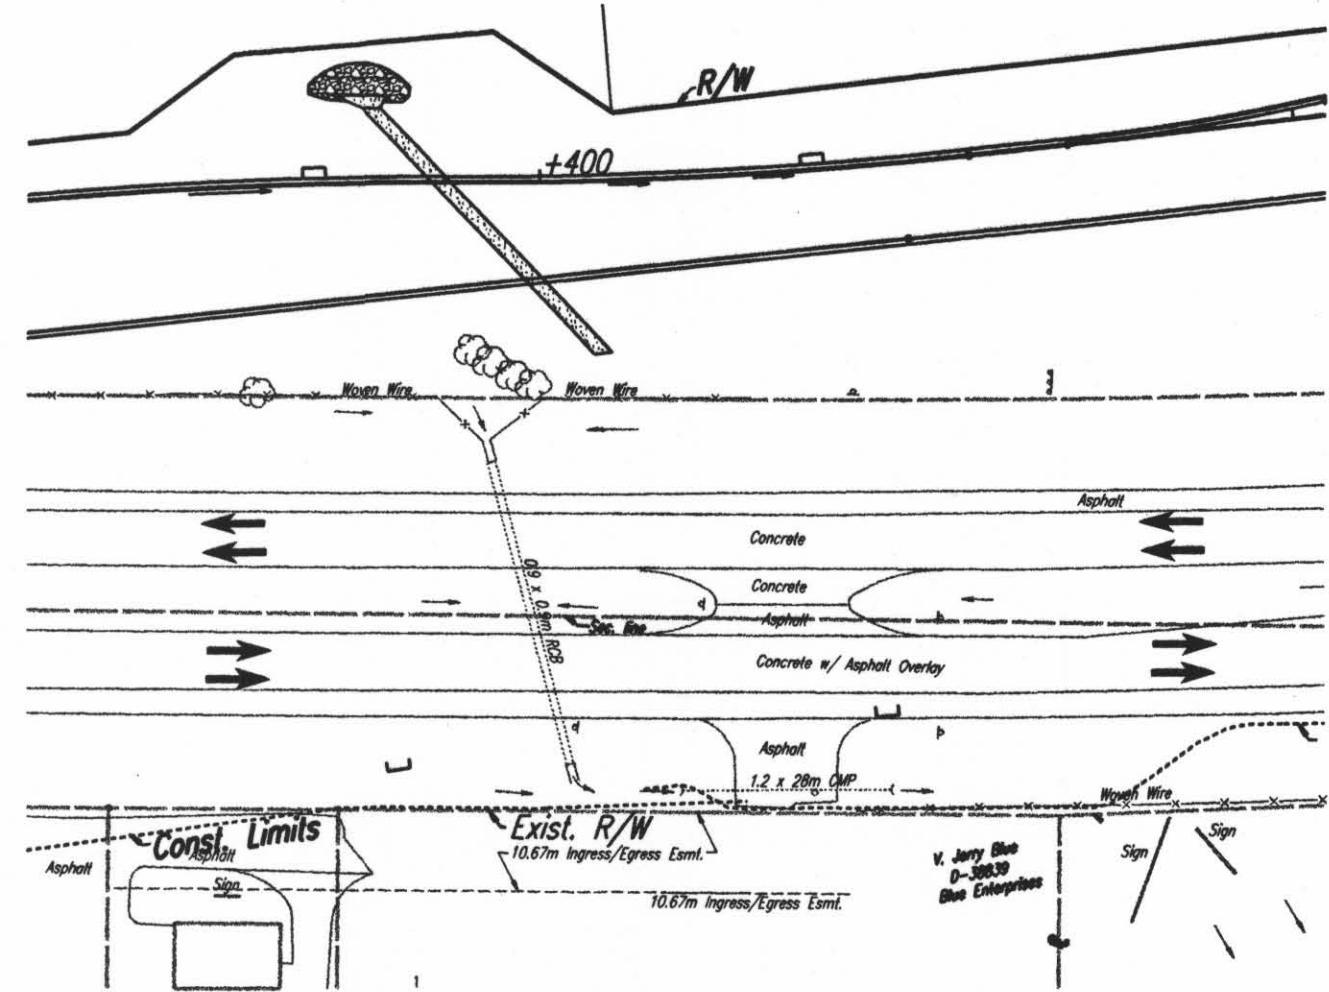

STA. 15+407
STAGE 1A
④

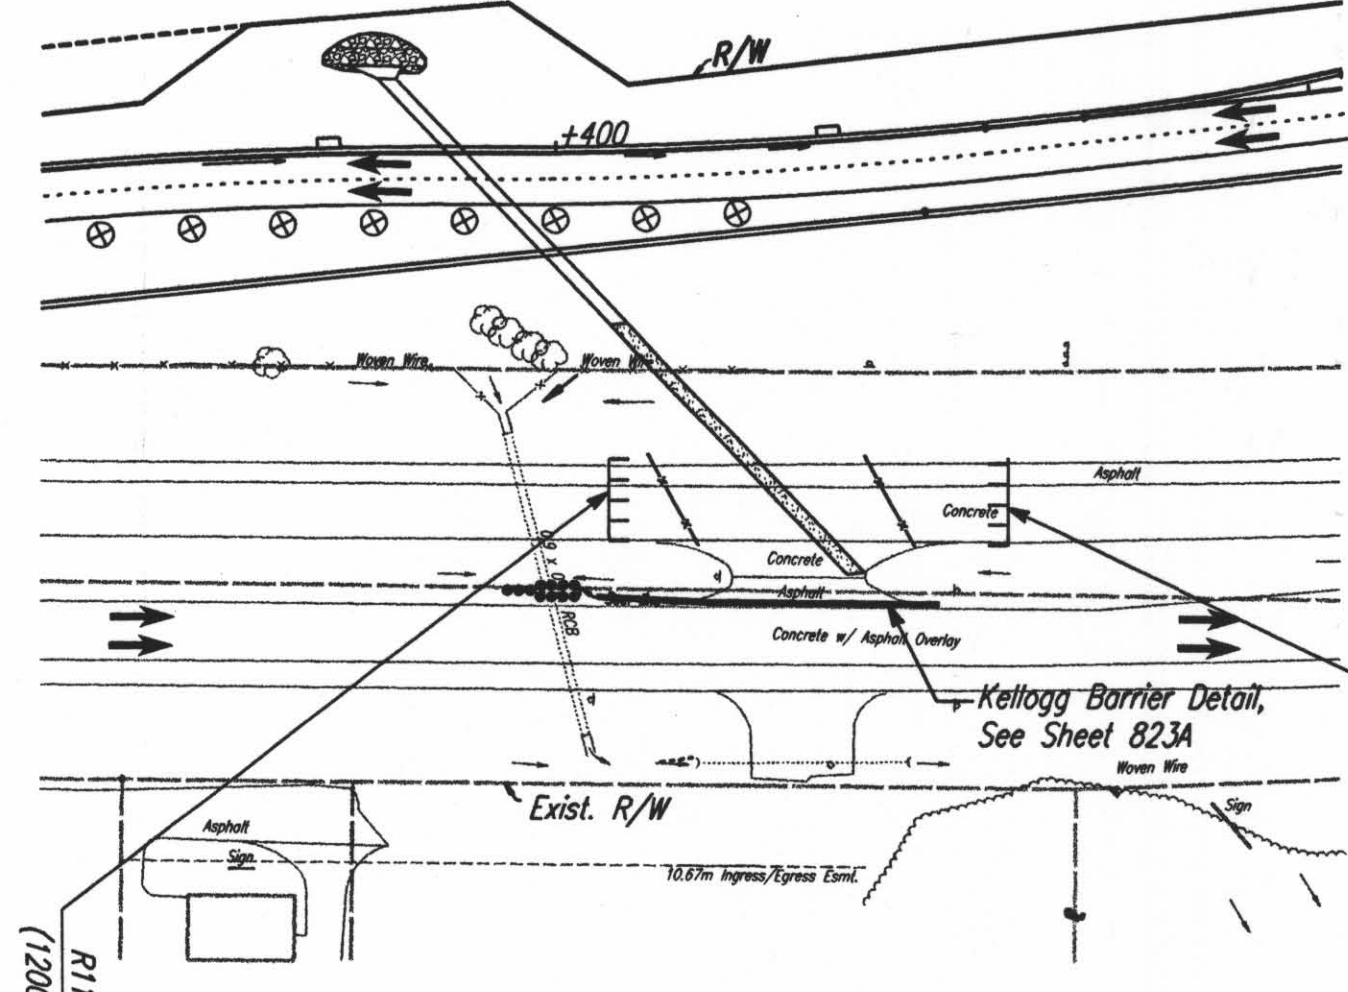

STA. 15+407
STAGE 2A
⑤

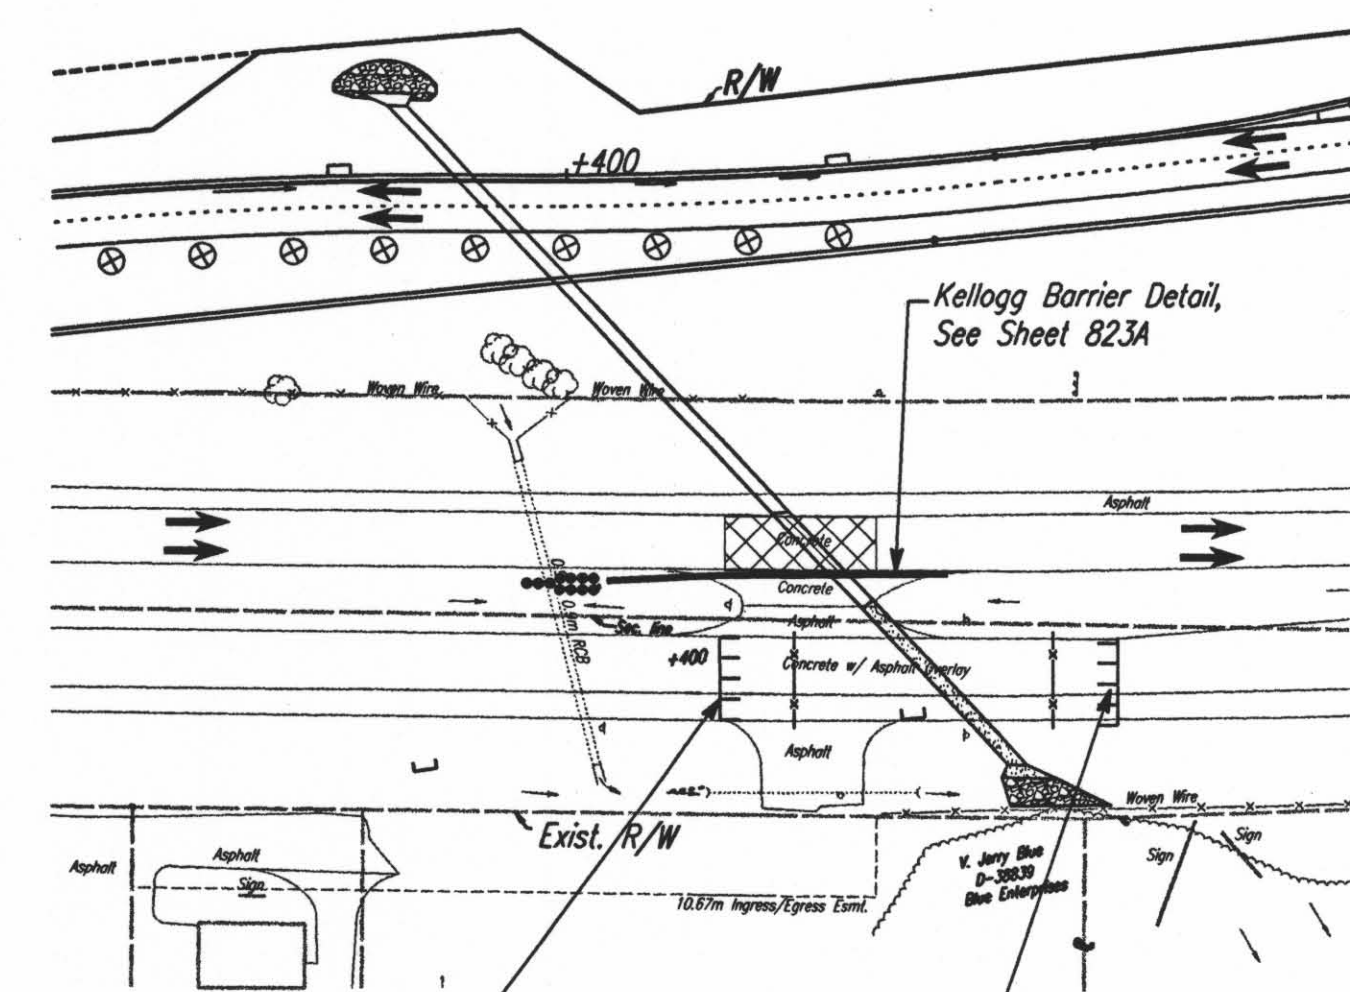

STA. 15+407
STAGE 2A
⑥

@ Frontage Rd. Lt.

- ① Construct RCB under Frontage Road Right. Construct Channel Right. Existing traffic flow on Kellogg.
- ② East Bound traffic on Frontage Road Right. West Bound traffic on existing West Bound Kellogg. Construct RCB under existing East Bound Kellogg.
- ③ East Bound traffic on Frontage Road Right. West Bound traffic on Frontage Road Left and Shoo-fly H. Construct RCB under existing West Bound lanes. Temporarily close South entrance to Resthaven.
- ④ Existing traffic flow on Kellogg. Construct RCB under Frontage Road Left.
- ⑤ West Bound traffic on Frontage Road Left. East Bound traffic on existing East Bound Kellogg. Construct RCB under existing West Bound Kellogg.
- ⑥ West Bound traffic on Frontage Road Left. East Bound traffic on existing West Bound Kellogg. Construct RCB under existing East Bound Kellogg.

Note:
Existing median inlets in conflict with Shoo-fly construction shall be protected with a steel plate. Steel plates shall be removed after eradication of Shoo-fly and regrade ditch to drain.

* See Sheet 795 for Curve Data

LEGEND

	Orange Construction Fence
	Temporary Pavement
	Work Area
	Reflectorized Drums @ 12m spacing
	Type III Barricade
	Traffic Lane

No.	Revisions	By	Date
CITY OF WICHITA RCB CONSTRUCTION SEQUENCE & TRAFFIC CONTROL SEDGWICK COUNTY			
 Professional Engineering Consultants, P.A. 303 S. TOPEKA • WICHITA, KANSAS 67202 316-262-2691 • FAX 316-262-3003			
Designed by	RWM	Checked by	WDH
Drawn by	JSB	Date	Apr-11, 2002
		Job No.	97362

DSNR: RWM OPER: JGP SCALE: 1:1000
 I:/1997/97362/SEQUENCE/RCBS.DGN 4-11-2002 15:17:15 LAST REV: BY:
