

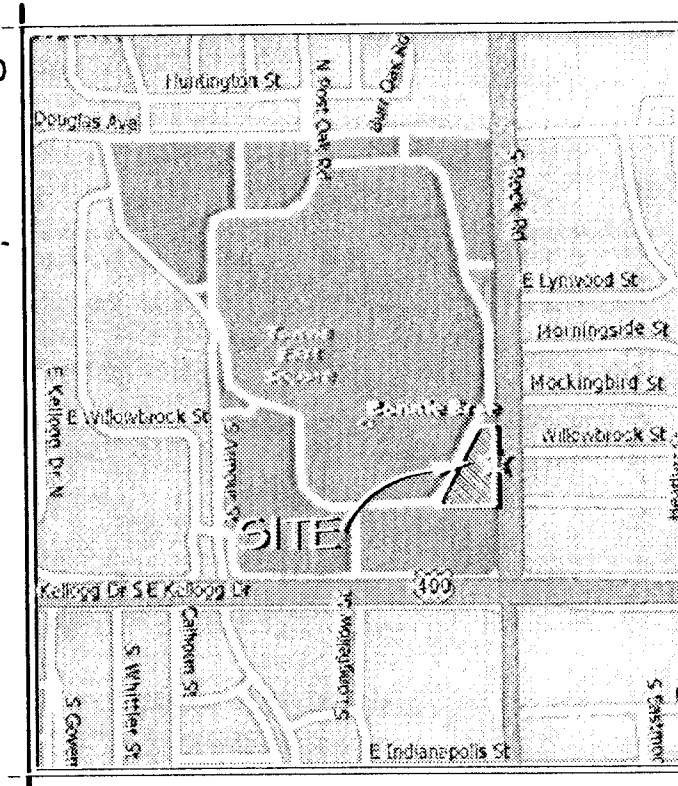



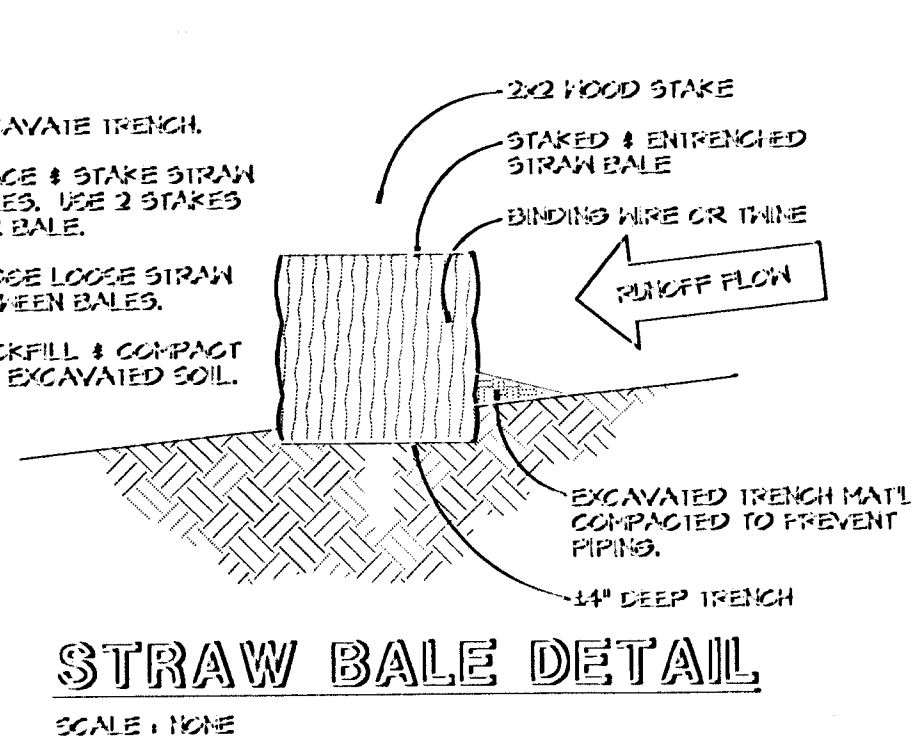

DESIGN and ENGINEERING

DANDELIN ARCHITECTS
STRUCTURAL AND CIVIL ENGINEERS
5105 Maryland Way Suite 200
Brentwood, Tennessee 37027
615-370-1779 fax: 370-9138
www.dandelinc.us

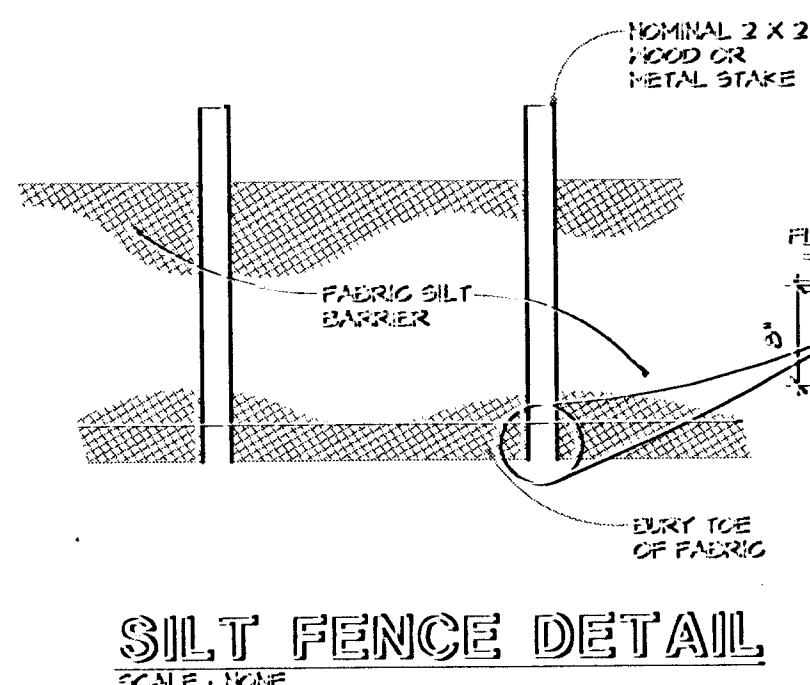

3001 Armory Dr., Suite 300
Nashville, Tennessee 37204
Phone: (615) 885-4056

Opportunity

Location
ROCK ROAD
NIGHTA, KANAWA
(EAST)

Job Number
40-0429/JDG

Revisions

- 1/22/03 FER CITY OF NECHITA SUBMITTED 1/14/03
- 2/05/03 FER CITY OF NECHITA PUBLIC WORKS.
- 2/24/03 ADD EROSION CONTROL
- 03/30/01 FER DEVELOPER AND CPT ROCK ROAD PLANS
- 6/14/01 FER FEH AND FPS

4/4

EROSION CONTROL PLAN
October 30, 2003
PROJECT #121

NOTES

1. OTHER: LOANVILLE ROADHOUSE, INC.
3011 ASHCROFT DRIVE
NASHVILLE, TENNESSEE 37204
TELEPHONE: (615) 252-1420
2. BOUNDARY INFORMATION TAKEN FROM TOPOGRAPHIC SURVEY BY:
BAUGHMAN COMPANY, P.A. (312) 282-7011
313 ELLIS ST. NIGHTLA, KS 61211
DATED: JULY 11, 2008
3. TOTAL AREA OF SITE: 1.08 ACRES
4. PARKING SUMMARY:
18 PARKING SPACES FOR CARS
5 HANDICAPPED PARKING SPACES

121 TOTAL PARKING SPACES
5. BUILDING: 1250 SQUARE FEET
6. THE CONTRACTOR SHALL BID AND PERFORM THE WORK IN ACCORDANCE WITH ALL LOCAL, STATE AND NATIONAL CODES AND THE REQUIREMENTS OF THE LOCAL UTILITY COMPANIES.
7. PERSONS USING THIS DRAWING SHOULD CONTACT LOCAL UTILITY COMPANIES FOR EXACT LOCATIONS OF UNDERGROUND UTILITIES.
8. ALL DIMENSIONS ARE TO FACE OF CURB, UNLESS OTHERWISE NOTED.
9. UNLESS NOTED OTHERWISE, CURB RADIUS 30'.
10. DO NOT SCALE THIS DRAWING AS IT IS A REPRODUCTION AND SUBJECT TO DISTORTION.

SEQUENCE OF CONSTRUCTION

THE GENERAL FORMAT FOR EARTHMOVING ACTIVITIES SHALL BE AS FOLLOWS:

- A. INSTALLATION OF FILTER FABRIC FENCE AND CONSTRUCTION EXIT.
- B. DEMO OF BUILDING AND PAVING AND REMOVAL OF TREES.
- C. EXCAVATION OF SOIL FROM EXISTING DRIVEWAY. CONTRACTOR TO LOCATE SUITABLE AREA FOR SOIL STORAGE AND WILL APPLY TEMPORARY SEED WITHIN 5 DAYS. FILTER FABRIC FENCE WILL BE USED AS REQUIRED AROUND STOCKPILE.
- D. GRASS GRADING AND STABILIZATION OF PARKING AREAS, GENERAL SITE GRADING AS DEMONED ON THE PLANS.
- E. CONSTRUCTION OF STORM DRAIN SYSTEM AND INLET PROTECTION.
- F. BUILDING CONSTRUCTION, INSTALLATION OF ROOF DRAINS AND OTHER UTILITIES.
- G. FINAL GRADING AND INSTALLATION OF CURB AND GUTTER.
- H. PAVING OF PARKING AREAS AND DRIVES.
- I. REGISTERED PREPARATION OF ROOT STAKES, ROOTS, CABLE WIRE, CABLE STAKES, AND ANY OTHER MATERIAL WHICH MAY HINDER PROPER GROWTH OF PLANT GROWTH. RE-SEEDING TOPSOIL. BREAK UP TOPSOIL TO A DEPTH OF 12" UNTIL THE SOIL IS SUITABLE FOR PLANTING. PERM TO RESEED THE TOPSOIL. IS TO BE RAKED SMOOTH TO PROPER GRADES.
- J. REMOVAL OF REMAINING TEMPORARY CONTROLS

MAINTENANCE

ALL TEMPORARY EROSION AND SEDIMENTATION CONTROLS SHALL BE MAINTAINED THROUGHOUT THE CONSTRUCTION PHASE OF THE PROJECT ACCORDING TO THE FOLLOWING SCHEDULE:

ROCK CONSTRUCTION ENTRANCE
1. THE SIGNIFIES THICKNESS

1. THE STRUCTURE'S THICKNESS WILL BE CONSTANTLY MAINTAINED TO THE SPECIFIED DIMENSION BY ADDING ROCK. A STOCKPILE OF ROCK MATERIAL WILL BE MAINTAINED ON THE SITE FOR THIS PURPOSE.
2. AT THE END OF EACH CONSTRUCTION DAY, ALL SEDIMENT DEPOSITED ON THE ROADWAY WILL BE REMOVED AND RETURNED TO THE CONSTRUCTION SITE.
3. WASHING OF THE ROADWAY WITH WATER IS NOT PERMITTED.

FILTER FABRIC FENCE
LINE FENCE INSTAL

1. THE FENCE INSTALLATION SHALL BE INSPECTED AFTER EVERY PUMP-GENERATING EVENT. ANY NECESSARY REPAIR WILL BE MADE IMMEDIATELY.
2. ACCUMULATED SEDIMENTS WILL BE REMOVED AS REQUIRED TO KEEP THE FENCE FUNCTIONAL. IN ALL CASES, REMOVE SEDIMENTS FROM THE ACCUMULATIONS REACH 1/2 THE ABOVE STATED HEIGHT OF THE FENCE.
3. ALL UNDERCUTTING OR EROSION OF THE SOIL NEAR THE FENCE WILL BE REPAIRED IMMEDIATELY WITH COMPACTED BACKFILL MATERIAL.
4. ADHERE TO ANY MANUFACTURER'S RECOMMENDATIONS FOR REPLACING FILTER FABRIC DUE TO TEARINGS.

IT SHALL BE THE RESPONSIBILITY OF THE CONTRACTOR TO MAINTAIN THE ROOF DRAINS AND THE SEDIMENT STRUCTURES DURING CONSTRUCTION.

ADDITIONAL EROSION AND SEDIMENTATION CONTROLS SHALL BE INSTALLED WHERE NECESSARY OR WHERE DIRECTED BY THE LOCAL SEDIMENTATION AND EROSION CONTROL OFFICE AS CONSTRUCTION PROGRESSES.

DESIGN	00
CONSTRUCTION	10-000
AS-BUILT	10-000

These design documents are the exclusive property of Design and Engineering, P.C. The information shown may not be used on the drawings reproduced without written permission of Design and Engineering, P.C.
