


**BENCHMARKS:**  
 BM #1 Square cut in top of curb adjacent to the SE corner of Lot 2, Block B, The Woods Addition  
 Elev. = 1381.25 NGVD29  
 BM #2 Square cut in top of curb NW end of median, Reserve "F" The Woods Addition  
 Elev. = 1385.54 NGVD29

Static W.S.E. = 1366.5

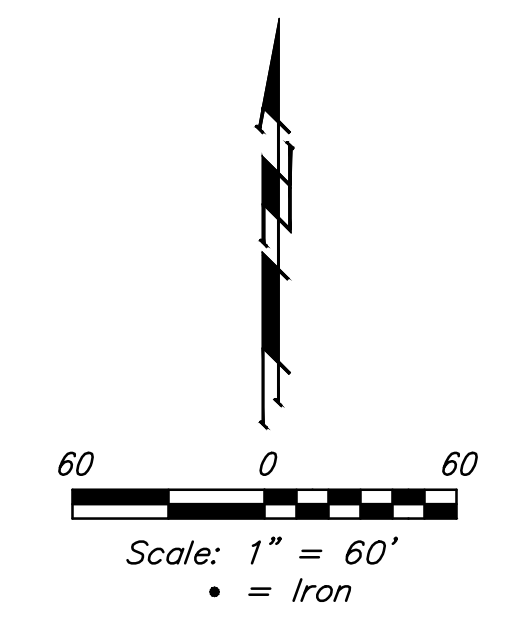

**EROSION CONTROL PLAN LEGEND**

- FENCING
- CUT-OFF TRENCH
- TEMPORARY DITCH

**NOTES:**  
 Contractor shall make sure all erosion control is in place before project is accepted. This plan represents the minimum standard. Any additional erosion control measures shall be installed by the Contractor as needed.

All areas disturbed during construction shall be seeded, mulched, and fertilized as per Cover Sheet General Notes.

EROSION CONTROL MEASURE	MAINTAIN
CUTT-OFF TRENCH (LF)	0
CONSTRUCTION ENTRANCE (EA)	1
CURB INLET BARRIER (EA)	0
DITCH CHECK (EA)	0
DROP INLET PROTECTION (EA)	0
EROSION CONTROL (LS)	0
MULCH WATTLES (LF)	0
ORANGE SAFETY FENCE (LF)	1,553
EROSION CONTROL MAT (SY)	0
MAINTAIN EROSION CONTROL BMP's (LS)	0

\* ALL EXISTING BMPs INCLUDING CONSTRUCTION ENTRANCE, SEDIMENT BARRIERS, SILT FENCE, CUT-OFF TRENCH, AND EROSION CONTROL MAT SHALL BE MAINTAINED AND REPAIRED IF NECESSARY.

**CAUTION!**  
 Vibratory equipment shall not be operated within pipeline right-of-way

Maintain 50'x12' Gravel Construction Entrance.

Maintain 1,165 L.F. 4' Orange Safety Fence

Maintain 388 L.F. 4' Orange Safety Fence

**Baughman** The Woods Addition - Phase III  
**EROSION CONTROL**  
 Water Distribution System

Baughman Company, P.A. 315 Ellis St. Wichita, KS 67211 P 316-262-2271 F 316-262-0149  
 ENGINEERING | SURVEYING | PLANNING | LANDSCAPE ARCHITECTURE

PROJECT NUMBER 448-90165	DESIGN AEG	DRAWN JAK
REVISIONS:	APPROVED	DATE 2/18/16
		SCALE Noted
		SHEET

**5 OF 12**
