




NOTE TO CONTRACTOR:

Contractor Will Notify K.G.E.
(Mr Koester Ed. 335) Before excav.
is started on this project.
Contractor will exercise extreme
caution while excavating over conduit.

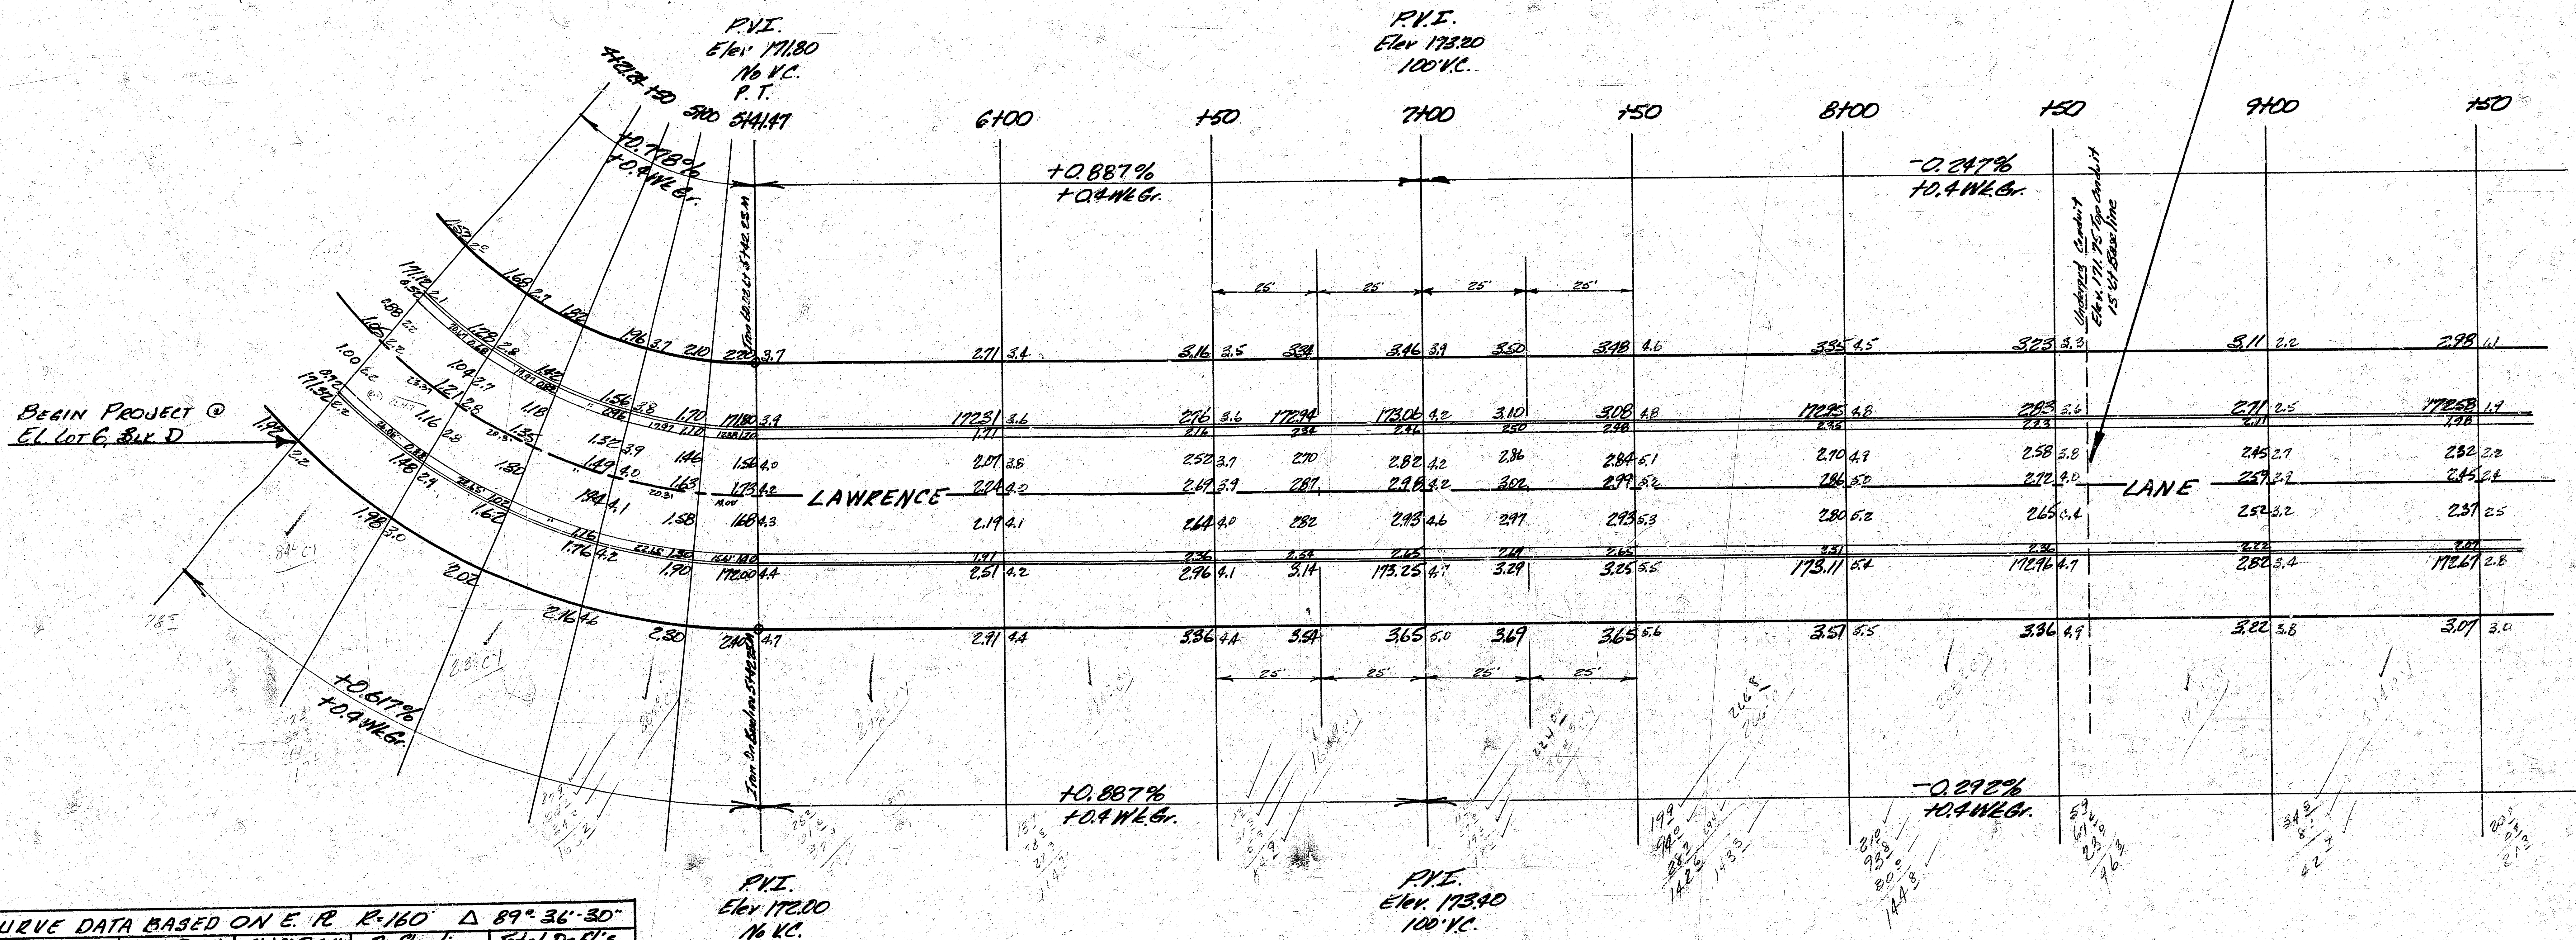

CURVE DATA BASED ON E. R. R. 160' Δ 89° 36' 30"					
Sta	Arc	Chd B @ NCb	Chd B @ SCb	Deflection	Total Defl's
PC 2192					
4+21.24	129.24	120.26'	84.10'	23° 08' 27"	23° 08' 27"
+50	28.76	37.46'	17.21'	5° 08' 57"	28° 17' 24"
+75	25.0	23.88'	16.70'	4° 28' 35"	32° 45' 39"
5+00	"	"	"	"	37° 14' 34"
+25	25.0	23.88'	16.70'	4° 28' 35"	41° 43' 09"
PT 5742.25	17.25	16.47'	11.52'	3° 05' 06"	44° 48' 15"

10.7430 Min. / Ff.

Excavation
Prop.
2127 ³/₄
2225.9 * C.Y.
222.6 + 10%
2448.5 C.Y. Total
* Includes 100 C.Y. Ditch Excav.

Comp. Fill
Prop
462³
450.2 CY.
45.0 + 10%
495.2 C.Y. Total

LAWRENCE LANE
FL. LOT 6, Bk D, 3RD. ADDN. WOODLAWN VILLAGE
TO N. LOT 4, Bk D, 3RD ADDN. WOODLAWN VILLAGE

26' - 2' - 30' A.C.

CITY OF WICHITA, KANSAS
B. E. SMITH CITY ENGINEER
DATE MAR. 1966 PROJ. C13-8

14-Eng
1-Wh.

