


B.M. 158.76 "R" in R.C. Co. Inc. top. ab. N. end of
W. curb on Maus 30' S. of 12th St.

NOTE:

Contractor to grade parkings and compact fill
for proposed sidewalk. Sidewalk to be const. by others.

NOTE:

Excavated material to be used on
Maus Lane, Project C18-49
All the excavated material will be
needed on project C18-49

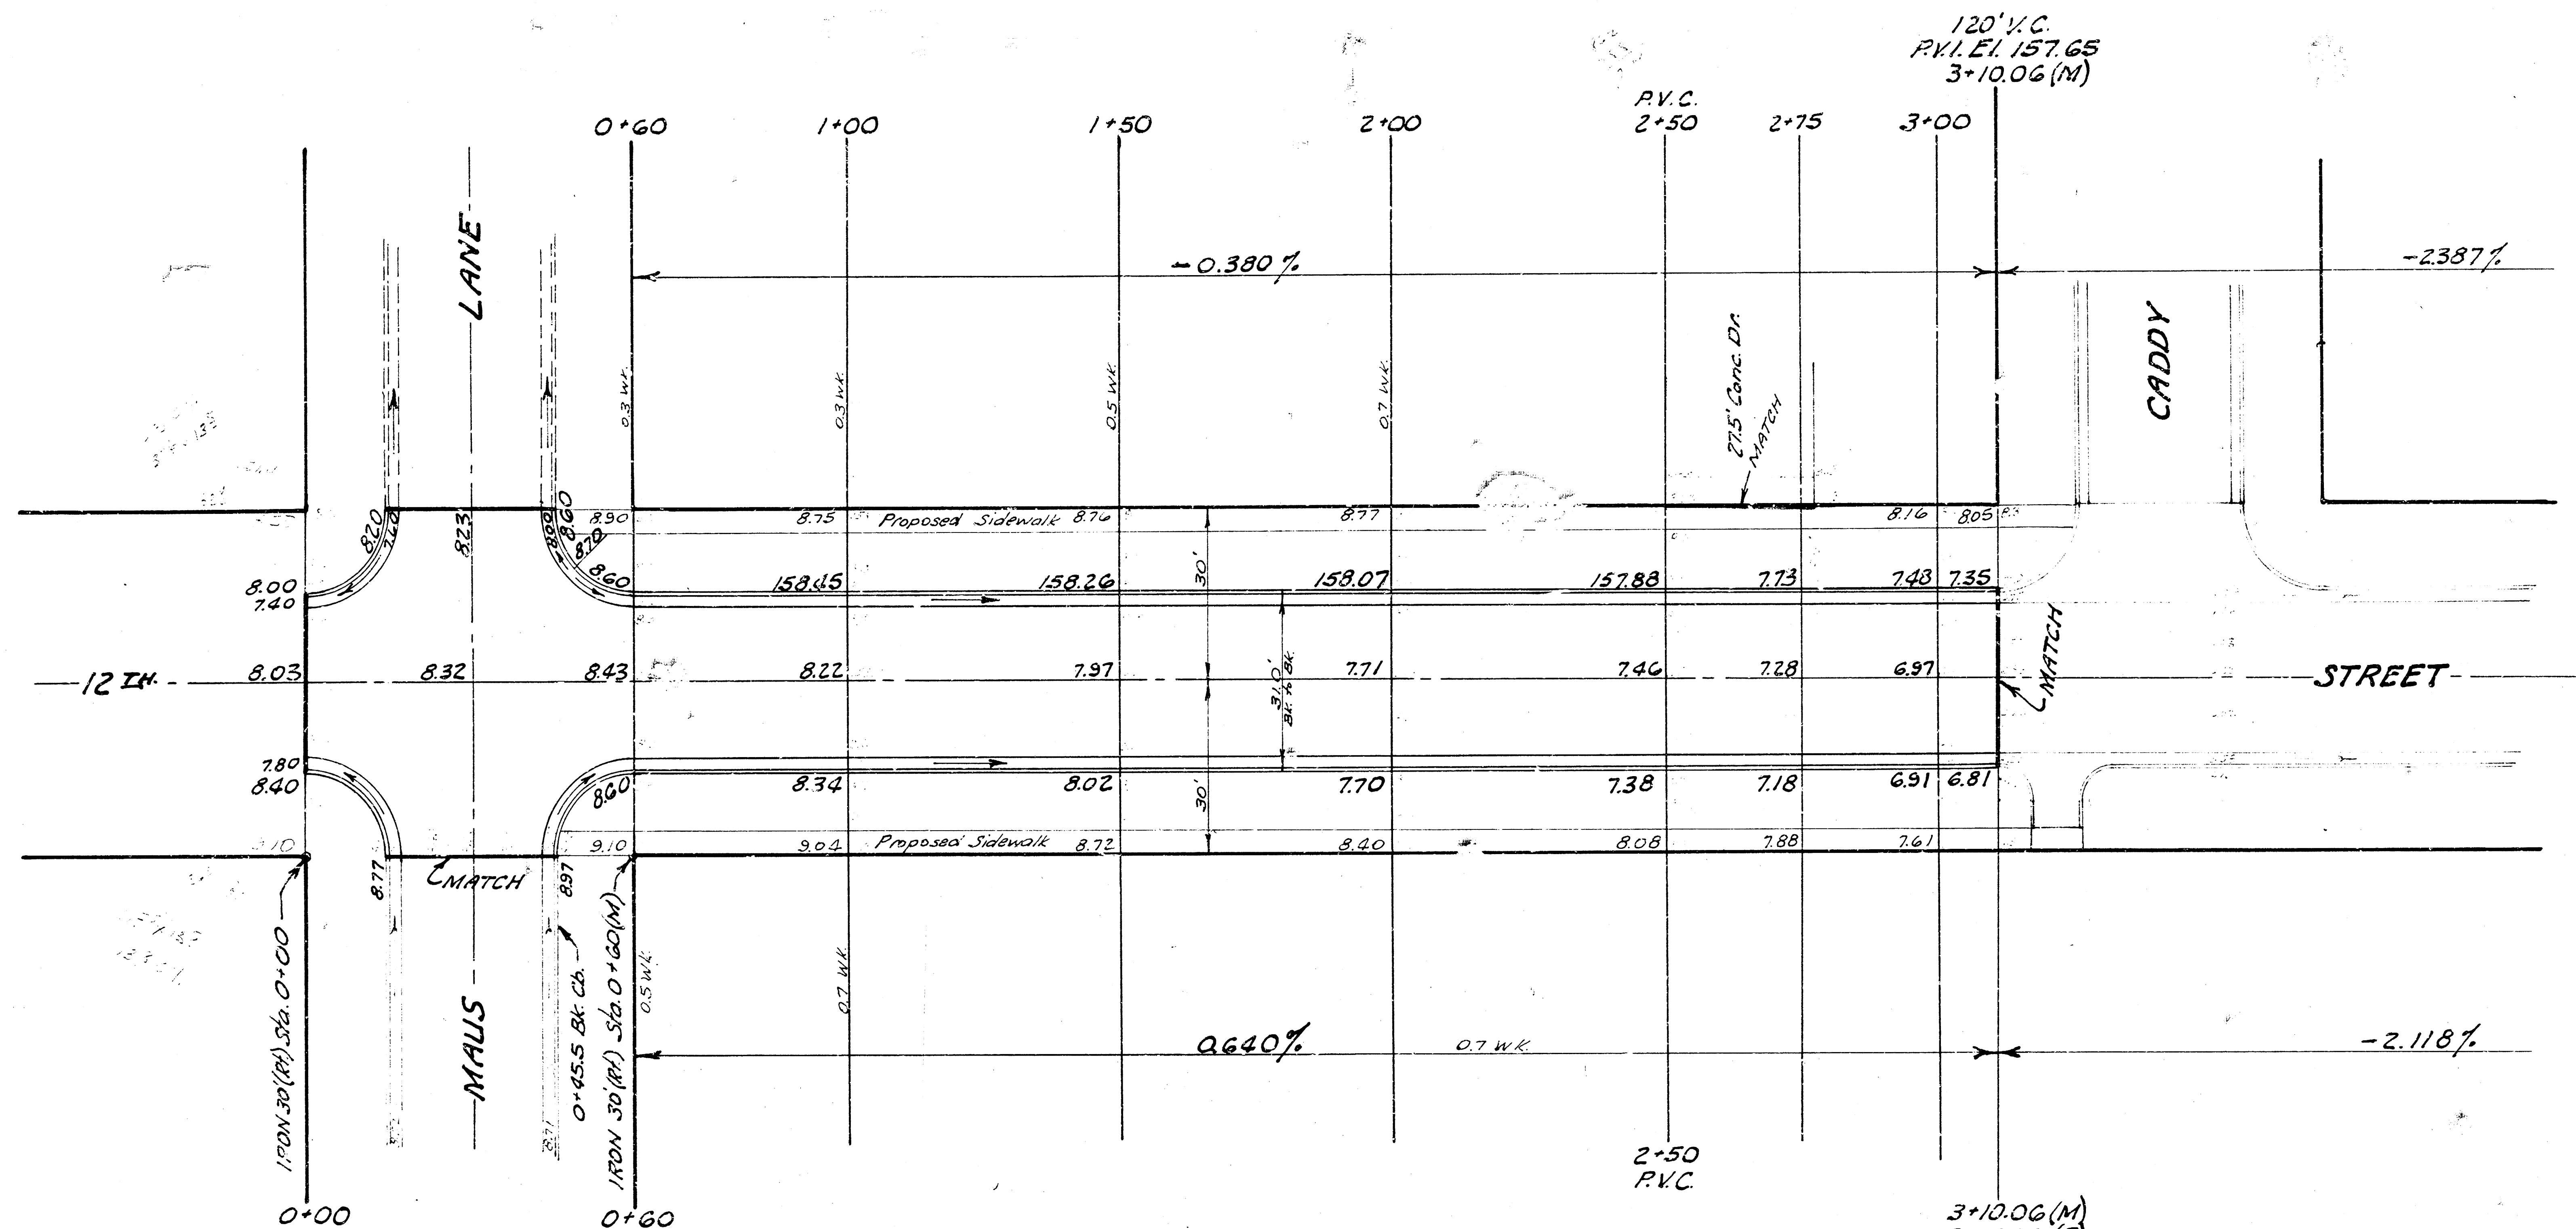

PROPERTY EXC.	
+10 %	573 Cu. Yds.
Totals	630 Cu. Yds.

PROPERTY COMP. FILL
160 Cu. Yds. Sub-Grade Modification

CITY EXC.	
	119 Cu. Yds.
	12 " "
Totals	131 Cu. Yds.

CITY COMP. FILL
60 Cu. Yds. Sub-Grade Modification

12TH STREET
W.L. MAUS LANE to W.L. LOT 4
BLK. 9 WESTLINK VILLAGE 8TH
26-2-30 A.C.
B.E. SMITH CITY ENGINEER
CITY OF WICHITA KANSAS
Date: Sept. 1970
Project No. C18-47

1/2
