

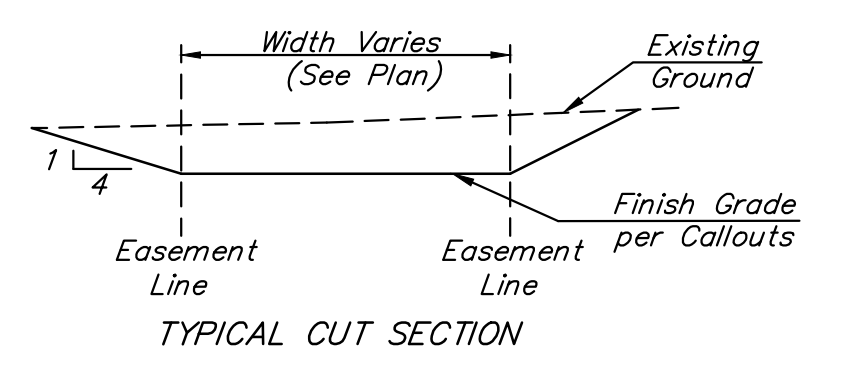
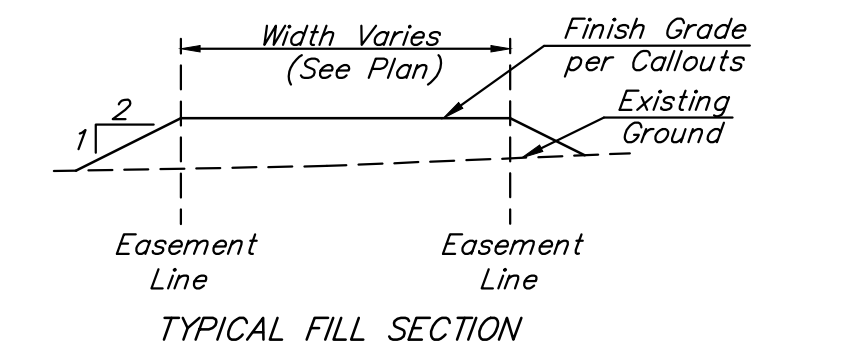


**EROSION CONTROL PLAN LEGEND**

- DROP INLET PROTECTION
- DITCH CHECKS
- SILT FENCING
- EROSION CONTROL MAT

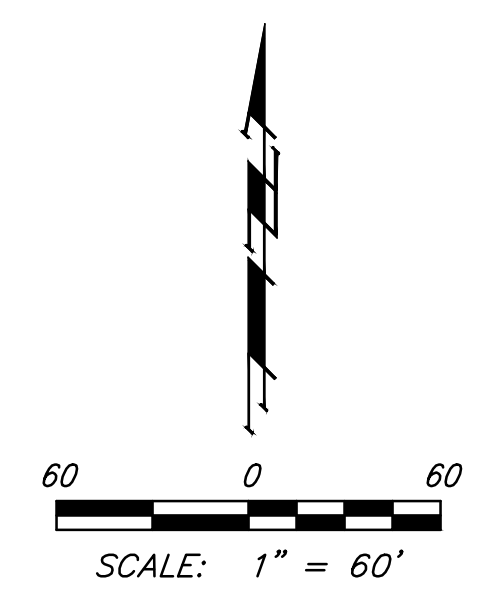

**SECTION A-A**

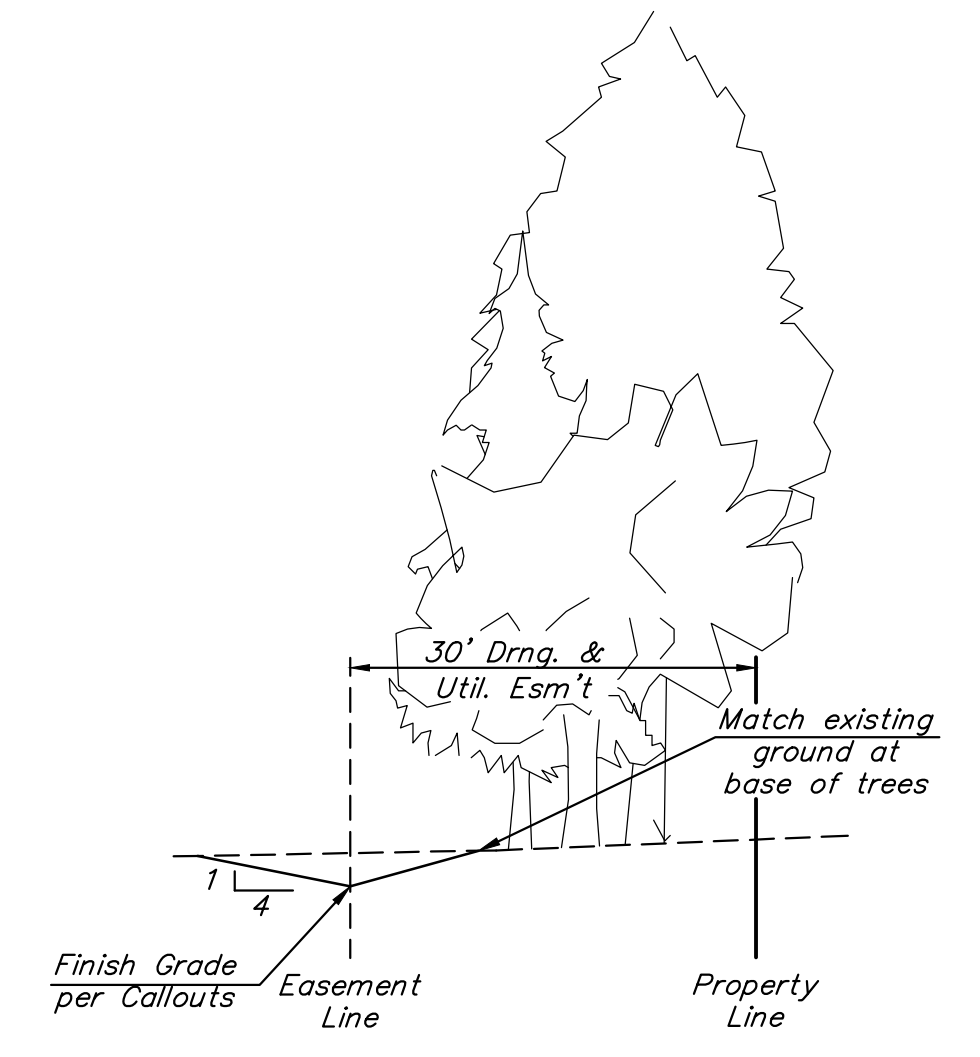

**SECTION B-B**

Existing Grade  
 = Easements To Be Graded

Approximate Easement Grading Quantities:  
 (For Information Only)

Excavation: 254 C.Y.  
 Fill: 14 C.Y.

The Contractor shall grade the easements as shown to the elevations given on the Easement Grading Plan. All costs for grading shall be incidental to the Easement Grading Bid Item. The Contractor shall 'straight' grade the easements between the elevations given. Where a callout designates 'Match', the Contractor will grade to the existing ground elevation.

Maintain 50'x12' Gravel Construction Entrance.

Install 504 L.F. Silt Fence Sediment Barrier.

Install Back of Curb Protection.

Install Curb Inlet Sediment Barriers.

Static WS Elev = 158.0 City Datum  
 100-yr Design WS Elev. = 160.7 City Datum

Match grading at edge of existing walk.  
 Contractor to ensure positive grade to pond.

Static WS Elev = 158.0 City Datum  
 100-yr Design WS Elev. = 160.7 City Datum

Existing Rip-rap

Grade Easement per Section A-A (This Sheet)

Grade Easement per Section B-B (This Sheet)

Install Back of Curb Protection.

Grade Easement per Section B-B (This Sheet)

Install Drop Inlet Protection.

Underground irrigation systems within Reserve "A" have not been field verified. Contractor shall contact Developer to coordinate construction. Contractor shall be responsible for preservation of these systems and repair any damage caused by construction at no additional cost to the project.

		<b>Liberty Park 3rd Addition - Phase 2B</b> <b>EROSION CONTROL &amp; EASEMENT GRADING</b> <b>Street Improvements</b>	
		<small>Baughman Company, P.A. 315 Ellis St. Wichita, KS 67211 P 316-262-7271 F 316-262-0149          ENGINEERING   SURVEYING   PLANNING   LANDSCAPE ARCHITECTURE</small>	
PROJECT NUMBER 472-84069	DESIGN JAK	DRAWN JAK	DATE 3/11/14
REVISIONS:	APPROVED	SCALE Noted	SHEET <b>16 OF 24</b>
