
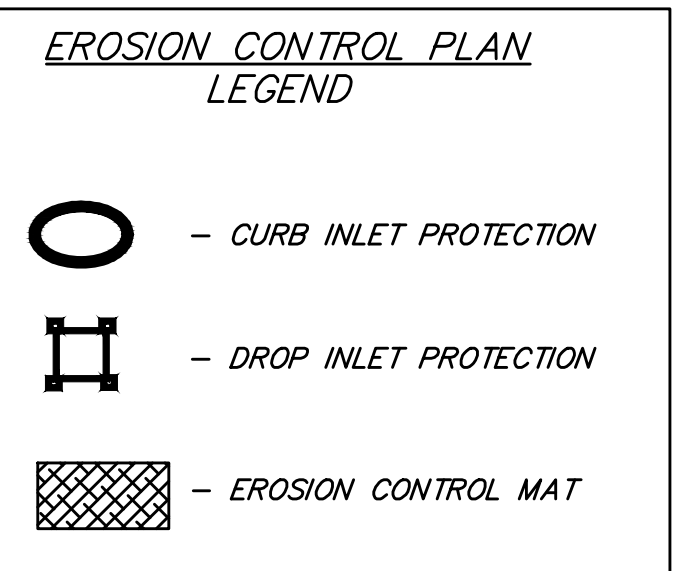
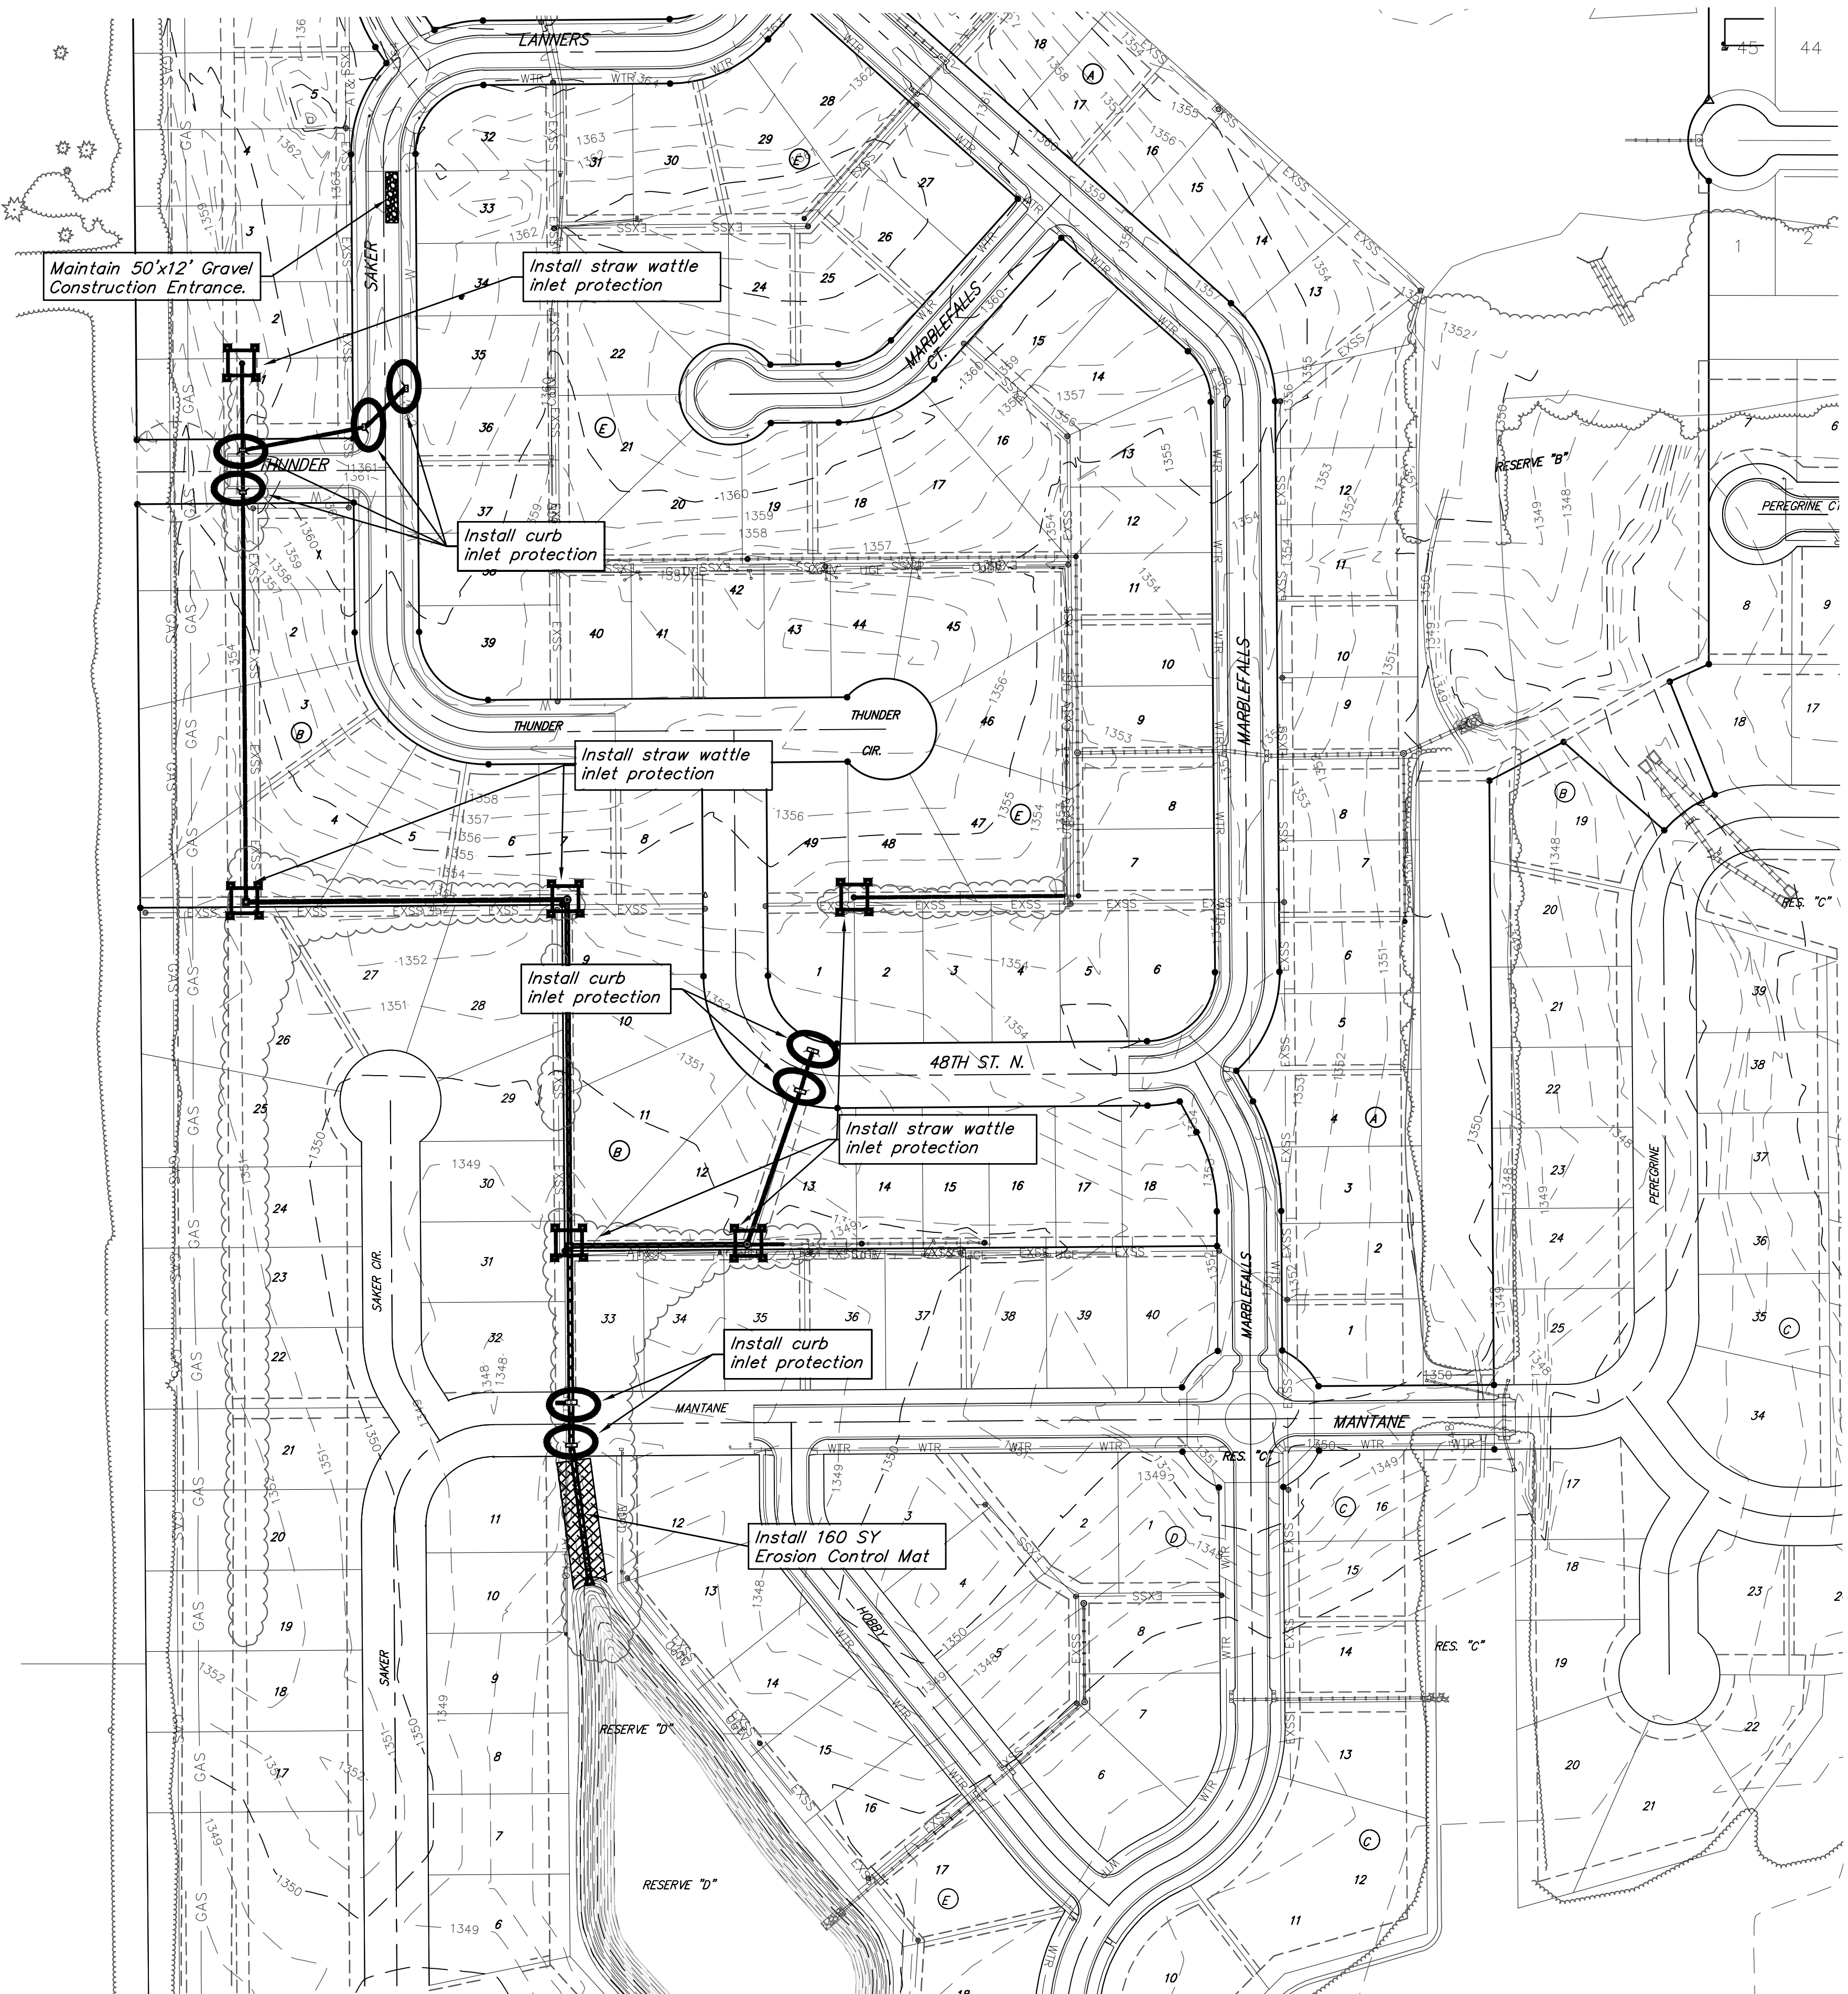


BENCHMARKS:
 BM #1: "□" Top of Curb NE of the most easterly corner of Lot 28, Block E, Falcon Falls 2nd Addition
 Elev. = 1361.23 (NGVD29)

BM #2: "□" Top of Curb North of the NE corner of Lot 2, Block D, Falcon Falls 3rd Addition
 Elev. = 1351.76 (NGVD29)

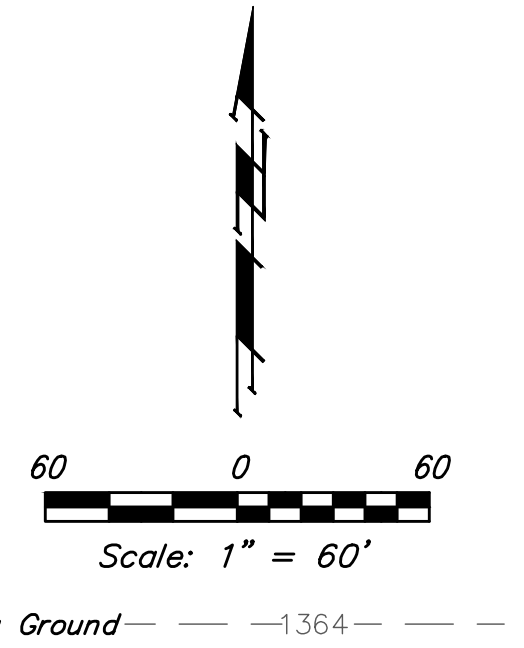

NOTES:

- Contractor shall make sure all erosion control is in place before project is accepted. This plan represents the minimum standard. Any additional erosion control measures shall be installed by the Contractor as needed.
- Removal of Gravel Construction Entrance for pavement construction shall be included in bid item "Site Clearing & Restoration"
- This Plan is Not To Be Used As A Comprehensive Grading Plan. All Spot Elevations Are Proposed & Subject To Change.

All areas disturbed during construction shall be seeded, mulched, and fertilized as per Cover Sheet General Notes.

EROSION CONTROL MEASURE	INSTALL	MAINTAIN
CONSTRUCTION ENTRANCE (EA)	0	1
DROP INLET PROTECTION (EA)	6	0
CURB INLET PROTECTION (EA)	8	0
EROSION CONTROL MAT (SY)	160	0

* ALL EXISTING BMPs INCLUDING CONSTRUCTION ENTRANCE, SEDIMENT BARRIERS, SILT FENCE, CUT-OFF TRENCH, AND EROSION CONTROL MAT SHALL BE MAINTAINED AND REPAIRED IF NECESSARY.

Baughman

Baughman Company, P.A. 315 Ellis St. Wichita, KS 67211 P 316-262-7271 F 316-262-0149
ENGINEERING | SURVEYING | PLANNING | LANDSCAPE ARCHITECTURE

Falcon Falls 2nd Addition - Phase 4A

EROSION CONTROL

Storm Water Sewer Improvements #731

<small>PROJECT NUMBER</small> 468-85340	<small>DESIGN</small> AEG
<small>REVISIONS:</small>	<small>DRAWN</small> JAK
	<small>DATE</small> 9/04/18
	<small>SCALE</small> Noted
	<small>SHEET</small> 10 OF 24

C:\Projects\Falcon Falls 2nd\Phase 4A\SW 1805-E010\SW PLANS.DWG
