

BENCHMARK: FOUNTAIN & GILBERT
S.E. 24th St. E. END
ELEVATION = 1615.2 CITY DATUM

RECONNECT SANITARY
SERVICE LINE INTO MAN-
HOLE AS NECESSARY

REMOVE & REPLACE
FENCES AS NECESSARY
AND IN GOOD CONDITION

CONTACT OWNERS OF ADJACENT
LOTS 48 HOURS PRIOR TO
REMOVAL OF FENCES

STA. 0+00; EXISTING
MANHOLE TOP ELEV. 176.10

REMOVE & REPLACE
CUMBER BLOCK AS
NECESSARY



REMOVE & RELOCATE
CURB & ANCHOR AS
NECESSARY

REMOVE & REPLACE
EXISTING PAVEMENT
AS NECESSARY

STA. 0+00; CONSTRUCT
PREFER CONCRETE MAN-
HOLE, TOP 174.50

STATION 871.77 REMOVE OR SAND
FILL EXISTING MANHOLE


ABANDON 871.77 OF
EXISTING SAN SEWER
LINE; PLUG LINE @
STA. 0+00 & 11.877

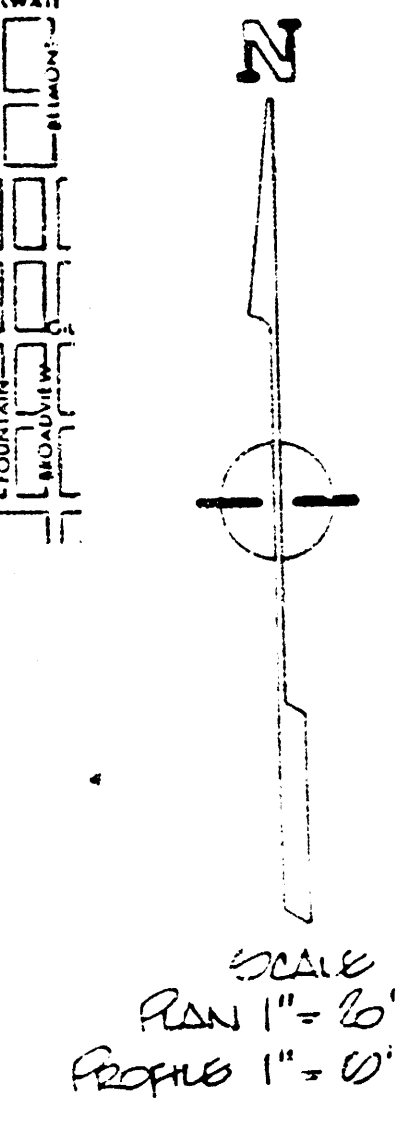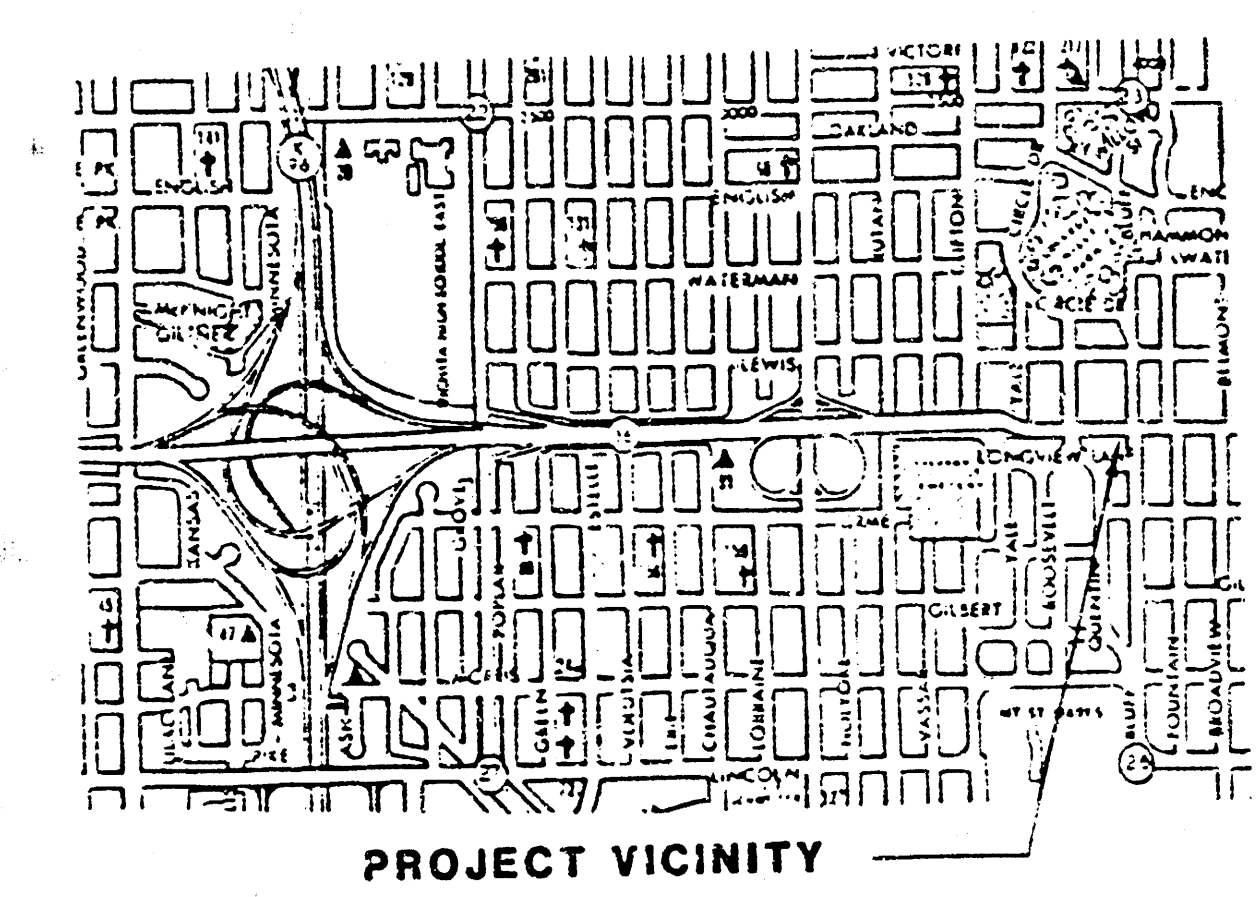

APPROVED AS NOTED
By CITY ENGINEER OF WICHITA
Sanitary Sewers *ELB 4/30/86*
Storm Sewers _____
Driveway Approaches _____
Water Mains _____
Paving _____

NOTE TO CONTRACTOR
This project will be constructed under the supervision of the CITY ENGINEER and conforming to the SPECIFICATIONS of the CITY OF WICHITA. The CONTRACTOR will pay the City of Wichita for all costs of plan review, inspection and booking per contract.

NOTE CONTRACTOR TO CONTACT THE ADJACENT OWNERS TO THE WEST 48 HOURS PRIOR TO ANY CONSTRUCTION REQUIRING REMOVAL OF ANY FENCE OR CURB. ONLY THE NECESSARY AMOUNT OF FENCE TO CONSTRUCT THE MANHOLE, AND REPLACE ALL FENCE IN GOOD CONDITION.
ABANDON THE EXISTING SEWER LINE TO THE EAST, AND SAND FILL TO REMOVE THE MANHOLE AS PER CITY SPECIFICATIONS.
CONTRACTOR TO CONTACT UTILITY COMPANIES PRIOR TO CONSTRUCTION TO VERIFY LINE LOCATIONS AND TO MAKE ANY ADJUSTMENTS FOR NECESSARY DEPTHS AND LOCATIONS FOR ADJUSTMENTS.

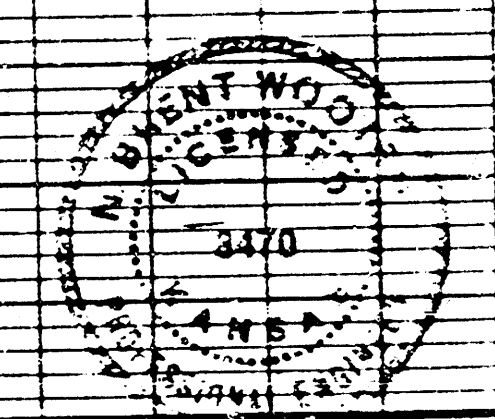

**MANHOLE CONSTRUCTION AND SEWER
ABANDONMENT FOR LOTS 1&2
LONGVIEW TERRACE ADDITION**
CITY OF WICHITA, KS.
PROJECT NO.
168-76-245-80001-000-000-068

BAUGHMAN COMPANY, P.A.
SURVEYING & ENGINEERING
310746-7271 • 330 LAURA • WICHITA, KANSAS 67211

PLATE 1-SINGLE PLAN AND PROFILE-FULL LINE
PRINTED IN U.S.A.

**FILMED FROM THE BEST
AVAILABLE COPY**
