

**General Notes**

1. Silt Fence Removal. Contractor shall remove all silt fence on the project once vegetation has been established to 70% coverage by area.


**Legend**

- Silt Fence (28,500 LF)
- Back of Curb Protection (300 LF)
- Ditch Check (9 Ea.)
- Curb Inlet Protection (3 Ea.)
- Sodding (1.9 acres)
- Permanent Seeding (1.6 acres)

**Estimated Seeding Areas**

Project Area Brome seed areas = Approximately 1.6 acres

1. Erosion control is to meet all federal, state, county and local code standards.
2. Contractor shall provide erosion protection throughout project construction. The plan provided here is for final protection. Various phases of this plan shall be implemented or modified to control erosion. Modifications of the plan shall be approved by the owner's representative.
3. All areas disturbed shall be seeded and fertilized as follows:  
 Brome Grass @ 200 lbs/acre  
 10-20-10 @ 200 lbs/acre
4. All seed shall be distributed with an acceptable drill intended for such operations, or other equipment approved by the owner's representative. Seeding depth shall be 1/4" maximum.
5. All seeded areas shall be immediately mulched w/prairie hay at 2 tons/acre. Anchor mulch by crimping into topsoil with suitable mechanical equipment.
6. Contractor is responsible for maintaining and implementing all erosion control until Final Inspection.

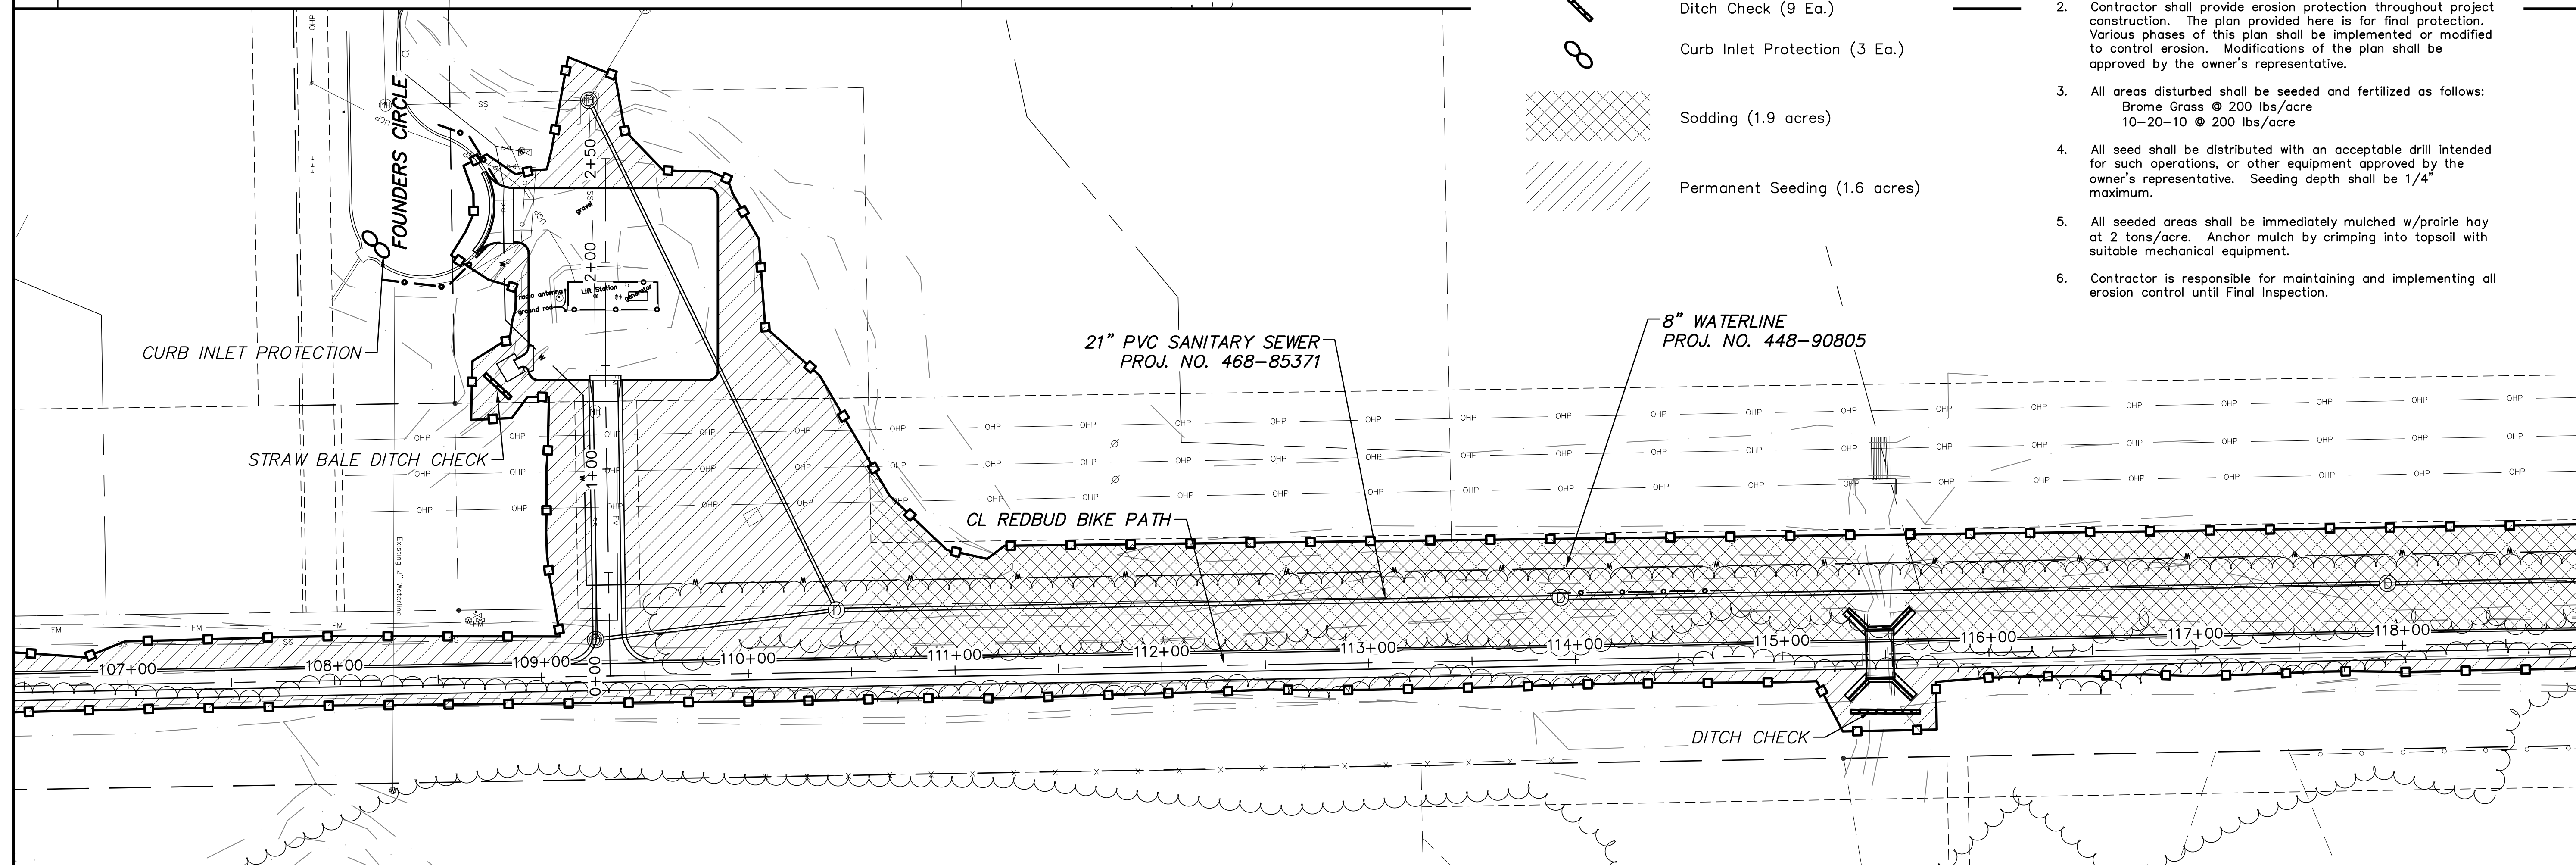

REDBUD MULTI-USE PATH K-96 TO 159TH STREET EAST SEEDING / SWPPP CITY OF WICHITA, KANSAS CARY JANZEN, P.E. - CITY ENGINEER C.O.N. Project #472-65360, C.C.A. #707125	By	Approved	Revision
	Date		
<b>POE &amp; ASSOCIATES, INC.</b> CONSULTING ENGINEERS 544 West Douglas Avenue Wichita, KS 67203 Phone 316/685-4114 FAX 316/685-4444	No.		
	Sheet	of	222
Engineer: T. EVANS Designer: J. UNRUH Dwg: P:\0207 Redbud Multi-Use\0207-Redbud-Use-Cal grade.dwg - SWPPP Pore Job No: 102127 Date: APRIL 2018			
