


B.M. 122.07 S.E. CORNER PORCH HOUSE # 2003 NORTH PENNSYLVANIA N.W. CORNER 19TH & PENN.
 B.M. 122.64 "T" IN TORY L-IRE PLUG 19TH & HYDRAULIC.
 B.M. 124.37 S.E. CORNER LOWER CONC. STEP SCHOOL S.S.-N.W. 19TH & 21ST

STATIONING ON #
 0+00 C.P.P. Bt 110.4 Lt 150
 0+06 C.P.P. Bt 16.0 To P. POLE
 0+06 Lt 30.0 BEGIN HEDGE
 0+15 Lt 25.0 1" TEAK
 0+26 Bt 26.0 1" TEAK
 0+31 Lt 21.0 MAPLE
 0+34 Lt 26.0 WATER METER
 0+44 Bt 23.0 1" W.K.
 0+45 Lt 23.0 1" W.K.
 0+52 Bt 23.0 1" TEAK
 0+54 Lt 23.0 1" TEAK
 0+54 Lt 23.0 1" TEAK
 0+57 Lt 15.0 BEGIN 12" R.C.P.
 0+58 Bt 12.0 BEGIN 12" R.C.P.
 0+59 Bt 15.0 END 12" R.C.P.
 0+60 Lt 15.0 END 12" R.C.P.
 0+74 Bt 30.5 BEGIN HEDGE
 0+82 Bt 19.0 1" ELM
 0+91 Bt 19.0 WATER METER
 0+91 Lt 19.0 WATER METER
 1+00 Lt 30.0 1" W.K.
 1+00 Bt 30.0 1" W.K.
 1+07 Bt 20.0 1" ELM
 1+13 Bt 15.5 BEGIN 12" R.C.P.
 1+13 Bt 15.5 BEGIN 12" R.C.P.
 1+15 Bt 31.5 END HEDGE
 1+23 Lt 16.0 END 12" R.C.P.
 1+25 Bt 18.5 END 12" R.C.P.
 1+26 Bt 18.5 P. POLE
 1+28 Bt 18.5 P. POLE
 1+40 Bt 21.5 WATER METER
 1+42 Lt 20.5 WATER METER
 1+50 Lt 30.5 1" W.K.
 1+50 Bt 30.5 1" W.K.
 1+61 Bt 29.0 END HEDGE
 1+64 Bt 12.5 BEGIN 12" R.C.P.
 1+64 Lt 14.0 BEGIN 12" R.C.P.
 1+77 Bt 12.5 END 12" R.C.P.
 1+77 Lt 14.0 END 12" R.C.P.
 1+91 Bt 23.0 WATER METER
 1+91 Lt 23.0 WATER METER
 2+00 Bt 30.0 1" W.K.
 2+00 Lt 30.0 1" W.K.
 2+15 Bt 12.5 BEGIN 12" R.C.P.
 2+15 Lt 15.5 BEGIN 12" R.C.P.
 2+27 Bt 12.5 END 12" R.C.P.
 2+27 Lt 15.5 END 12" R.C.P.
 2+42 Lt 21.5 WATER METER
 2+42 Bt 23.0 WATER METER
 2+50 Bt 30.0 1" W.K.
 2+50 Lt 30.0 1" W.K.
 2+64 Lt 15.0 BEGIN 12" R.C.P.
 2+64 Bt 12.5 BEGIN 12" R.C.P.
 2+77 Lt 15.0 END 12" R.C.P.
 2+77 Bt 11.5 END 12" R.C.P.
 2+78 Bt 15.0 P. POLE
 2+93 Bt 21.0 WATER METER
 2+93 Lt 21.0 WATER METER
 3+00 Bt 30.0 1" W.K.
 3+00 Lt 30.0 1" W.K.
 3+02 Bt 30.0 BEGIN HEDGE
 3+13 Lt 30.0 END HEDGE
 3+13 Lt 14.0 BEGIN 12" R.C.P.
 3+13 Lt 14.0 BEGIN 12" R.C.P.
 3+24 Bt 15.0 END 12" R.C.P.
 3+24 Lt 14.0 END 12" R.C.P.
 3+38 Bt 22.0 WATER METER
 3+41 Lt 25.0 WATER METER
 3+50 Lt 30.0 1" W.K.
 3+50 Bt 30.0 1" W.K.
 3+64 Bt 12.0 BEGIN 12" R.C.P.
 3+64 Lt 14.0 BEGIN 12" R.C.P.
 3+75 Bt 12.0 END 12" R.C.P.
 3+78 Lt 14.0 END 12" R.C.P.
 3+89 Bt 20.0 WATER METER
 3+94 Lt 20.0 WATER METER
 4+00 Bt 29.8 1" W.K.
 4+00 Lt 30.5 1" W.K.
 4+11 Lt 22.0 1" TEAK
 4+14 Bt 11.0 BEGIN 12" R.C.P.
 4+14 Lt 15.0 BEGIN 12" R.C.P.
 4+24 Bt 15.0 BEGIN 12" R.C.P.
 4+25 Bt 11.0 END 12" R.C.P.
 4+25 Lt 14.0 END 12" R.C.P.
 4+25 Lt 14.0 END 12" R.C.P.
 4+35 Bt 22.0 WATER METER
 4+43 Lt 22.0 WATER METER
 4+50 Lt 30.0 1" W.K.
 4+50 Bt 29.8 1" W.K.
 4+64 Bt 12.0 BEGIN 12" R.C.P.
 4+64 Lt 14.0 BEGIN 12" R.C.P.
 4+65 Bt 29.0 END 5' PICKET FENCE
 4+75 Lt 24.0 BEGIN 5' PICKET FENCE
 4+77 Lt 14.0 END 12" R.C.P.
 4+77 Lt 14.0 END 12" R.C.P.
 4+87 Bt 22.0 WATER METER
 4+87 Lt 30.0 1" W.K.
 4+97 Bt 30.0 1" W.K.
 4+97 Lt 30.0 1" W.K.
 5+12 Lt 30.6 END 3' PICKET FENCE
 5+14 Lt 14.5 BEGIN 12" R.C.P.
 5+27 Lt 14.5 END 12" R.C.P.
 5+47 Lt 22.0 WATER METER
 5+47 Bt 23.0 WATER METER
 5+50 Bt 30.0 1" W.K.
 5+55 Lt 17.0 TO DENDMAN
 5+63 Bt 14.0 BEGIN 12" R.C.P.
 5+66 Lt 15.0 BEGIN 12" R.C.P.
 5+78 Bt 14.0 END 12" R.C.P.
 5+78 Lt 13.0 END 12" R.C.P.
 5+87.30 Bt 16.0 TO P. POLE
 5+87.30 Lt 11.0 P. POLE

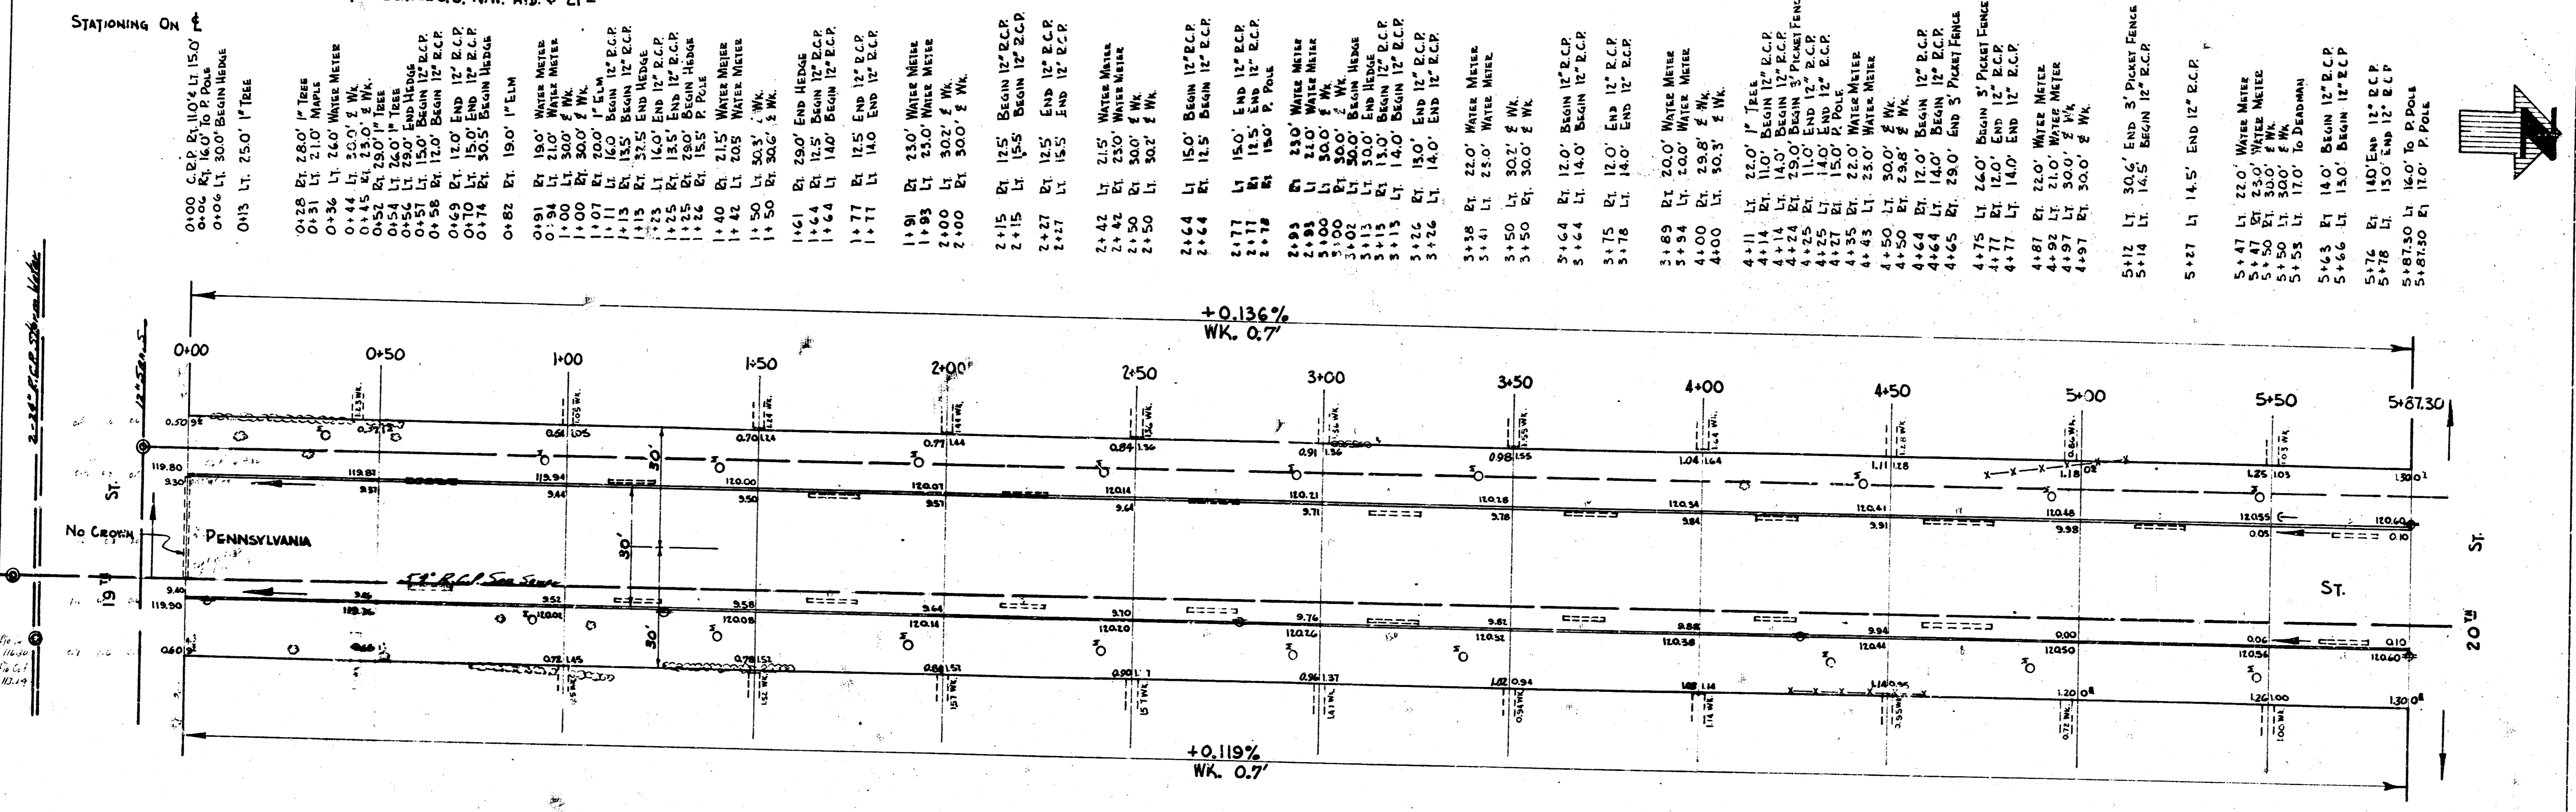

NOTE TO FIELD ENGINEER & CONTRACTOR
 ALL ENTRANCE PIPES ARE TO BE DISPOSED
 OF IN ACCORDANCE TO CITY DIST CHECKER'S
 INSTRUCTIONS.

PROP.	TOTAL EXCAV.	CITY
1269.9		0 CU. Yd.
127.0		
1396.9		



PENNSYLVANIA ST.
 N.L. 19TH - S.L. 20TH
 30' CONC. & C.B.
 CITY OF WICHITA, KANS.
 B.E. SMITH CITY ENGINEER
 FEB. 1957 PROJ. NO. C-13-286
