


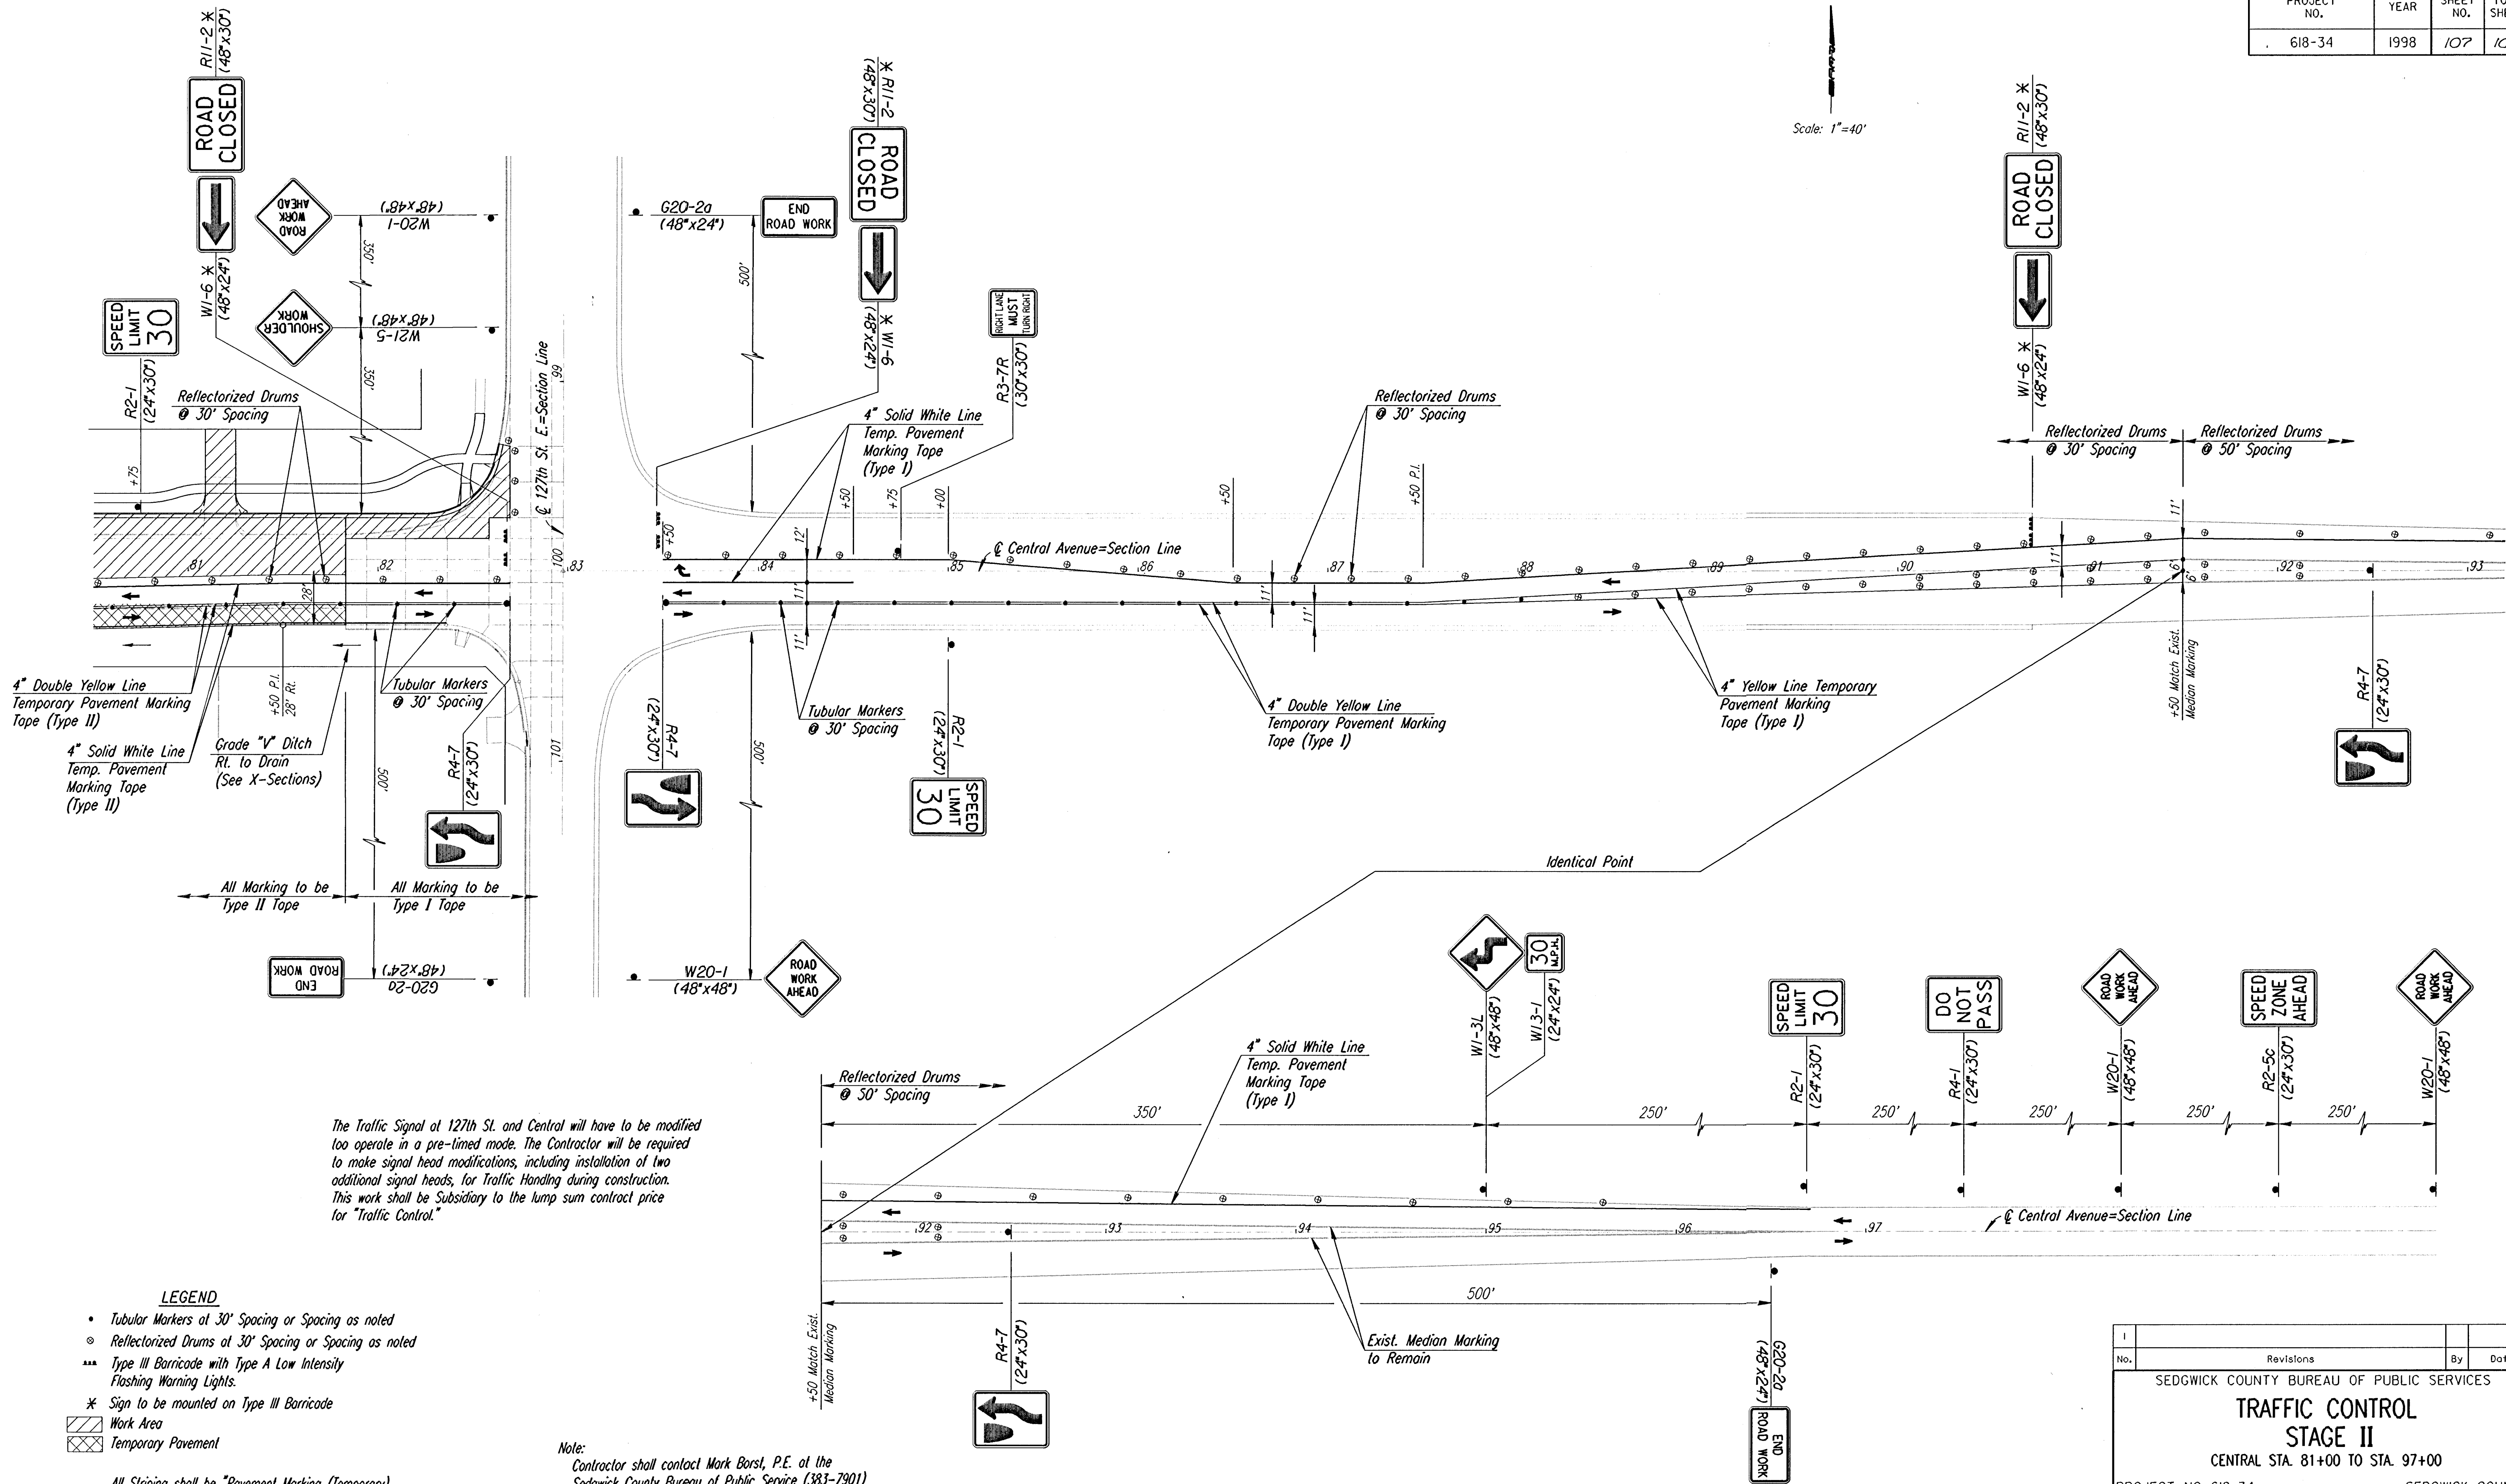

The Traffic Signal at 127th St. and Central will have to be modified to operate in a pre-timed mode. The Contractor will be required to make signal head modifications, including installation of two additional signal heads, for Traffic Handling during construction. This work shall be Subsidiary to the lump sum contract price for "Traffic Control."

LEGEND

- Tubular Markers at 30' Spacing or Spacing as noted
- Reflectorized Drums at 30' Spacing or Spacing as noted
- *** Type III Barricade with Type A Low Intensity Flashing Warning Lights.

* Sign to be mounted on Type III Barricade

Work Area

Temporary Pavement

All Striping shall be "Pavement Marking (Temporary) (Type as shown)".

Note:

Contractor shall contact Mark Borst, P.E. at the Sedgwick County Bureau of Public Service (383-7901) prior to beginning work that affects the Traffic Signal at Central and 127th Street E.

I			
No.	Revisions	By	Date
SEDGWICK COUNTY BUREAU OF PUBLIC SERVICES			
TRAFFIC CONTROL			
STAGE II			
CENTRAL STA. 81+00 TO STA. 97+00			
PROJECT NO. 618-34		SEDGWICK COUNTY	
PROFESSIONAL ENGINEERING CONSULTANTS, P.A.			
ENGINEERS			
WICHITA, KANSAS			
Designed by	WDH	Checked by	RPG
Drawn by	MAF	Date JULY 1997	Job No. 95297-2
