

BENCHMARKS:
 RR spike in asphalt, SW COR., N1/2,
 SW1/4, Sec. 34, TWP. 26-S, R-2-E.
 Elev. = 1400.59 NAVD88


Square cut in top of curb
 North side of Brookview Cir.
 Approx. 14.5' south of the SE cor.
 of Lot 55, Block E, Brookfield Addn.
 Elev. = 1376.51 NAVD88

City of Wichita Benchmark Disk
 in top of curb, North side of
 Brookview Cir. adjacent to fire hydrant
 Approx. 17.8' SW of the SE cor. of
 Lot 58, Block E, Brookfield Addn.
 Elev. = 1376.51 NAVD88



Irons			
Point #	Northing	Easting	Description
1	1,710,224.38	1,685,819.67	SCR IP
2	1,710,125.87	1,685,897.20	Iron
3	1,710,151.35	1,685,921.56	Iron
4	1,710,155.73	1,686,146.52	Iron
5	1,710,172.68	1,686,246.20	Iron
6	1,710,180.00	1,686,622.34	Iron
7	1,710,181.69	1,686,709.32	Iron
10	1,710,276.41	1,688,491.69	N1/4COR
11	1,710,216.42	1,688,493.01	Iron
12	1,708,434.40	1,688,532.32	Iron
13	1,708,314.79	1,687,434.98	Iron
14	1,708,375.36	1,687,466.71	Iron
15	1,708,431.69	1,687,432.50	Iron
16	1,708,468.12	1,687,337.71	Iron
17	1,708,463.53	1,687,200.91	Iron
18	1,708,423.09	1,687,137.52	Iron
19	1,708,356.21	1,687,077.37	Iron
20	1,708,342.53	1,687,009.18	Iron
21	1,708,452.99	1,686,886.36	Iron
22	1,708,327.13	1,685,927.82	Iron
23	1,708,413.61	1,685,925.62	Iron
24	1,710,141.15	1,686,623.10	Iron
25	1,710,079.18	1,686,631.93	Iron
26	1,710,067.22	1,686,711.55	Iron
27	1,710,039.71	1,686,643.43	Iron
28	1,710,051.74	1,686,712.48	Iron
29	1,709,995.10	1,686,726.94	Iron
30	1,709,983.85	1,686,662.70	Iron
31	1,710,041.37	1,686,532.22	Iron
32	1,709,984.06	1,686,523.25	Iron
33	1,709,987.30	1,686,477.84	Iron
34	1,710,045.30	1,686,477.10	Iron
35	1,710,043.00	1,686,298.19	Iron
36	1,709,985.01	1,686,298.94	Iron
37	1,710,026.60	1,686,213.67	Iron
38	1,709,972.54	1,686,234.68	Iron
39	1,709,952.90	1,686,110.33	Iron
40	1,710,010.80	1,686,113.64	Iron
41	1,710,042.43	1,686,875.70	Iron
42	1,709,986.21	1,686,861.45	Iron
43	1,710,043.68	1,687,111.90	Iron
44	1,709,987.61	1,687,126.74	Iron
106	1,709,711.10	1,687,110.71	Iron
107	1,709,649.60	1,687,092.97	Iron
108	1,709,823.40	1,686,739.62	Iron
109	1,709,769.33	1,686,773.86	Iron
110	1,709,702.65	1,686,906.88	Iron
111	1,709,671.01	1,686,935.20	Iron
112	1,709,659.98	1,686,859.19	Iron
113	1,709,623.32	1,686,977.87	Iron
114	1,709,562.76	1,687,032.06	Iron
115	1,709,520.08	1,686,984.36	Iron
116	1,709,189.64	1,687,079.94	Iron
117	1,709,141.65	1,686,963.34	Iron
118	1,709,093.96	1,687,006.02	Iron
119	1,709,122.65	1,687,034.40	Iron
120	1,709,168.02	1,687,111.74	Iron
121	1,709,110.68	1,687,168.96	Iron
122	1,709,070.69	1,687,110.84	Iron
123	1,709,028.22	1,687,155.19	Iron
124	1,709,074.77	1,687,193.25	Iron
125	1,708,988.72	1,687,279.34	Iron
126	1,708,940.67	1,687,246.85	Iron
127	1,708,942.55	1,687,347.63	Iron
128	1,708,894.50	1,687,315.14	Iron
129	1,708,897.73	1,687,529.40	Iron
130	1,708,840.08	1,687,535.82	Iron
131	1,708,903.76	1,687,583.57	Iron
132	1,708,922.02	1,687,600.46	Iron
133	1,708,932.97	1,687,698.82	Iron
134	1,708,918.87	1,687,719.31	Iron
135	1,708,923.84	1,687,763.90	Iron
136	1,708,866.20	1,687,770.32	Iron
137	1,708,924.52	1,687,985.37	Iron
138	1,708,866.84	1,687,979.31	Iron
139	1,708,853.79	1,688,103.46	Iron
140	1,708,911.47	1,688,109.52	Iron
141	1,708,853.87	1,688,246.77	Iron
142	1,708,781.60	1,688,237.28	Iron
143	1,708,945.64	1,686,744.27	Iron

Irons			
Point #	Northing	Easting	Description
144	1,708,918.08	1,686,809.45	Iron
145	1,708,866.33	1,686,747.13	Iron
146	1,708,832.81	1,686,775.72	Iron
147	1,708,885.36	1,686,837.35	Iron
148	1,708,847.94	1,686,855.01	Iron
149	1,708,808.60	1,686,812.40	Iron
150	1,708,749.89	1,686,871.88	Iron
151	1,708,793.01	1,686,910.66	Iron
152	1,708,766.75	1,686,939.86	Iron
153	1,708,723.63	1,686,901.07	Iron
154	1,708,814.43	1,686,648.00	Iron
155	1,708,862.69	1,686,596.15	Iron
156	1,708,883.33	1,686,588.56	Iron
157	1,708,905.42	1,686,648.63	Iron
158	1,708,886.85	1,686,655.46	Iron
159	1,709,012.21	1,686,584.45	Iron
160	1,708,969.53	1,686,536.76	Iron
161	1,709,104.48	1,686,501.89	Iron
162	1,709,147.71	1,686,463.21	Iron
163	1,709,184.38	1,686,504.20	Iron
164	1,709,141.16	1,686,542.87	Iron
165	1,709,224.06	1,686,561.64	Iron
166	1,709,172.58	1,686,588.37	Iron
167	1,709,282.02	1,686,639.00	Iron
168	1,709,241.91	1,686,680.89	Iron
169	1,709,327.86	1,686,682.89	Iron
170	1,709,287.74	1,686,724.78	Iron
171	1,709,255.02	1,686,367.19	Iron
172	1,709,212.35	1,686,319.50	Iron
173	1,709,327.60	1,686,273.23	Iron
174	1,709,385.13	1,686,280.55	Iron
175	1,709,453.79	1,686,318.37	Iron
176	1,709,411.56	1,686,366.46	Iron
177	1,709,568.84	1,686,419.39	Iron
178	1,709,584.09	1,686,433.50	Iron
179	1,709,623.06	1,686,398.77	Iron
180	1,709,661.65	1,686,442.08	Iron
181	1,709,622.68	1,686,476.80	Iron
182	1,709,526.61	1,686,467.49	Iron
183	1,709,601.55	1,686,561.24	Iron
184	1,709,657.77	1,686,530.65	Iron
185	1,709,703.41	1,686,595.38	Iron
186	1,709,655.72	1,686,638.06	Iron
187	1,709,774.09	1,686,674.37	Iron
188	1,709,726.39	1,686,717.05	Iron
189	1,709,418.63	1,686,216.77	Iron
190	1,709,379.96	1,686,173.55	Iron
191	1,709,476.23	1,686,087.41	Iron
192	1,709,514.91	1,686,130.63	Iron
193	1,709,609.21	1,686,093.87	Iron
194	1,709,608.44	1,686,035.88	Iron
195	1,708,748.79	1,686,521.37	Iron
196	1,708,727.05	1,686,514.17	Iron
197	1,708,678.90	1,686,457.50	Iron
198	1,708,675.31	1,686,434.89	Iron
199	1,708,645.70	1,686,408.32	Iron
200	1,708,686.76	1,686,359.22	Iron
201	1,708,466.44	1,686,174.99	Iron
202	1,708,413.12	1,686,213.83	Iron
203	1,708,429.72	1,686,131.81	Iron
204	1,708,362.21	1,686,153.87	Iron
205	1,708,330.02	1,686,041.74	Iron
206	1,708,412.28	1,686,048.00	Iron
207	1,708,415.22	1,685,989.19	Iron

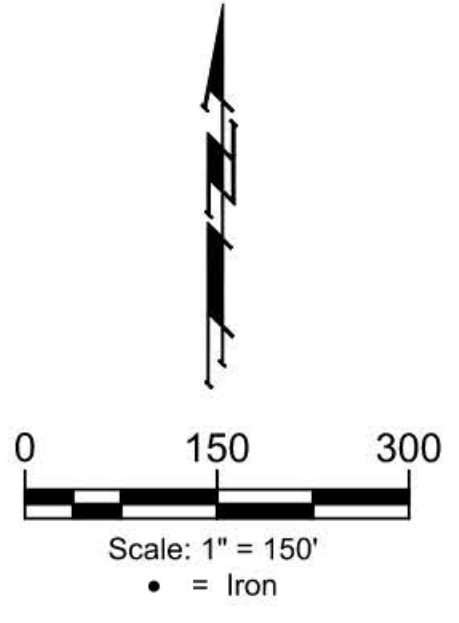

**BAUGHMAN
 COMPANY**
 315 Ellis St.
 Wichita, KS 67211
 316-262-7271
 BaughmanCo.com

BROOKFIELD ADDITION
COORDINATES

Sidewalk Improvements
 PROJECT NUMBER:
 DESIGN: AEG DRAWN: JAK
 DATE: July 7, 2021
 SHEET **13** OF **16**

File: C:\Projects\Brookfield Addition - 16-04-P190\Engineering\Reserve J - Sidewalk\Sidewalk_21-05-E909.dwg
