1) Design Speed: Those items delegated to temporary traffic control should be designed and installed using the posted/legal speed of the roadway prior to work starting.

2) Minimum Lane Width: Lane widths shall be a minimum of 11' (measured between centerlines of pavement markings) or as shown on the plans, or as directed by the engineer. A lane width less than 11' may require restricted roadway width signing.

3) Consideration should be made to separate pedestrian and, if needed, bicycle movements from both work site activity and vehicular traffic. Unless a reasonable safe route that does not involve crossing the roadway can be provided, pedestrians should be appropriately directed with advance signing that encourages them to cross to the opposite side of the roadway. In urban and suburban areas with high vehicular traffic volumes, these signs should be placed at intersections (rather than midblock locations) so that pedestrians are not confronted with midblock work sites that will induce them to attempt skirting the work site or making a midblock crossing.

4) When existing pedestrian facilities are disrupted, closed, or relocated, the temporary facilities shall be detectable and include accessibility features consistent with the features present in the existing pedestrian facility.

5) When the driving surface open to traffic is milled or is a temporary surface made of loose material, or when directed by the engineer a W8-15 (Grooved Pavement) or W8-7 (Loose Gravel) sign shall be used on mainline approaches. This sign should be placed a "C" distance after the W20-1 (Road Work Ahead) sign. A W8-15p motorcycle plaque shall be used to supplement the W8-15 or W8-7 signs. All signs shall be displayed as long as the condition is present.

6) Alternative temporary rumble strip options may be available. Please contact the Temporary Traffic Control Unit for more information at 785-296-1179 or 785-296-1183.

STATE	PROJECT NO.	YEAR	SHEET NO.	TOTAL SHEETS
KANSAS	237042-005	2024	21	22

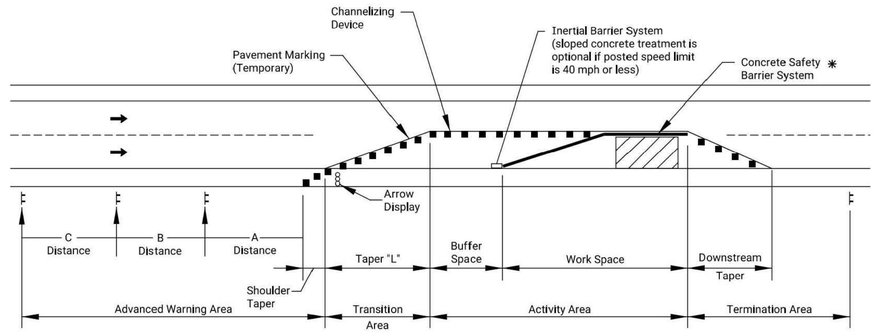

TYPICAL WORK ZONE COMPONENTS

✳When concrete barrier system is used, portable channelizing devices are not needed along the tangent barrier section.

Minimum advance warning sign spacing (in feet):

SPEED (MPH) ✳	*A*	*B*	*C*
URBAN (40 MPH OR LOWER)	*100*	*100*	*100*
URBAN (45 MPH OR HIGHER)	*350*	*350*	*350*
RURAL (55 MPH OR LOWER)	*500*	*500*	*500*
RURAL (60 MPH OR HIGHER)	*750*	*750*	*750*
EXPRESSWAY/FREEWAY	*1000*	*1500*	*2640*

✳ Posted speed prior to work starting

The minimum spacing between signs shall be no less than 100', unless directed by the engineer.

The spacing between any signs may be increased beyond the minimum values in the table above as approved by the engineer in order to maximize visibility.

Taper Formulas:

L = WS for speeds of 45 MPH or more

$L = WS^2/60$ for speeds of 40 MPH or less

Where: L = Minimum length of taper in feet
S = Numericial value of posted speed prior to work starting in MPH
W = Width in offset feet

Shifting Taper=1/2 L
Shoulder Taper=1/3 L

Channelizer Placement:

(1) The spacing between devices in transition area (taper) should not exceed a distance in feet equal to 1/2 the posted speed limit in mph prior to work starting.

(2) The spacing between devices in the advanced warning area and the activity area should not exceed a distance in feet equal to two times the posted speed limit in mph prior to work starting.

(3) Channelizing devices shall be placed for optimum visibility, normally at right angles to the traffic flow.

(4) Place directional indicator barricades in series to direct traffic onto the new path. The arrow sign should not be visible to opposing traffic.

(5) Alternating diagonal orange and white striping must slope downward in the direction traffic is expected to pass.

Buffer Space

SPEED (MPH) ✳	*20*	*25*	*30*	*35*	*40*	*45*	*50*	*55*	*60*	*65*	*70*	*75*
LENGTH (ft)	*115*	*155*	*200*	*250*	*305*	*360*	*425*	*495*	*570*	*645*	*730*	*820*

✳ Posted speed prior to work starting

Neither work activity nor storage of equipment, vehicles, or material should occur in the buffer space. When a protection vehicle is placed in advance of the work space, only the space upstream of the vehicle constitutes the buffer space.

If temporary concrete safety barrier system is used to separate approaching traffic from the work space, the barrier system shall be considered part of the activity area. A full lane width should be available throughout the length of the buffer space. See typical work zone components above.

NO.	DATE	REVISIONS	BY	APP'D
02	03-13-18	W8-15p usage changed to Shall	R.W.B.	E.K.G.
01	08-18-15	Channelizer spacing info	R.W.B.	K.E.

KANSAS DEPARTMENT OF TRANSPORTATION

TRAFFIC CONTROL GENERAL NOTES

TE700

FHWA APPROVAL		03-13-18	APP'D.	Eric Kocher
DESIGNED B.A.H.	DETAILED R.W.B.	QUANTITIES	TRACED	
DESIGN CK.	DETAIL CK.	QUAN.CK.	TRACE CK.	

KDOT Graphics Certified 07-18-2022 Sh. No. 21

KDOT Graphics Certified

PEC
PROFESSIONAL ENGINEERING CONSULTANTS
303 SOUTH TOPEKA
WICHITA, KS 67202
316-262-2691 www.pec1.com

CITY OF WICHITA

HUNTER JAMES WILES
LICENSED
Hunter Wiles
29849
01/03/2025
KANSAS
PROFESSIONAL ENGINEER

STORMWATER SEWER IMPROVEMENTS AT WASSALL AND HYDRAULIC

CITY OF WICHITA
SEDGWICK COUNTY, KANSAS
458-2024-085592

Issue:		

JOB NO.	237042-005
DATE	JANUARY 2025
PM	KMS
DESIGNED BY	HJW
DRAWN BY	BJH
CHECKED BY	TPA

TRAFFIC CONTROL GENERAL NOTES

CT151
21 OF 22

SAVED 11/6/2024 9:51:59 AM BY HUNTER.WILES
PLOTTED 1/3/2025 2:17:04 PM BY BRADLEY HAYNES
U:\WICHITA-CIVIL\2023\237042\005\2PD4_PLANS\030\237042-005-CT151.DWG
