F. E. Short

B.M. 115.47 S.W. Cor. lower Conc. step Hotel 100.4 E. 10th N.E. Cor. 10th & Washington

Install 2x5' Catchbasin, connect same to present catchbasin with 12" pipe.

1+53 tree W.

1+71 tree W.

1+80 power-pole W.

3+36 Power-Pole W.

5+45 Power-Pole W.

5+72 R.R. Control Box W.

5+77 W.U.T. Pole E.

B.M. 117.69 High point top limestone Cor. post N.S. Hotel 114.9 N. Washington

NOTE: Use ramp type crst

Ties to iron on W.S. Wash. & 15' S. of W. P.L. 10th St. W.
1. 18.60' N.E. to "K" in Keller Bk. Wk. N.
2. 28.35' E. to gauge of W. rail
3. 15.00' N. to ⊸ cut in W.K.

Ties to iron on E.S. Wash. & S.L. of 10th St. E.
1. 27.00' W. to gauge W. rail
2. 22.96' N.E. to "K" in Keller Ctr. Wk. E.
3. 30.00' N. to tacked Stake

Ties to iron on E.S. Wash. & 1/4-1/4 Line in 11th St.
1. 12.5' N. of S.L. 11th St. W.
2. 11.15' W. to gauge of W. rail

Fill under walk

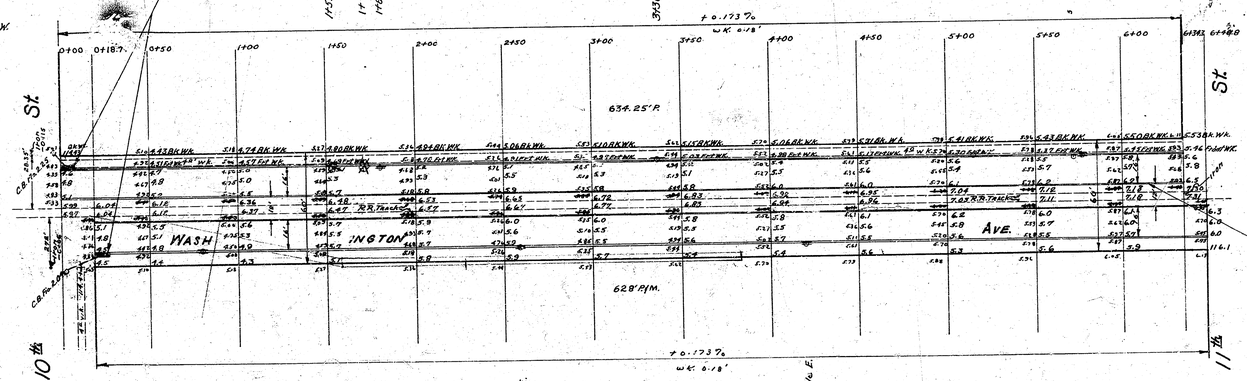

NOTE: Curbs shown along rail road are not to be installed. Use Flow Line grades for elevation of edge of slab.

NOTE: Where elevations will permit pour new walk over old walk. Otherwise, the old walk shall be removed.

0+80 W.U.T. Pole E.

2+59 W.U.T. Pole E.

4+20 W.U.T. Pole E.

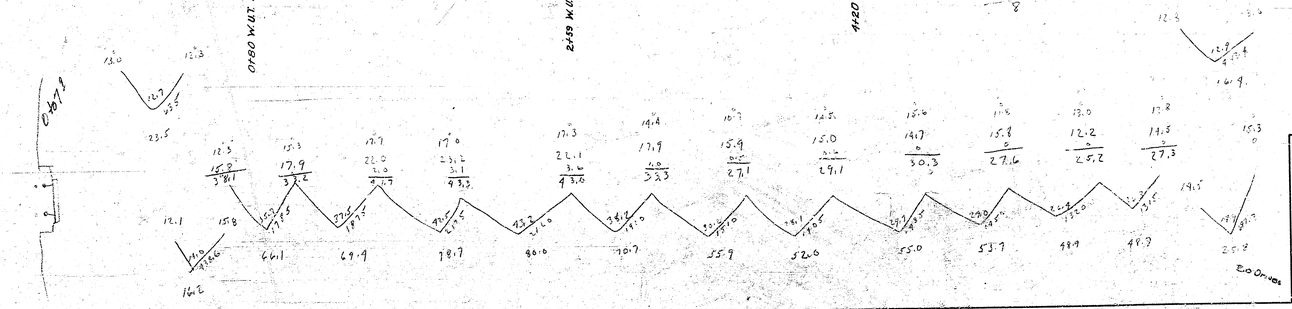

Proportionally

23.5
16.2
20.1
16.9
78.7
89.9
15.2
51.9
57.6
55.0
52.7
41.9
98.7
25.3
10.9
761.0
+109.0
837.1 Cu. yds.

Washington Ave.
10th St. N.L. ~ 11th St. S.L.
32' Conc. & Curb
City of Wichita, Kansas
L. K. White ~ City Engineer
October 4, 1949 Proj. # C-19-158

4 2 5 (51)
