BENCHMARK:

"□" Cut on Top of Curb, North Side Sietkes, NW of Center Line of Sietkes Ct., Shadybrook Meadow Addition.
Elev. = 1315.19 City Datum
(1322.59 NGVD)

NOTES:
1. This Plan Is Not To Be Used As A Comprehensive Grading Plan. All Spot Elevations Are Proposed & Subject To Change.

2. Each Lot Area Disturbed By Construction Shall Be the Responsibility of Each Individual Homeowner. Owner Responsible to Follow All SWPP Plans & Guidelines For The Area.

3. Erosion Control Matting, Seeding & Fertilizer Shall Be Installed at All Locations Where Fill of Excavation Will Cause the Finish Grade To Be Greater Than or Equal to a 5:1 Sideslope. All Other Disturbed Areas Shall be Seeded, Fertilized, & Mulched As Follows:

SEED --
8 lbs. per 100 s.f. of K-31 Fescue.
FERTILIZER --
12-24-12 Ratio - 850 lbs./ac.
MULCH --
2 Tons of Prairie Hay or Bromegrass Hay per Acre "Patted" w/Forks Or Punched Into Soil To Reduce Loss Due To Wind.

4. Install 8' Wide Culex/Excelsior Blanket, or Approved Equal, on Prepared Surface Back of Curb. Edge of Bloket Will Be At Back of Curb. Install Per Manufactures Recommendation, Including Staples.

- LIGHT STONE RIP-RAP (Installation Per Standard Specifications)
- DROP INLET PROTECTION (Use Drop Inlet Protection w/CMU Block Or Vorti-Pro, See SWPPP Guidelines For Details.)
- CURB INLET PROTECTION (Use Curb Inlet Protection w/ Gravel Pipe, See SWPPP Guidelines For Details.)
- STRAW BALE BARRIERS (Installation Details Under SWPPP Guidelines)
- SILT FENCING (Installation Details Under SWPPP Guidelines)

STORMWATER POLLUTION PREVENTION PLAN
CONTROL MEASURES LEGEND
NO SCALE

EROSION CONTROL MEASURE	UNITS	QUANTITY
SILT FENCE	L.F.	0
RIPRAP	S.Y.	0
DROP INLET BARRIER	EA.	8
CURB INLET BARRIER	EA.	3
STRAW BALE DITCH CHECK	EA.	0
EARTHEN DIKES	L.F.	0
BACK OF CURB CURLEX	S.Y.	2856
POND E.C. BLANKET	S.Y.	0
CONSTRUCTION ENTRANCE	EA.	1

QUANTITIES ARE FOR INFORMATION ONLY! CONTRACTOR SHALL VERIFY QUANTITIES PER SPECIFIC ENGINEERING PLAN SHEET.

CONTRACTOR SHALL REMOVE CONSTRUCTION ENTRANCE AT THE CONCLUSION OF CONSTRUCTION ACTIVITIES

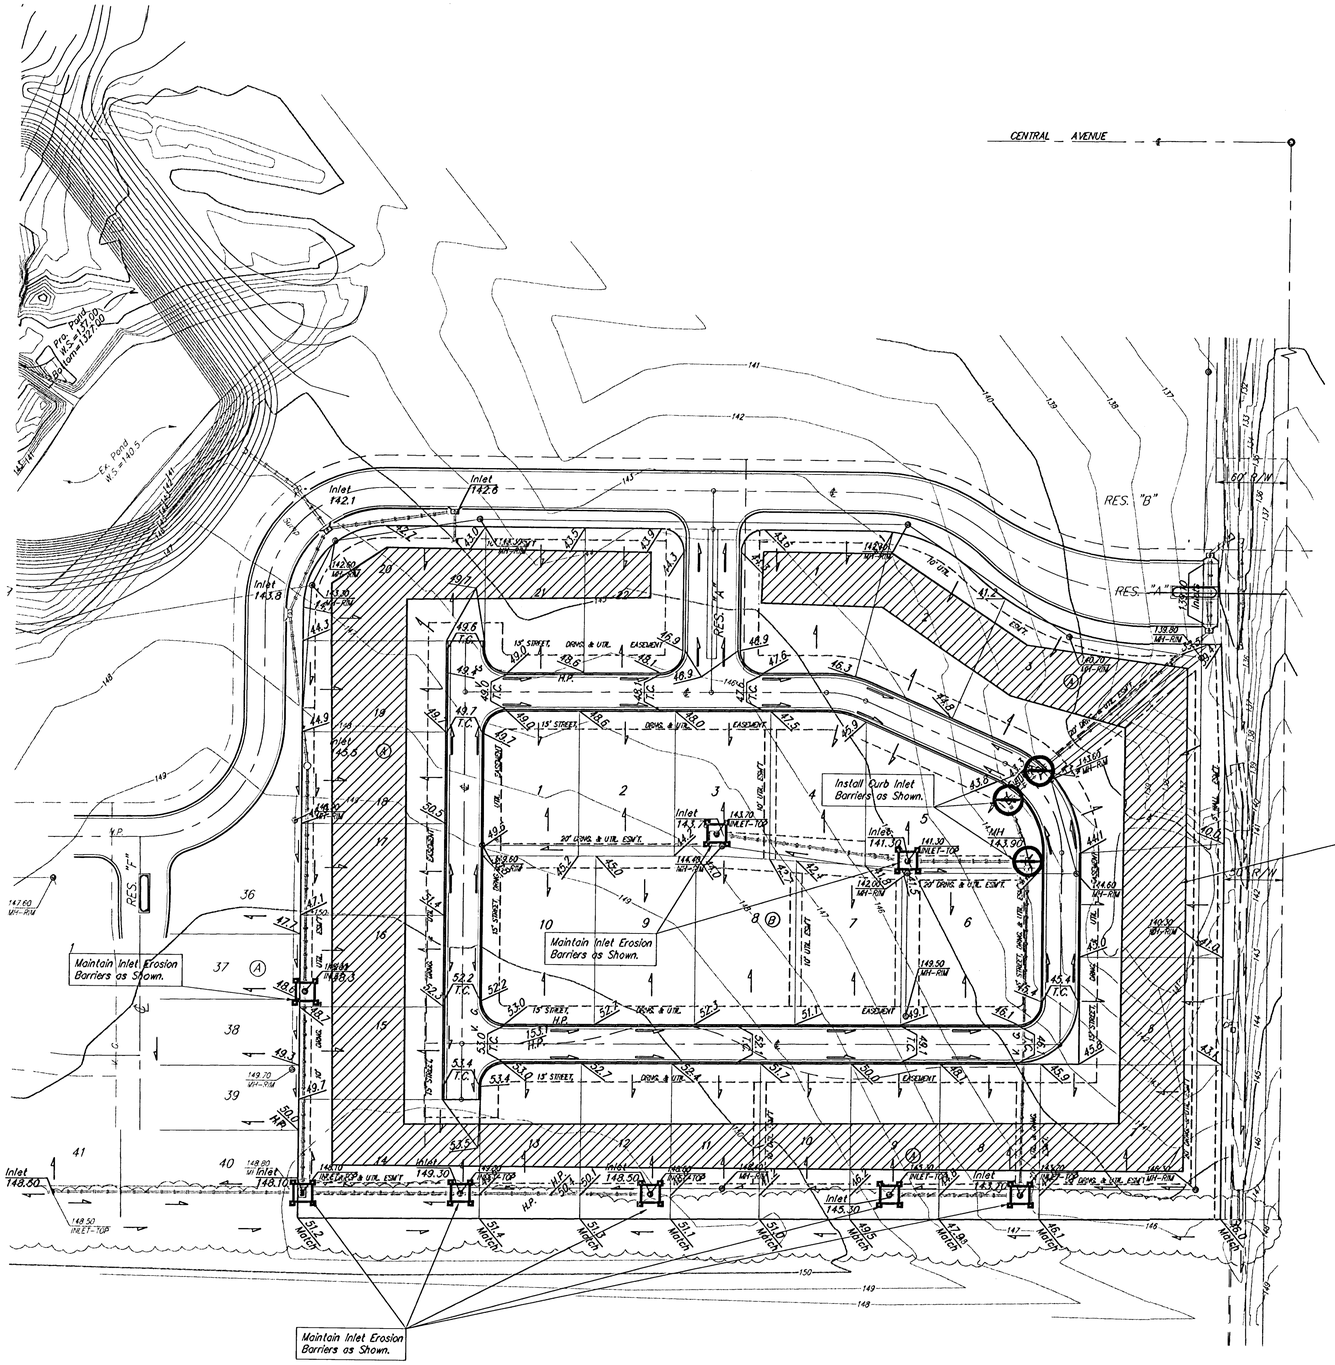

SCALE: 1" = 60'
• = Iron

SHOAL CREEK 2ND ADDITION
EROSION CONTROL PLAN
WICHITA, KANSAS

BAUGHMAN COMPANY P.A.
ENGINEERING, SURVEYING, & PLANNING
316-262-7271 • 315 ELLIS • WICHITA, KANSAS 67211

PROJECT NUMBER 472-83820
SHEET 10 OF 20
DESIGN NBW | DRAWN AEG | APPROVED | DATE 10/03 | SCALE 1" = 60'

SWPPP Sheet
