EROSION CONTROL PLAN LEGEND

- DROP INLET PROTECTION
- CURB INLET PROTECTION
- DITCH CHECKS
- SILT FENCING
- EROSION CONTROL BERM
- BACK OF CURB PROTECTION
- EROSION CONTROL MAT
- TEMPORARY DITCH
- STRAW WATTLE

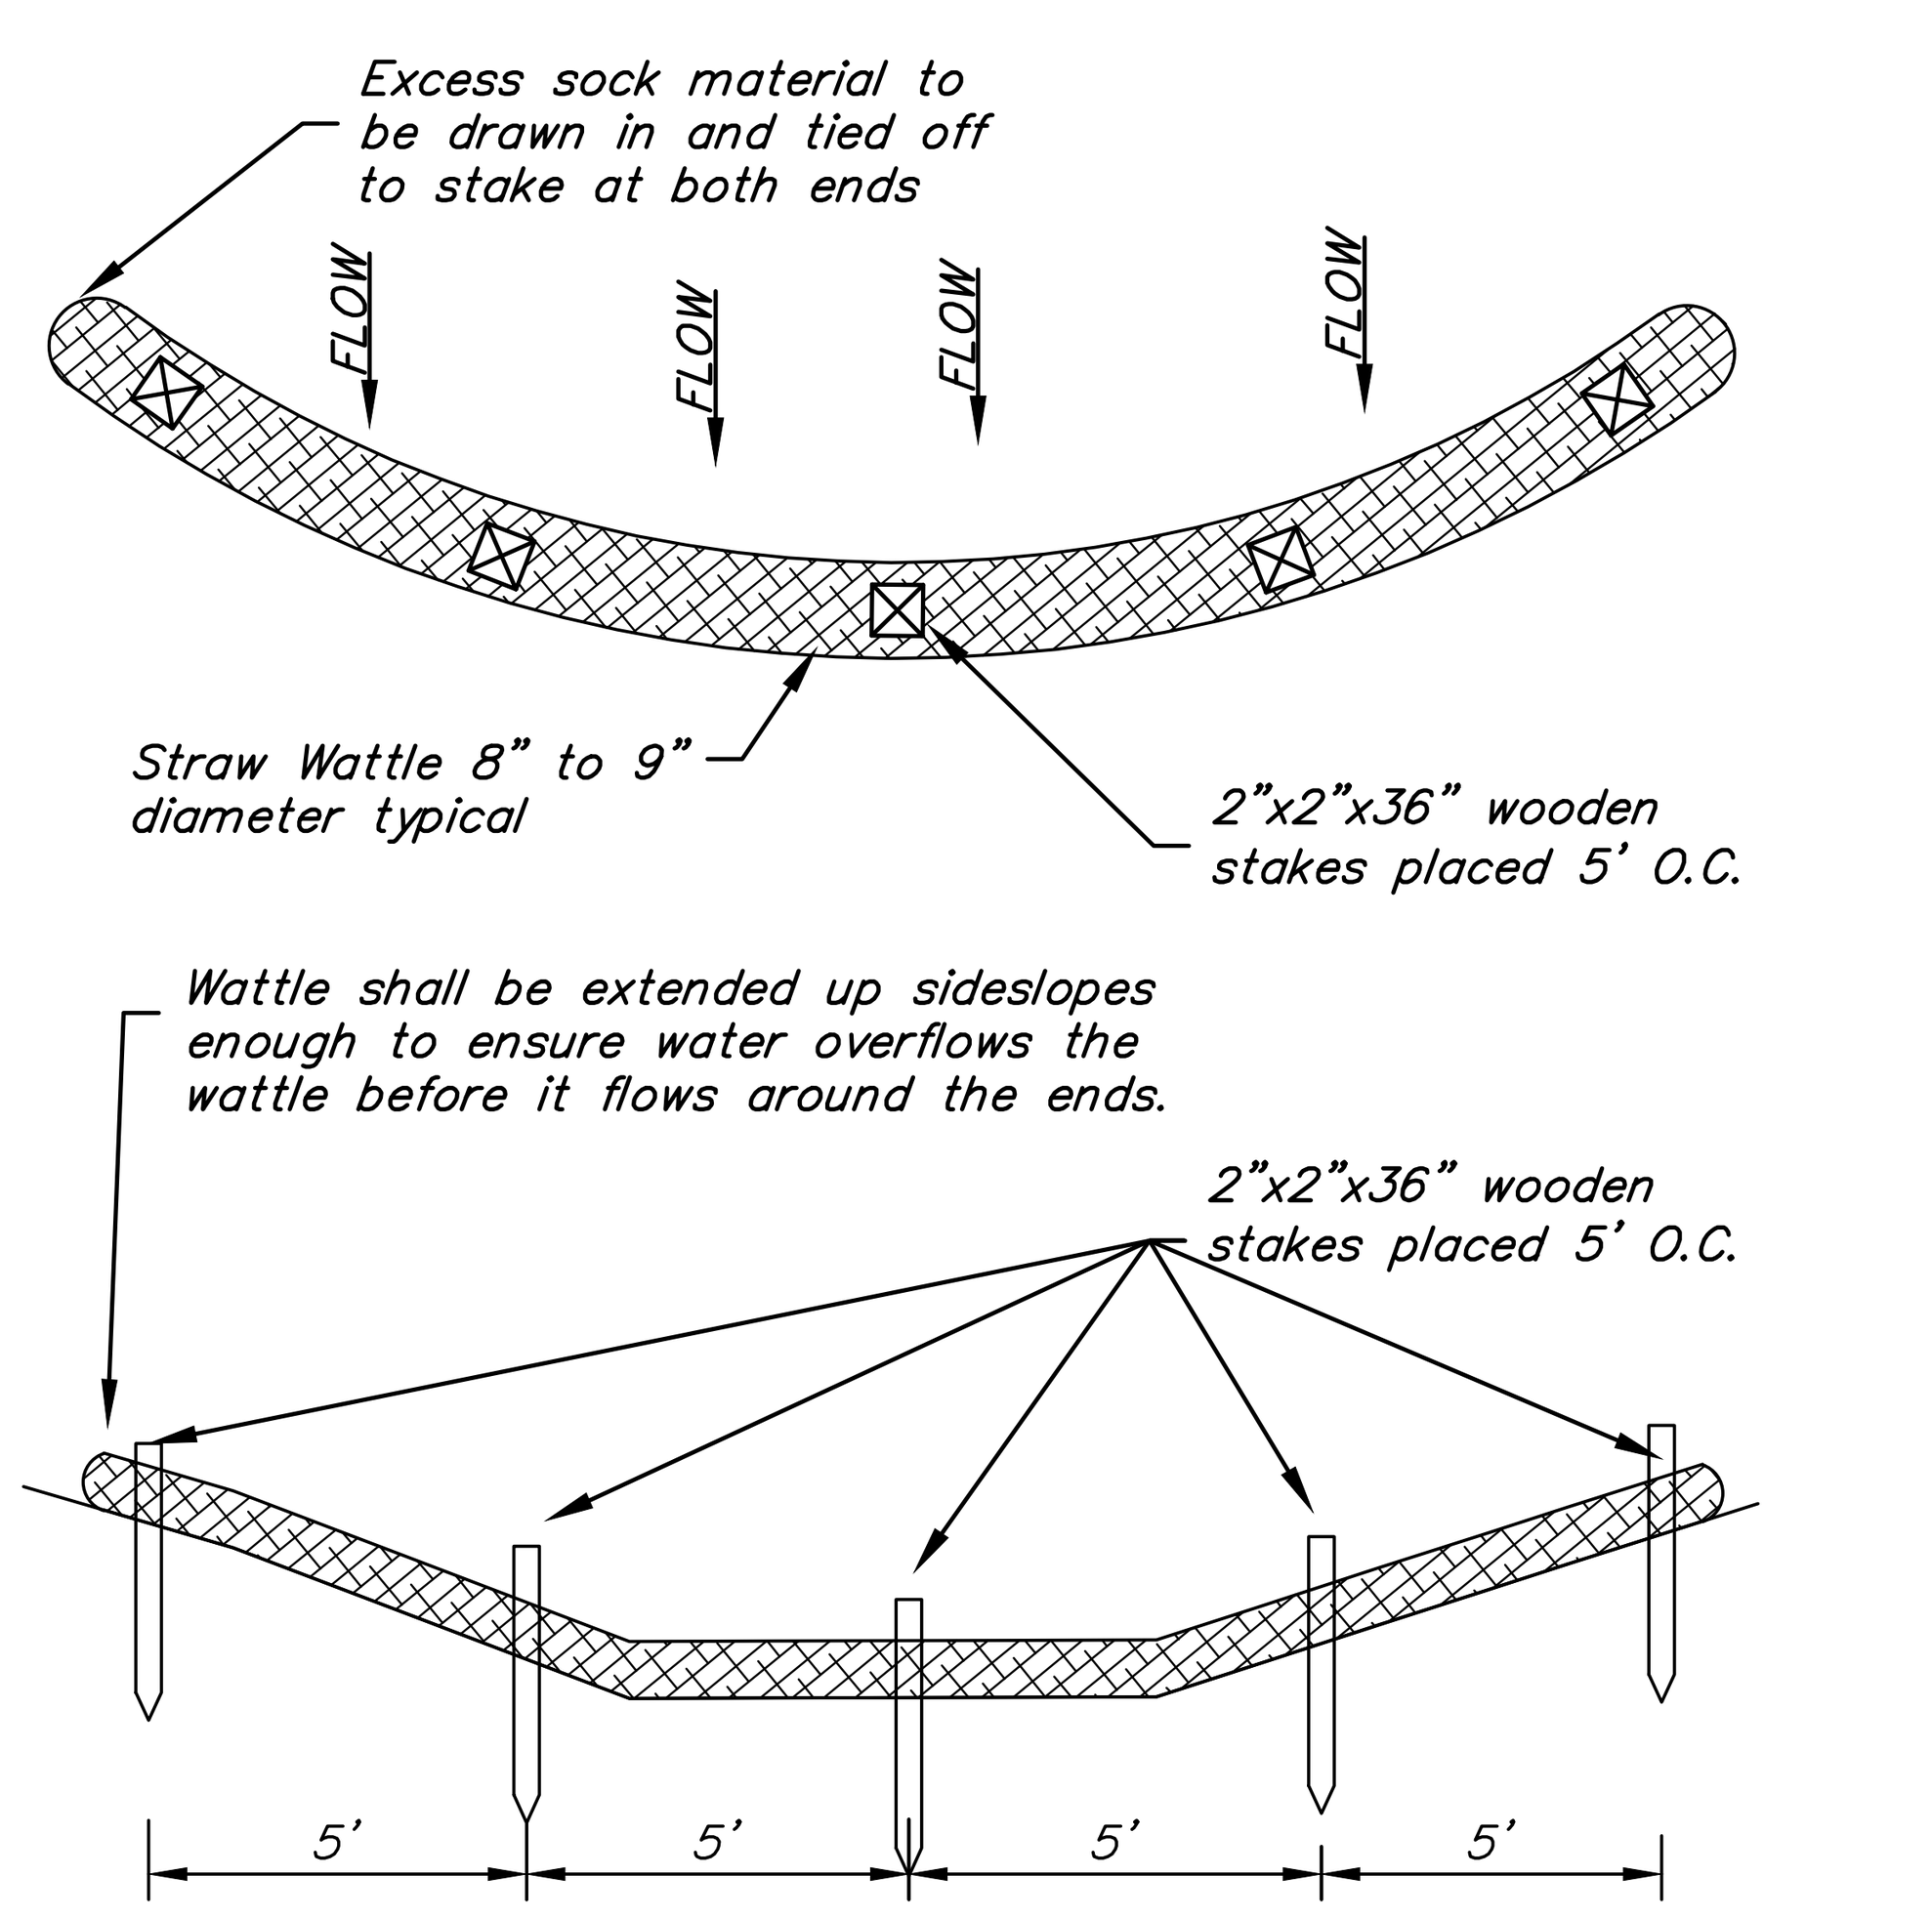

STRAW WATTLE DITCH CHECK DETAIL

NOTES:
1. All material to meet manufacturer specifications.
2. Ditch Check should be used in areas that drain 10 acres or less.
3. Sediment should be removed from behind check dam once the accumulated height has reached ½ height of the check dam.
4. Check dam can be direct seeded at the time of installation.
5. See Sheet X for spacing requirements.

EROSION CONTROL MEASURE	INSTALL	MAINTAIN	REMOVE
BACK OF CURB PROTECTION (LF)	0	0	0
CONSTRUCTION ENTRANCE (EA)	0	1	0
CURB INLET BARRIER (EA)	0	0	0
DITCH CHECK (EA)	0	18	0
DROP INLET PROTECTION (EA)	0	16	0
EROSION CONTROL (LS)	0	0	0
EROSION CONTROL BERM (LF)	0	2,887	0
SILT FENCE (LF)	0	2,537	0
EROSION CONTROL MAT (SY)	0	0	0
STRAW WATTLE DITCH CHECK (LF)	0	220	0

QUANTITIES ARE FOR INFORMATION ONLY! CONTRACTOR SHALL VERIFY QUANTITIES PER FINAL BID QUANTITY SHEET.

* ALL EXISTING BMPs INCLUDING CONSTRUCTION ENTRANCE, SEDIMENT BARRIERS, SILT FENCE, EROSION CONTROL BERM, AND EROSION CONTROL MAT SHALL BE MAINTAINED AND REPAIRED IF NECESSARY. REPLACEMENT OR REMOVAL OF EROSION CONTROL MEASURES TO BE PAID FOR BY L.S. BID ITEM "MAINTAIN EXISTING EROSION CONTROL BMPs"

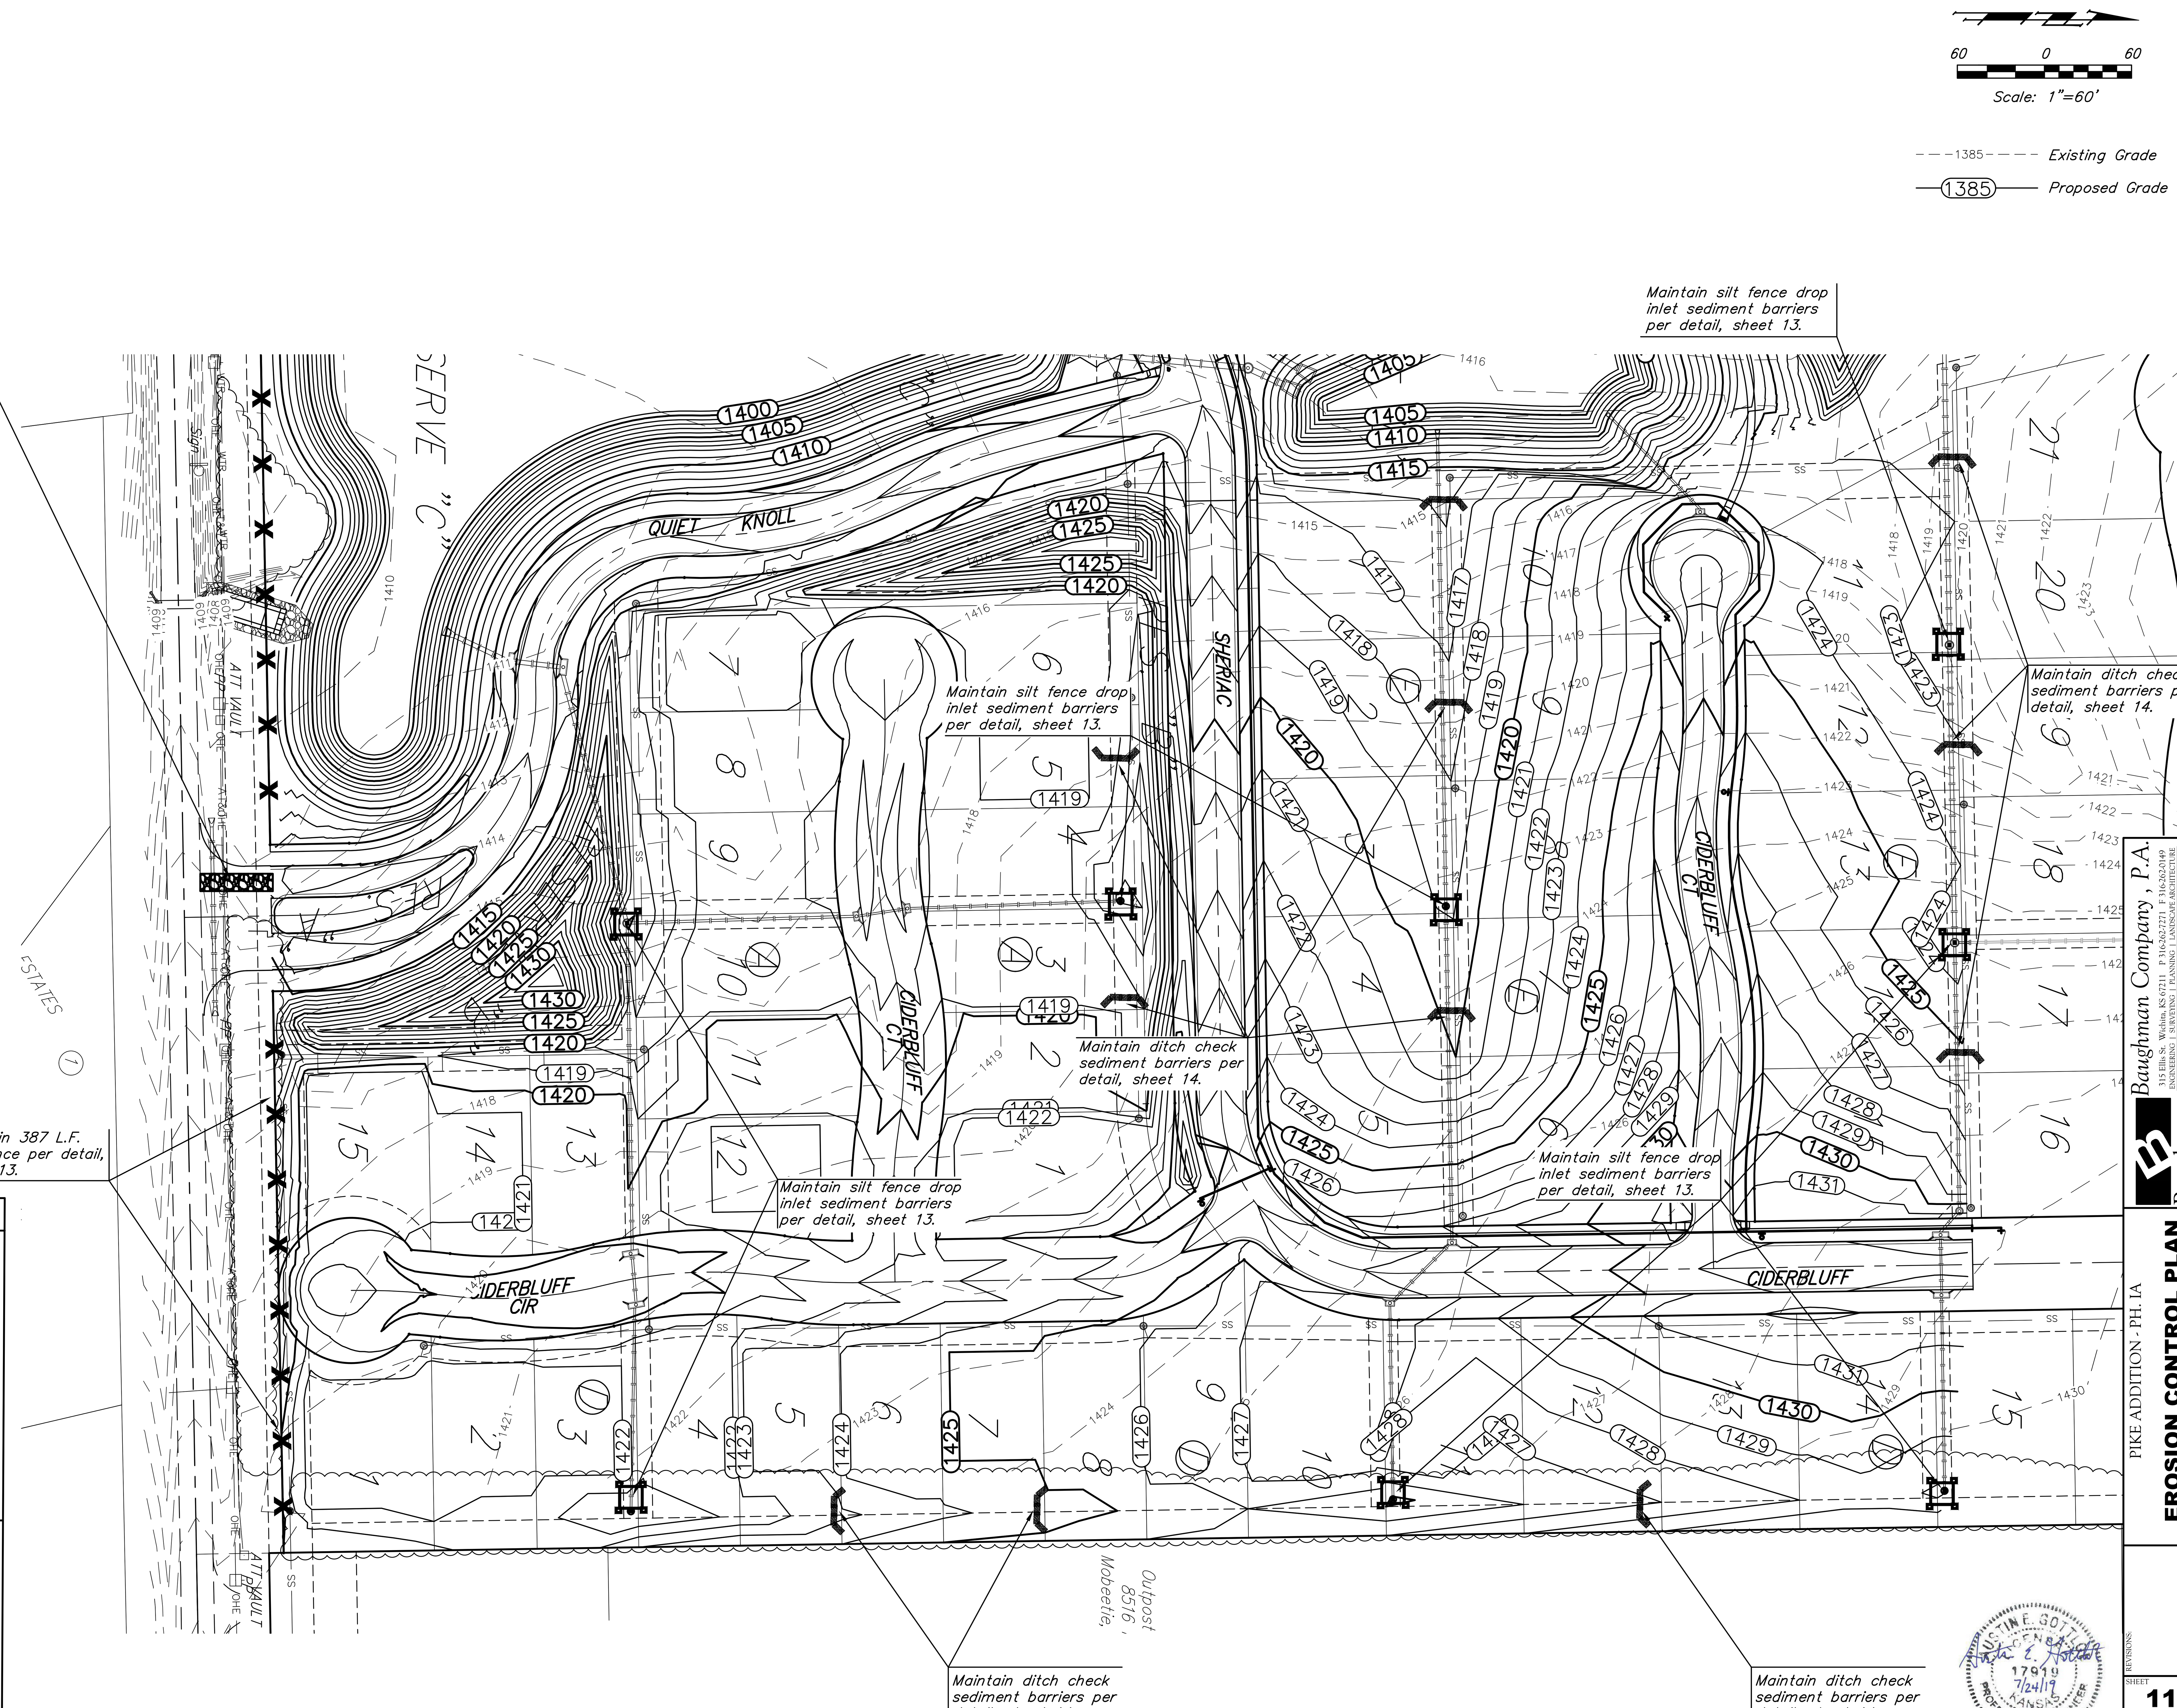

PIKE ADDITION - PH. IA

EROSION CONTROL PLAN
WATER DISTRIBUTION SYSTEM

Baughman Company, P.A.
315 Ellis St. Wichita, KS 67211 P 316-262-7271 F 316-262-0149
ENGINEERING | SURVEYING | PLANNING | LANDSCAPE ARCHITECTURE
Design: AEG Drawn: TMS Approved: Date: 07/19
File: Wtr.dwg

REVISIONS:

SHEET 11 OF 19
