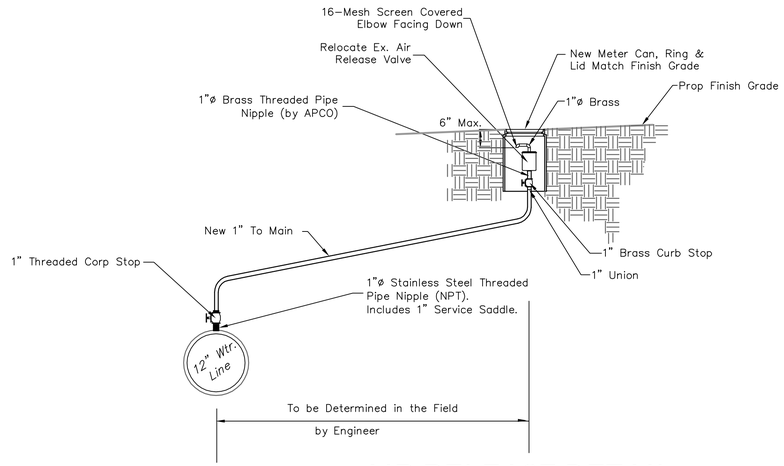

AIR RELEASE DETAIL

VALVE BOX ADJUSTMENT TABLE

Station	Roadway	Offset	Valve #	Notes
107+17.9	Dora	23.6' Lt	5043	2"
107+20.0	Dora	8.1' Lt	5044	6" (Not Found)
200+10.3	Dora	14.9' Lt	5041	6" (Hydrant)
200+18.6	Dora	3.9' Lt	6251	8"
200+19.0	Dora	20.0' Lt	3569	8"
200+22.0	Dora	7.1' Lt	3571	6"
203+71.7	Dora	1.4' Lt	3575	6"
204+00.0	Dora	8.0–25.0'±Lt	3576	6" (Not Found)
204+04.9	Dora	21.2' Lt	10139	6" (Hydrant)
300+18.1	Dora	22.3' Lt	3562	6"
600+22.2	Dora	28.1' Lt	3776	6"
300+51.9	Dora	22.4' Lt	3573	6"
300+59.2	Dora	20.4' Lt	2286	6"
300+63.9	Dora	19.6' Lt	5525	6" (Hydrant)
303+96.0	Dora	24.1' Lt	2283	2"
303+96.2	Dora	18.1' Lt	2287	2"
307+80.1	Dora	27.0' Lt	3778	2"
308+18.3	Dora	18.6' Lt	3579	2"
308+22.8	Dora	20.8' Lt	102	6" (Hydrant)
311+46.9	Dora	20.8' Rt.	5051	2"
311+54.8	Dora	23.8' Lt	2285	2"
315+24.1	Dora	15.9' Lt	4314	6"
315+28.5	Dora	24.6' Lt	2281	6"
315+29.3	Dora	15.9' Lt	4149	2"
406+17.1	Exposition	19.7' Rt	4315	2"
501+00.7	May	29.2' Lt	14325	6"
501+05.4	May	29.0' Lt	14326	2"
503+30.5	May	21.3' Lt	33130	8" (Hydrant)
503+34.2	May	22.8' Lt	4317	8"

METER BOX ADJUSTMENT TABLE

Address	Paving Station	Offset
1846 S. Sedgwick	5+99	20.6' Rt.
1902 S. Sedgwick	3+70	45.8' Rt.
1908 S. Sedgwick	10+97	24.4' Lt.
1913 S. Sedgwick	11+04	19.3' Rt.
2342 W. Dora	4+80	20.3' Rt.

The Contractor Shall be Required to Install New Meter Box and Ring & Cover.

METER SET ADJUSTMENT TABLE

Address	Paving Station	Offset
1850 S. Sedgwick	5+63	21.2' Rt.
1854 S. Sedgwick	5+01	19.9' Rt.

The Contractor Shall be Required to Install New Meter Box and Ring & Cover.

WATER SERVICE REPLACEMENT TABLE

Address	RCB Station	Meter Offset	Service	Remarks
1842 S. Sedgwick	--	Rt	Short	Relocate 5' East
1419 W. Dora	42+33	Rt	Long	Remove & Replace
1901 S. Fern	35+52	Rt	Long	Remove & Replace
1329 W. Dora	45+13	Rt	Short	Remove & Replace
1317 W. Dora	46+25	Rt	Short	Remove & Replace
1920 S. Exposition	50+13	Lt	Long	Tap Split w/ 1922
1922 S. Exposition	50+13	Lt	Long	Remove & Replace
1921 S. Exposition	50+16	Rt	Short	Remove & Replace
1923 S. Exposition	50+16	Rt	Short	Tap Split w/ 1921
1927 S. Exposition	50+64	Rt	Short	Remove & Replace
1928 S. Exposition	50+73	Lt	Long	Remove & Replace
1935 S. Exposition	51+25	Rt	Short	Remove & Replace
1934 S. Exposition	51+27	Lt	Long	Remove & Replace
1940 S. Exposition	51+73	Lt	Long	Remove & Replace
1941 S. Exposition	51+76	Rt	Short	Remove & Replace
1946 S. Exposition	52+23	Lt	Long	Remove & Replace
1947 S. Exposition	52+26	Rt	Short	Remove & Replace
1952 S. Exposition	52+73	Lt	Long	Remove & Replace
1953 S. Exposition	52+76	Rt	Short	Remove & Replace
1310 W. May	53+12	Lt	Long	Remove & Replace
1314 W. May	53+14	Rt	Short	Remove & Replace
1316 W. May	53+14	Rt	Short	Tap Split w/ 1314

New Meter Boxes to be at the Same Location as the Existing Boxes Unless Directed Otherwise.

Taps that are Currently Split in Existing Meter Boxes Shall be Separated into a Meter Box for Each Address.
