




FEMA REGION NO.	STATE	PROJECT NO.	FISCAL YEAR	SHEET NO.	TOTAL SHEETS
7	KANSAS	87N-0303-01	2003	101	143

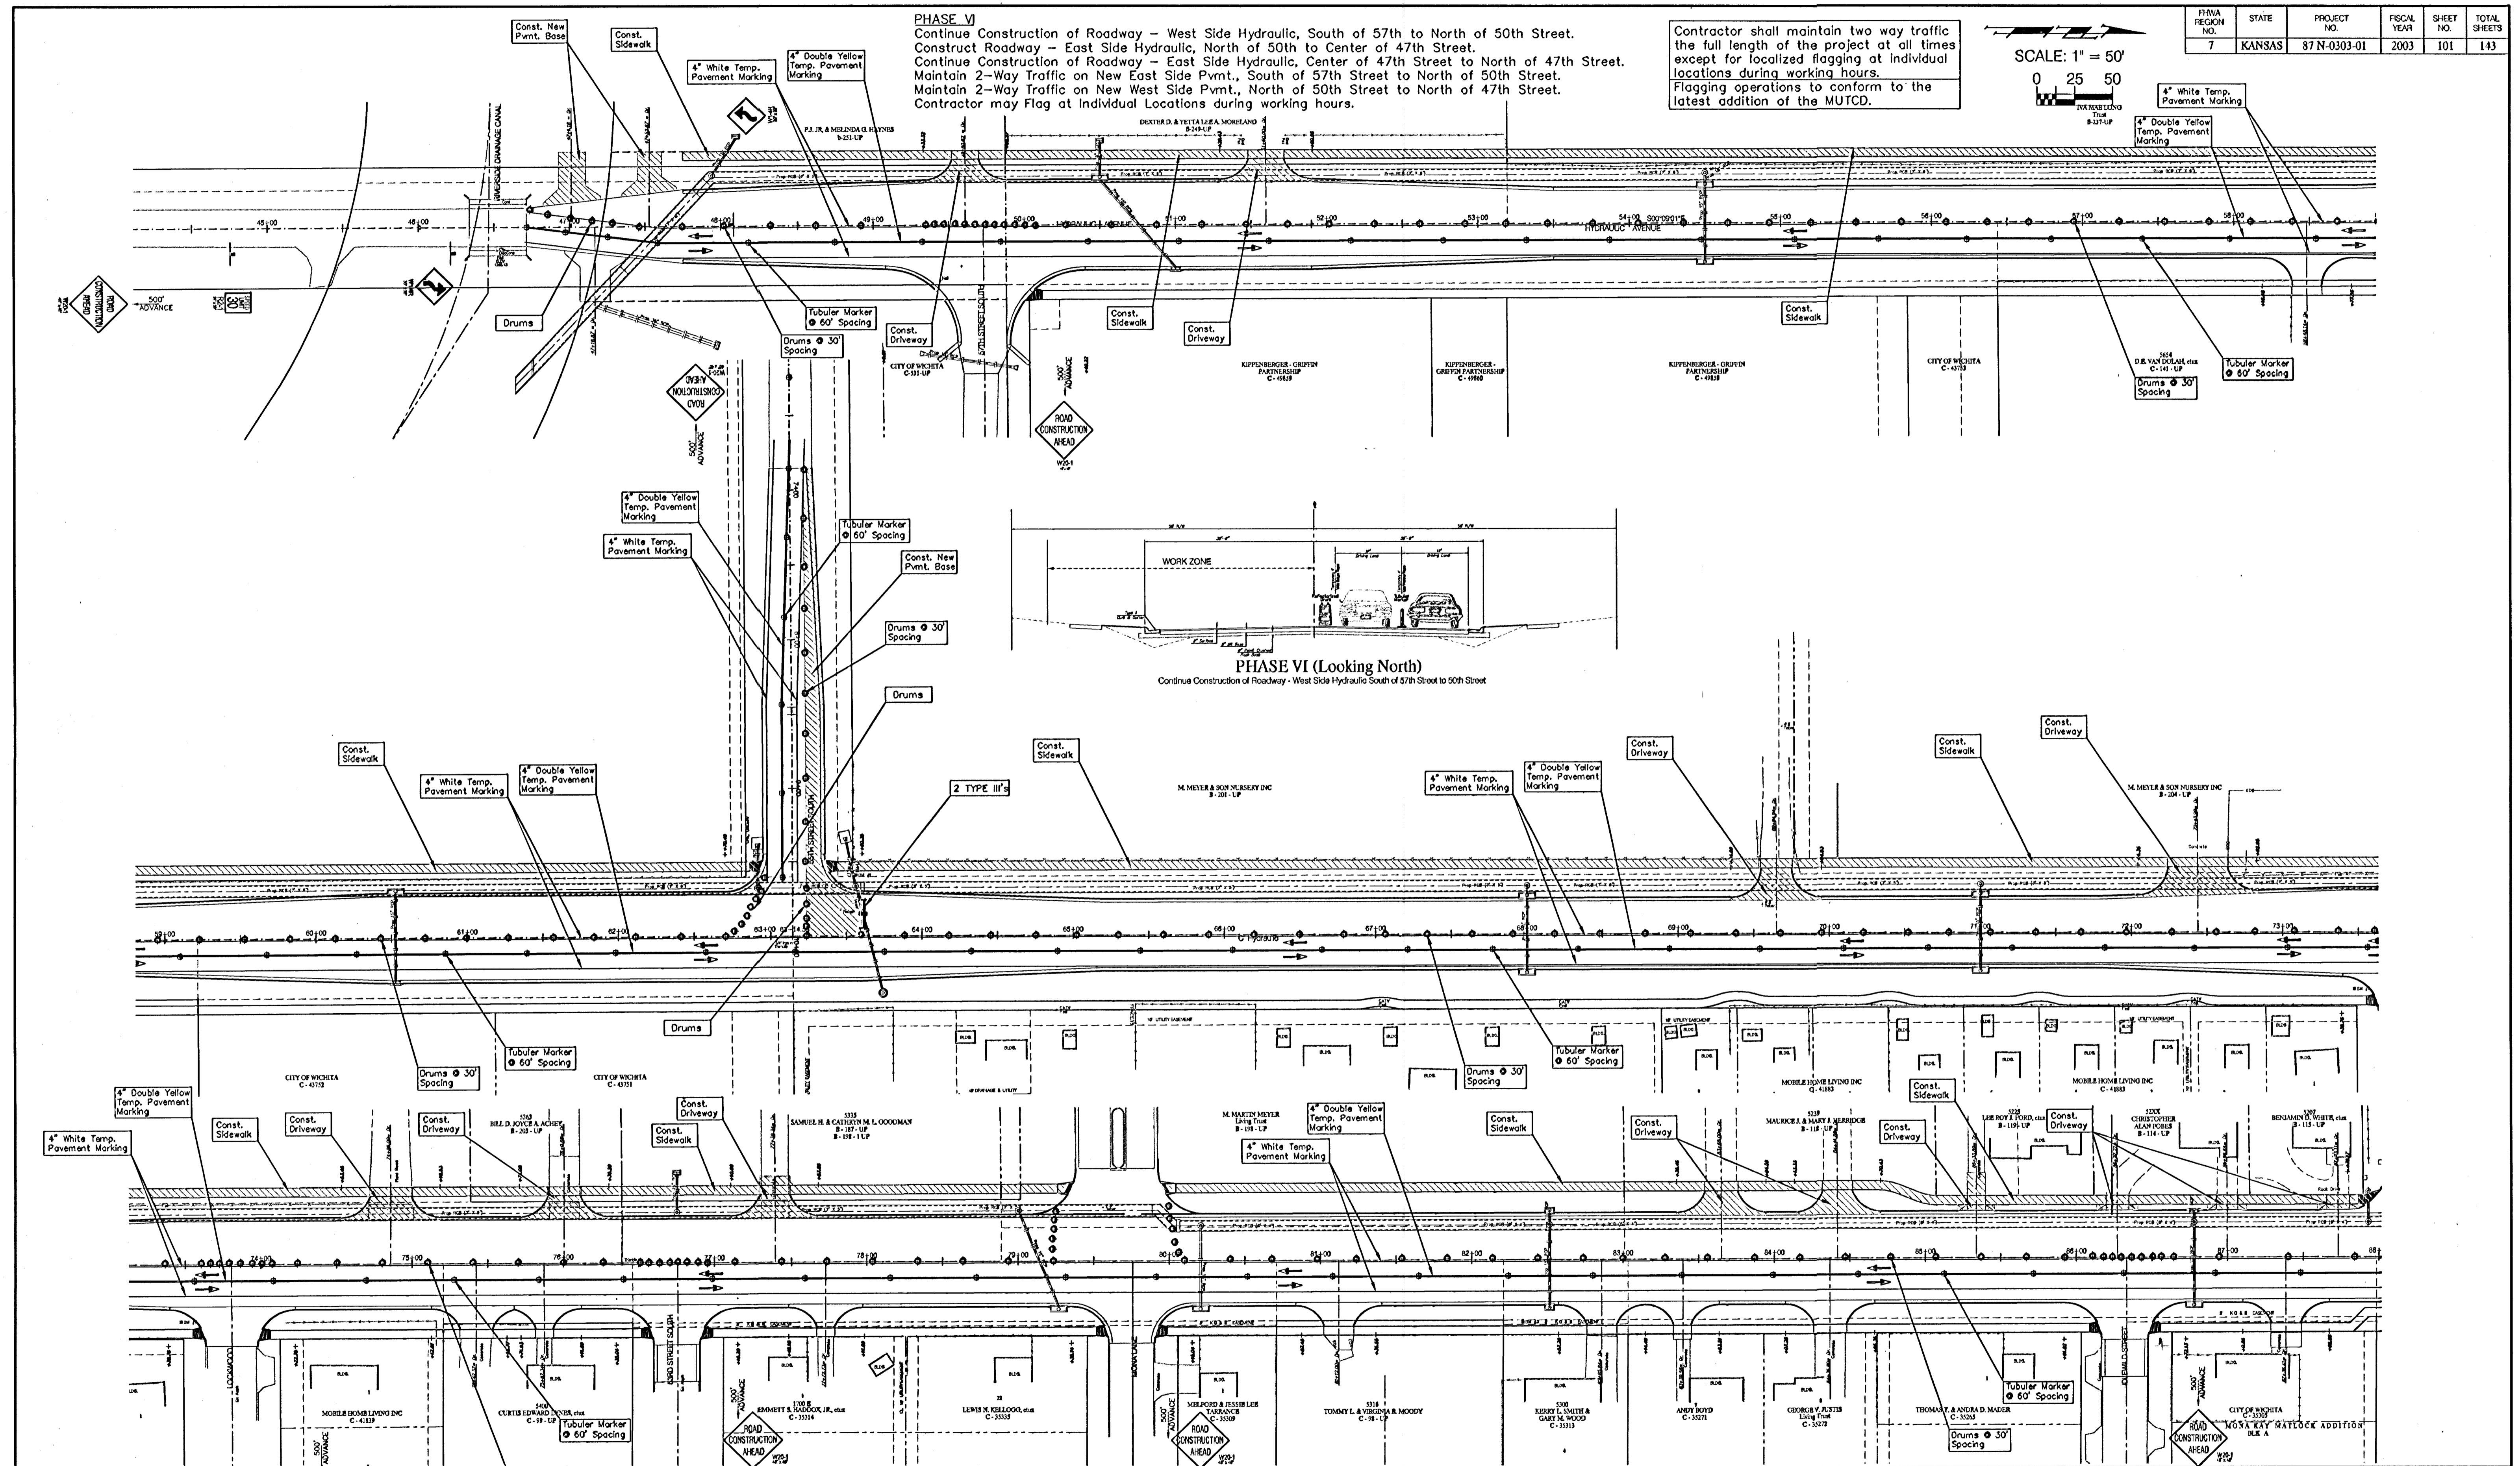

PHASE VI
 Continue Construction of Roadway - West Side Hydraulic, South of 57th to North of 50th Street.
 Construct Roadway - East Side Hydraulic, North of 50th to Center of 47th Street.
 Continue Construction of Roadway - East Side Hydraulic, Center of 47th Street to North of 47th Street.
 Maintain 2-Way Traffic on New East Side Pmt., South of 57th Street to North of 50th Street.
 Maintain 2-Way Traffic on New West Side Pmt., North of 50th Street to North of 47th Street.
 Contractor may Flag at Individual Locations during working hours.

Contractor shall maintain two way traffic the full length of the project at all times except for localized flagging at individual locations during working hours. Flagging operations to conform to the latest addition of the MUTCD.

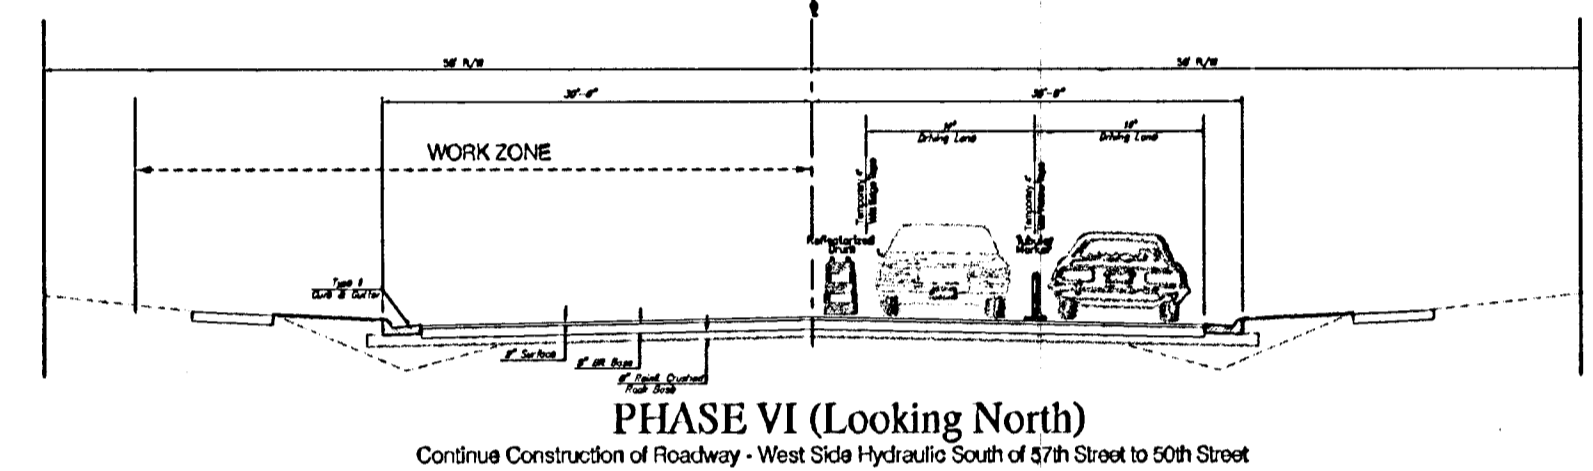

Contractor shall maintain access to all businesses and residences during construction.

Contractor shall maintain all drainage ways during construction.

PROJECT NUMBER 472 83902	SHEET NAME Conseq13	ENGINEERING DIRECTORY P:\Eng\Hydraulic\phs2\Conseq
DESIGN Azire	DRAWN Staff	APPROVED JFB
DATE March 04	SCALE 1"=50'	BAUGHMAN NO 99-09-E431

STREET & SWS IMPROVEMENTS
Construction Sequencing Plan Phs VI
 HYDRAULIC AVE PAVING - SOUTH OF 57TH STREET SOUTH TO 47TH STREET SOUTH

BAUGHMAN COMPANY, P.A.
 ENGINEERING, SURVEYING, & PLANNING
 318-202-7271 • 315 ELLIS • WICHITA, KANSAS 67211

SHEET 101 of 143
