


FHWA REGION NO.	STATE	PROJECT NUMBER	FISCAL YEAR	SHEET NUMBER	TOTAL SHEETS
7	KANSAS	87 N-0195-01	2001	75	127

BY	DATE
REFERENCES NOTED	
REFERENCES CHECKED	

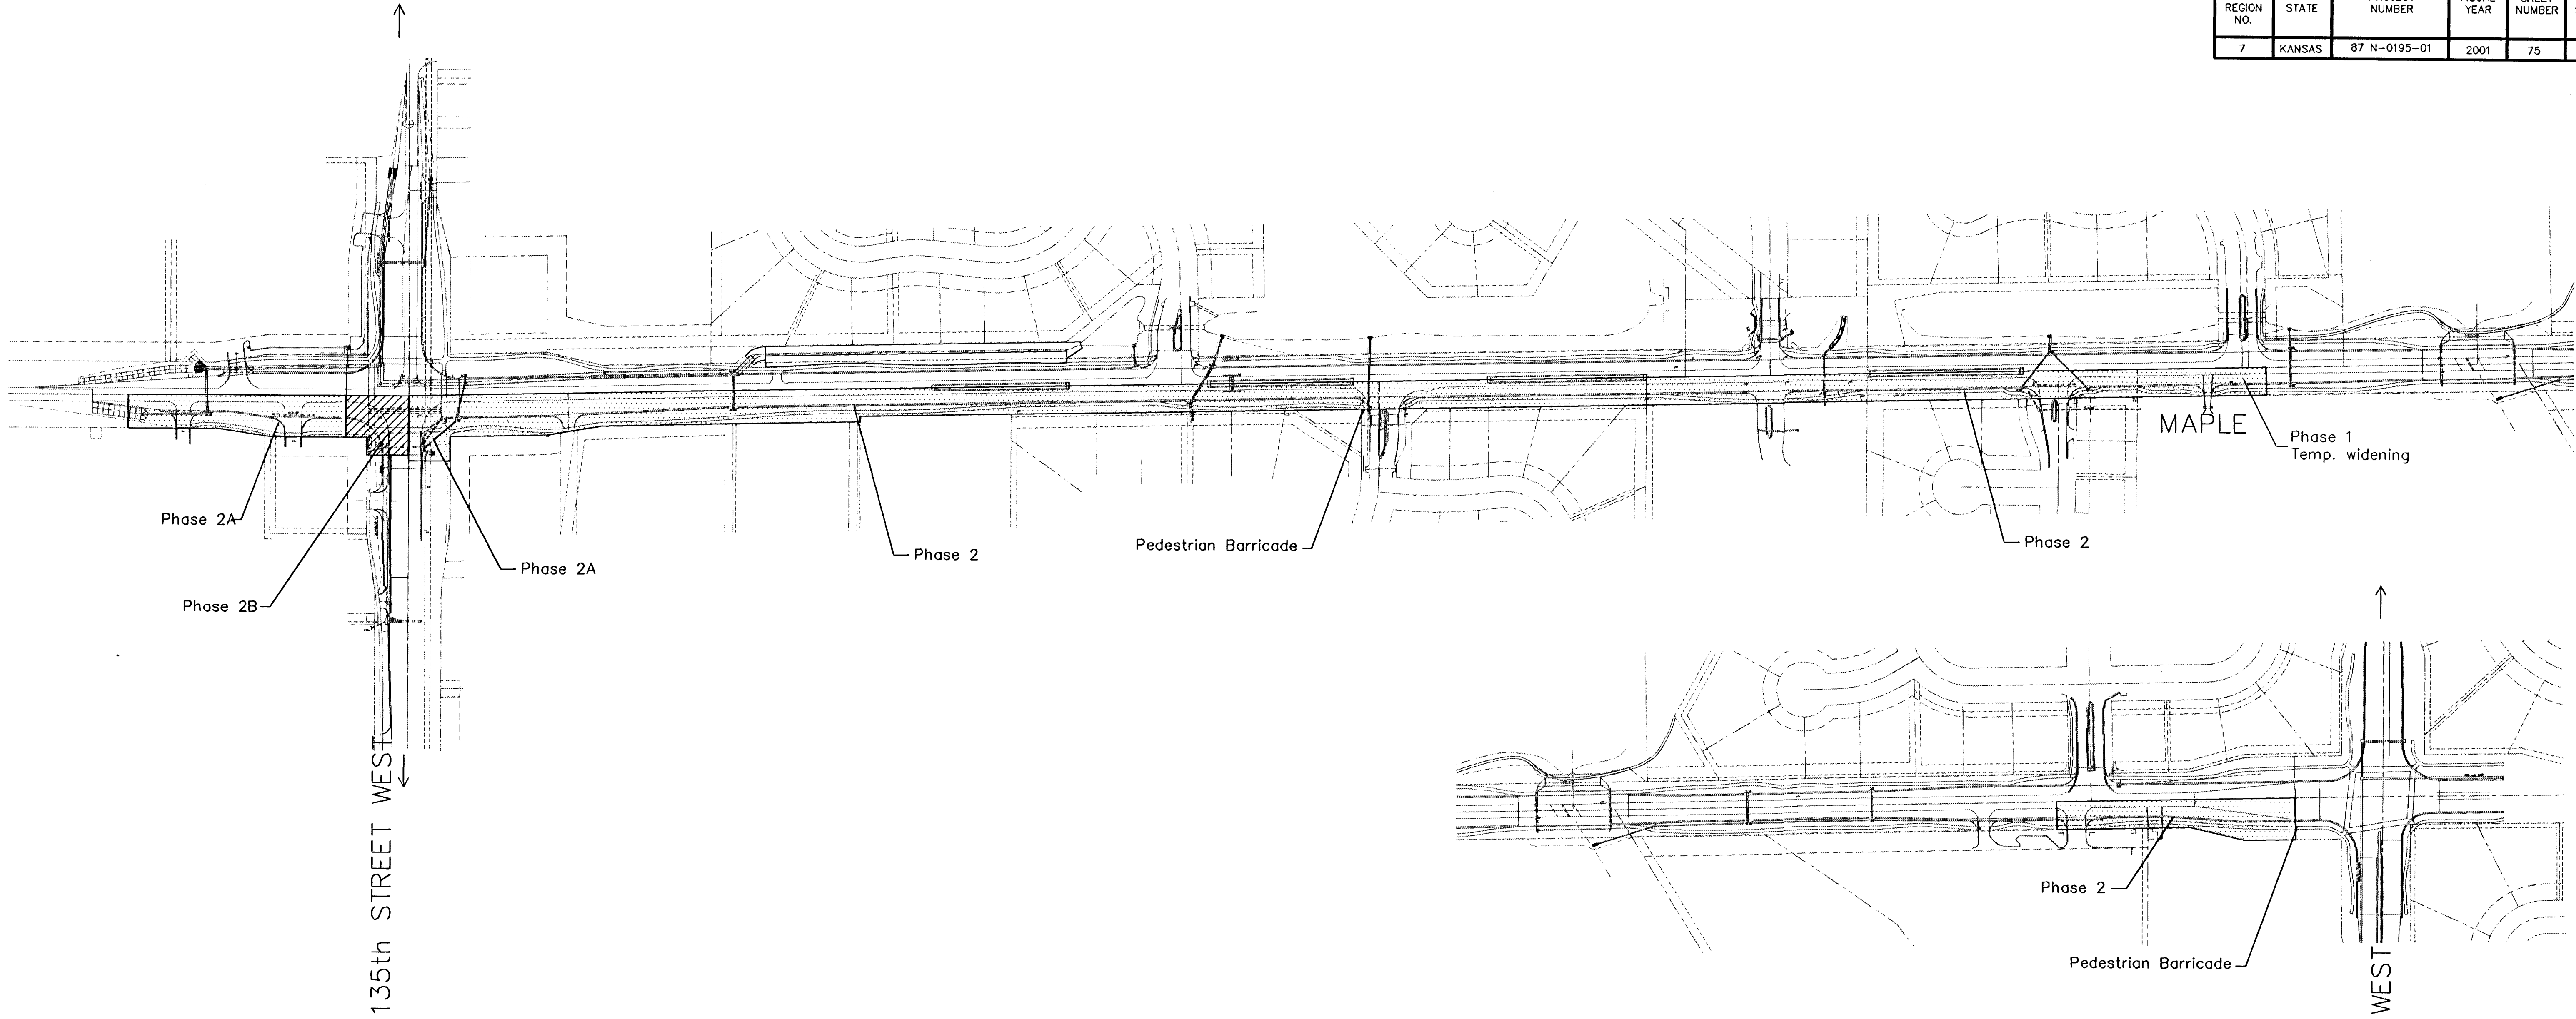

Phase	Handling of Traffic	Major Construction Items	Remarks
2	Move two-way traffic to the north half of Maple. (All vehicle traffic will now be on new pavement.)	Remove temporary pavement.	Paving operations shall be phased at entrances to allow continuous access.
2A	Keep two-way traffic on the east half of 135th St. Pedestrian traffic to be closed during construction of intersection and walk at Sta. 8+937 (Limuel), Sta. 9+330 (Firefly), and Sta. 9+952 (119th).	Construct storm sewer south of centerline of Maple. Construct SE quadrant of 135th and Maple intersection. (Phase 2A)	Traffic movements will be maintained during construction with grade differences being adjusted temporarily with the use of asphalt ramps.
2B	Move two-way traffic to the west half of 135th St.	Construct SW quadrant of 135th and Maple intersection. (Phase 2B)	

General Notes

All signs and pavement markings conflicting with this traffic control shall be covered or removed as directed by the engineer.

As the various construction activities progress, certain situations may arise which will preclude adhering to the original construction sequences or which in the opinion of the contractor, would readily adapt themselves to a more efficient phasing operation. Should this occur, the contractor may submit to the engineer an alternate plan for approval.

Two way traffic will be maintained on Maple and 135th Street with the exception of road closure between Breezy Pointe Circle and Cedar Park to allow for the construction of the bridge.

Contractor shall maintain existing drainage system nearly as possible during construction, or supplement the existing system with ditches and temporary pipes. Temporary pipes shall be removed or filled per City Standards before final construction.

No Scale

MAPLE IMPROVEMENTS - 135TH ST. W. TO 119TH ST. W.
CONSTRUCTION STAGING AND SEQUENCING
PHASE 2

SRB

924 NORTH MAIN
WICHITA, KANSAS 67203
www.srb1.com

316-254-8008
FAX 316-4621
E-Mail: srb@srb1.com

SAVOY, RUGGLES & BOHM, P.A.
ENGINEERING & SURVEYING

PROJECT NUMBER
472-76-245-83262-000-000-001

75

127
